CyberSeat | Project management evidence

First submission - analysis, design and planning | Team 3

Scope. A live review of all 24 YouTrack cards, with authentic board/list screenshots and detailed examples from all three participants. Screenshots are reproduced as captured; long views continue over consecutive pages with a small overlap.

Snapshot. 17 tasks Done, 2 in progress (ECR-17 release/access checks and ECR-19 this evidence PDF), and 5 queued. Of the queued tasks, ECR-20 is submission; ECR-12 and ECR-21 through ECR-23 are explicitly later implementation work.

Deadline. The October package is due before 18:00 on 24 October 2026, Astana time (UTC+5). Earlier dates in individual descriptions are internal planning targets. They are not additional university deadlines. Later implementation has a June 2027 planning horizon, not a fixed defence date.

Evidence boundary. This PDF records the state during preparation, before its own publication, final tagging and form submission. Their later completion must be evidenced in the live task comments. No submission receipt, completed application or executed final application tests is claimed.

Sources. YouTrack project | Team board | GitHub repository

Final report. The 122-page report includes all eleven sections and the supervisor reply. SHA-256: 90a21ccc617f828476907d384d6d92ebf268649780a53fa3fb1cff31a37e0837. The form requires the tag prob-period-1; the earlier task name pre-defense-1 is retained as an alias at the same final commit.

Mansur Urynbassar

Responsibilities and live task inventory

Visitor/admin UX, user research, scenarios and submission coordination.

Task / stage	Deliverable	Priority	Status	Deadline
ECR-1 October	[October 24] Define Visitor and Administrator Scenarios	Major	Done	24 Oct 2026 before 18:00
ECR-3 October	[October 24] Collect Evidence of Relevance and User Needs	Major	Done	24 Oct 2026 before 18:00
ECR-5 October	[October 24] Compare Existing Booking Systems	Major	Done	24 Oct 2026 before 18:00
ECR-9 October	[October 24] Prepare the Key-Scenario UX Prototype	Major	Done	24 Oct 2026 before 18:00
ECR-11 October	[October 24] Prepare the Use Case Diagram	Major	Done	24 Oct 2026 before 18:00
ECR-19 October	[24 октября] Объединить скриншоты YouTrack в один PDF	Major	In progress	24 Oct 2026 before 18:00
ECR-20 October	[24 октября] Загрузить материалы комиссии и проверить отправку до 18:00	Critical	Queue	24 Oct 2026 before 18:00
ECR-21 Later	[После 24 октября] Реализовать интерфейсы и интеграцию с API	Normal	Queue	Later stage

Aibekyly Alibi

Responsibilities and live task inventory

Proposal, literature/technology research, booking requirements, architecture and repository structure.

Task / stage	Deliverable	Priority	Status	Deadline
ECR-2 October	[October 24] Prepare the CyberSeat Project Proposal and Scope	Major	Done	24 Oct 2026 before 18:00
ECR-4 October	[October 24] Prepare the Critical Literature Review	Major	Done	24 Oct 2026 before 18:00
ECR-6 October	[October 24] Justify the Key Technology Choices	Major	Done	24 Oct 2026 before 18:00
ECR-7 October	[October 24] Specify Booking and Non-functional Requirements	Major	Done	24 Oct 2026 before 18:00
ECR-10 October	[October 24] Prepare the System Context and Draft Component Diagram	Major	Done	24 Oct 2026 before 18:00
ECR-12 Later	[After October 24] Design the Shared Database	Normal	Queue	Later stage
ECR-14 October	[October 24] Verify and Extend the README and GitHub Repository Structure	Major	Done	24 Oct 2026 before 18:00
ECR-17 October	[October 24] Verify Git History, Committee Access and the Submission Version	Major	In progress	24 Oct 2026 before 18:00
ECR-22 Later	[After October 24] Implement the Database and Reliable Booking API	Normal	Queue	Later stage

Akhmetov Nurali


Responsibilities and live task inventory

Administrative requirements, evaluation/management plans, supervisor feedback and consolidated report.

Task / stage	Deliverable	Priority	Status	Deadline
ECR-8 October	[October 24] Define Administrative Requirements and the Access-Control Matrix	Major	Done	24 Oct 2026 before 18:00
ECR-13 October	[October 24] Prepare the Verification and Evaluation Plan	Major	Done	24 Oct 2026 before 18:00
ECR-15 October	[October 24] Document Project Stages, Risks, and Dependencies	Major	Done	24 Oct 2026 before 18:00
ECR-16 October	[October 24] Obtain Supervisor Feedback and Address Comments	Major	Done	24 Oct 2026 before 18:00
ECR-18 October	[October 24] Verify the Submission Package Against the 11 Committee Requirements	Major	Done	24 Oct 2026 before 18:00
ECR-23 Later	[After October 24] Implement the Administrative Module and Reporting	Normal	Queue	Later stage
ECR-24 October	[October 24] Compile and Verify the Consolidated PDF Report	Critical	Done	24 Oct 2026 before 18:00

Team board overview

Original YouTrack screenshot | Part 1/4 | https://nerybr.youtrack.cloud/agiles/204-1/current

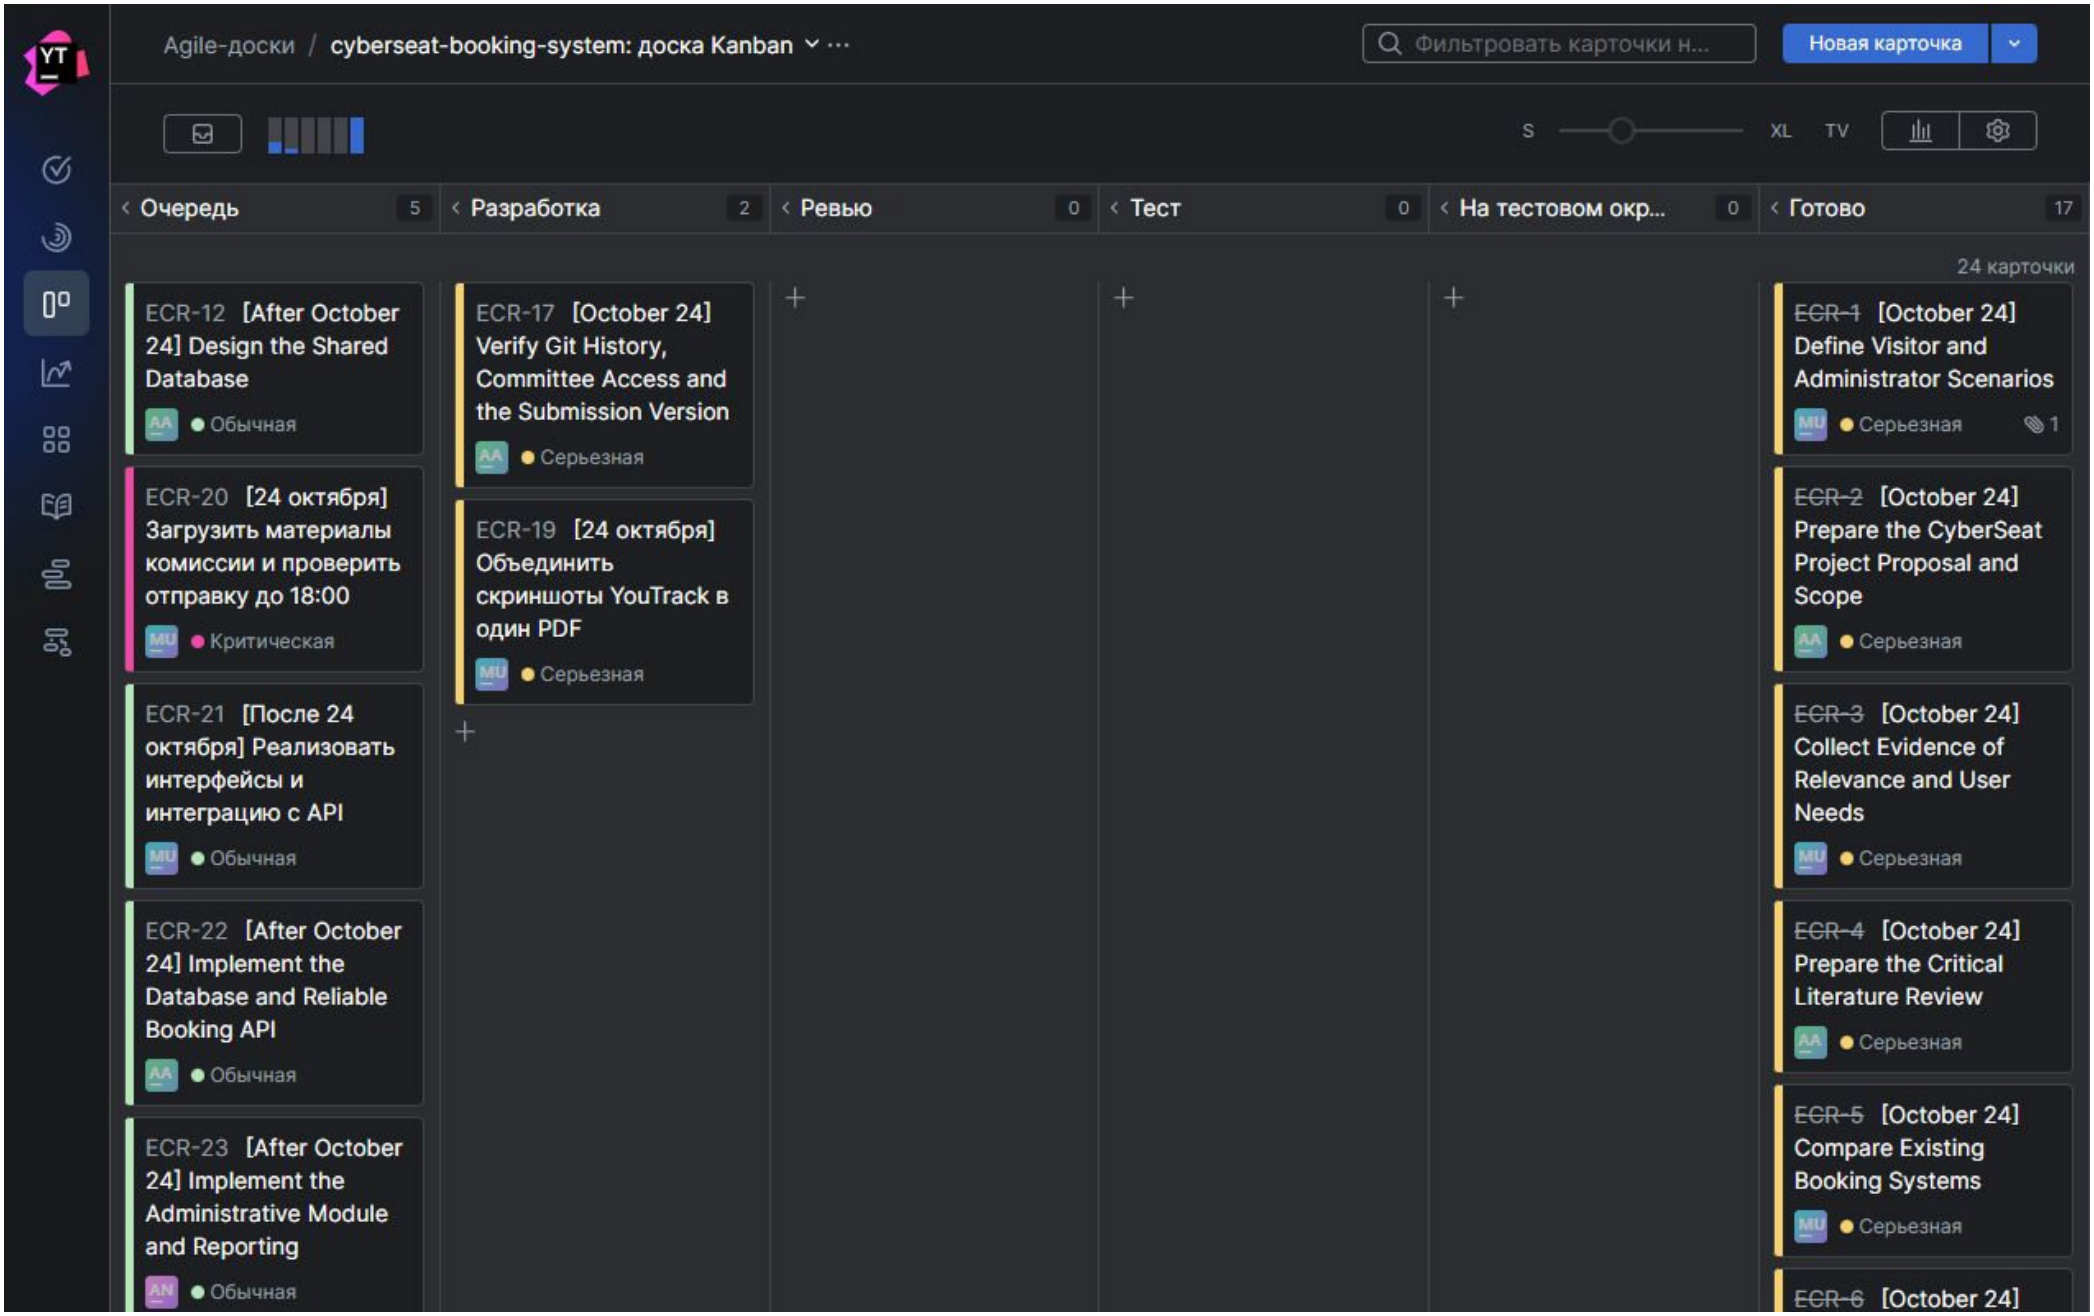

Team board overview

Original YouTrack screenshot | Part 2/4 | https://nerybr.youtrack.cloud/agiles/204-1/current



Team board overview

Original YouTrack screenshot | Part 3/4 | https://nerybr.youtrack.cloud/agiles/204-1/current




Team board overview

Original YouTrack screenshot | Part 4/4 | https://nerybr.youtrack.cloud/agiles/204-1/current



All 24 tasks - owners, priorities and statuses


Original YouTrack screenshot | Part 1/2 | https://nerybr.youtrack.cloud/issues/ECR

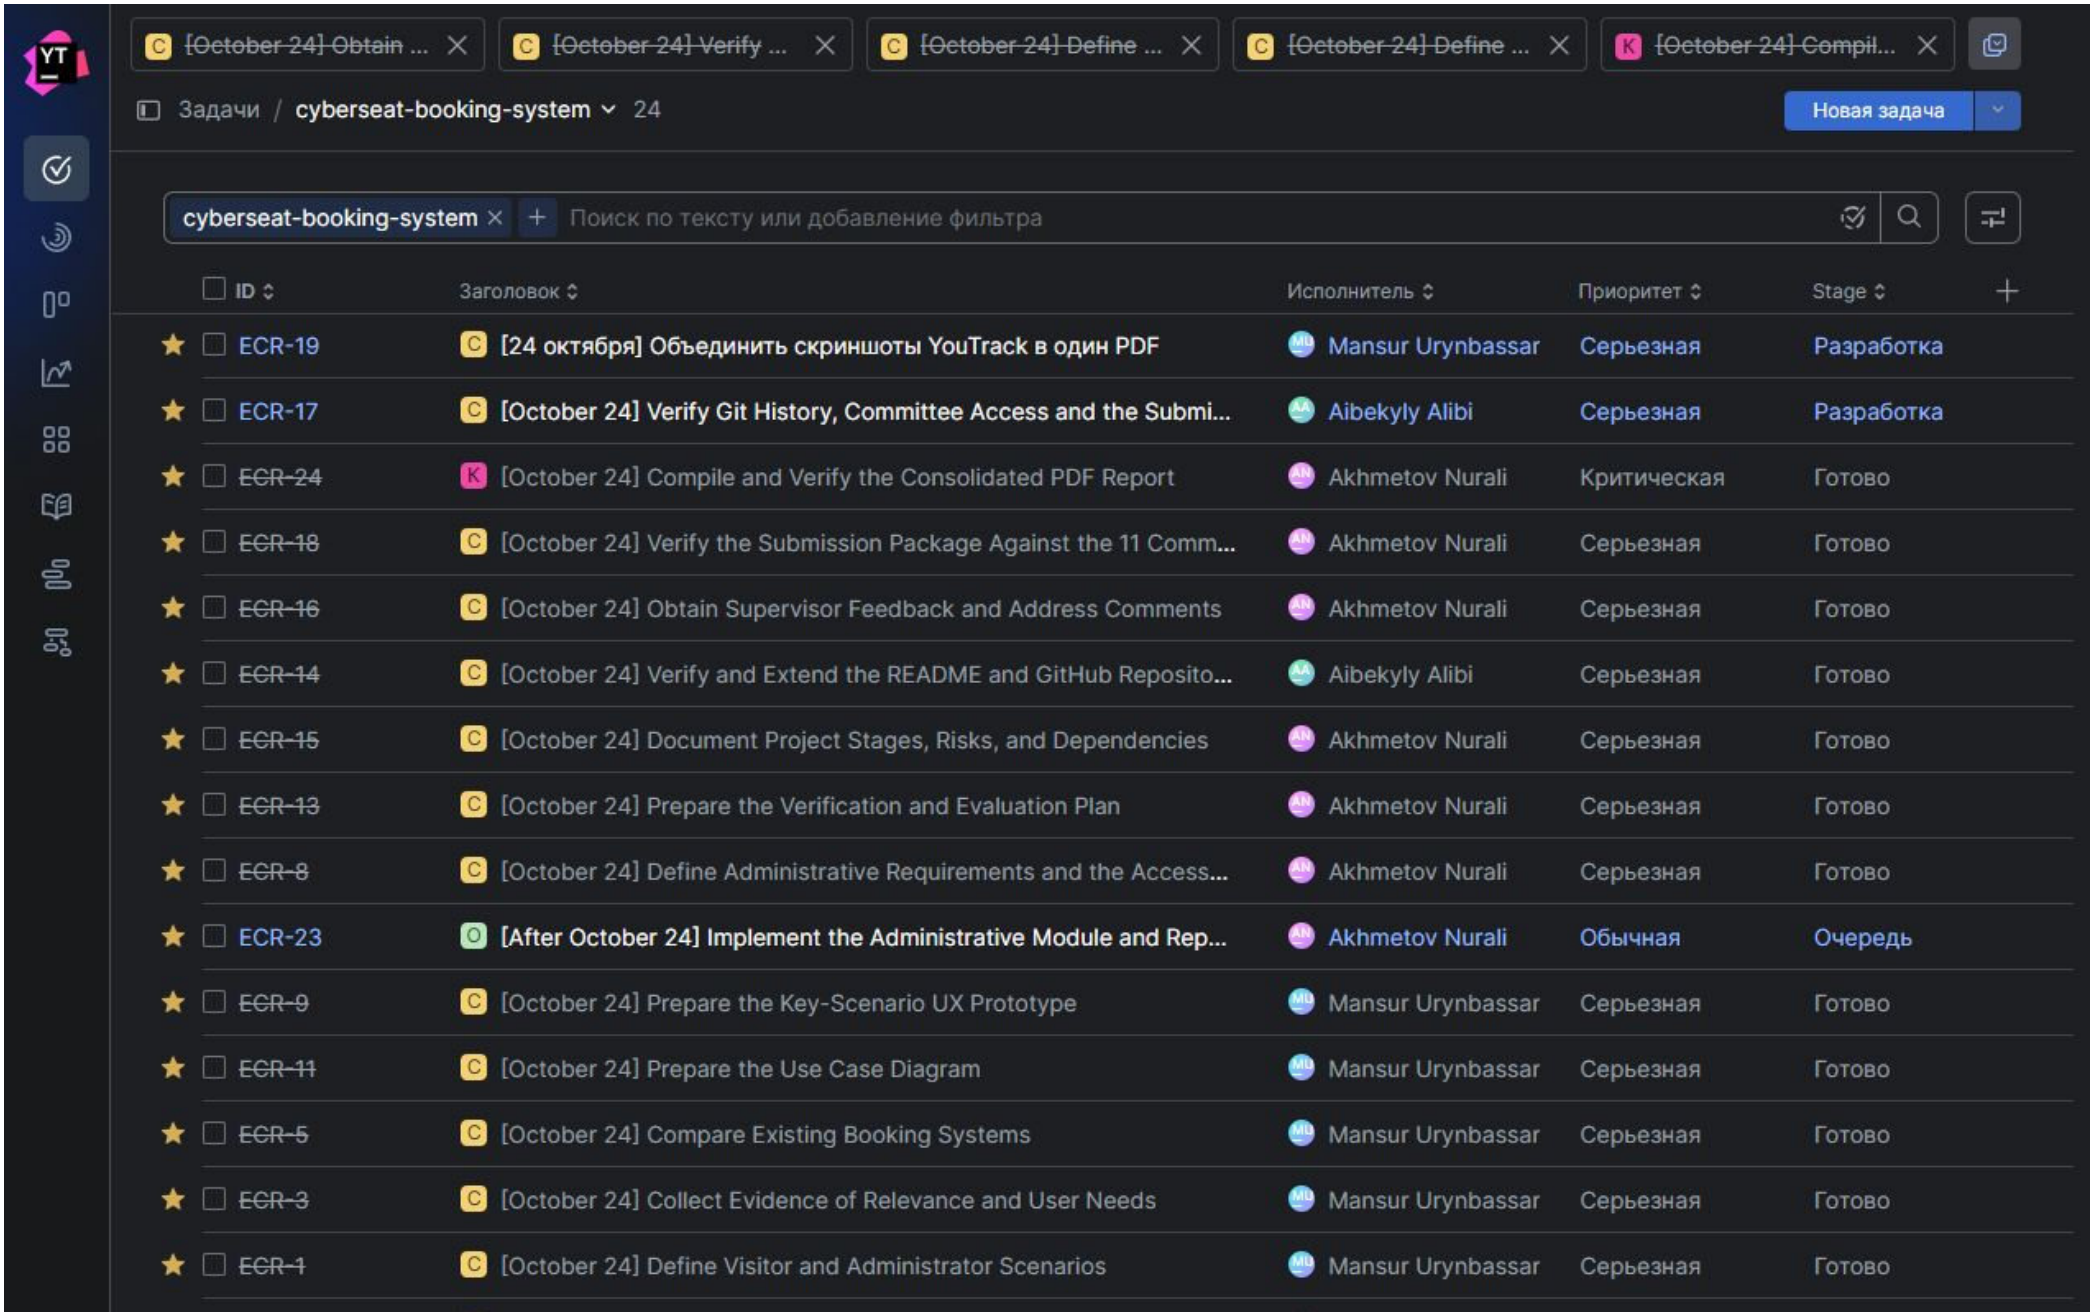

ID	Заголовок	Исполнитель	Приоритет	Stage
ECR-19	[24 октября] Объединить скриншоты YouTrack в один PDF	Mansur Urynbassar	Серьезная	Разработка
ECR-17	[October 24] Verify Git History, Committee Access and the Submi...	Aibekyly Alibi	Серьезная	Разработка
~~ECR-24~~	[October 24] Compile and Verify the Consolidated PDF Report	Akhmetov Nurali	Критическая	Готово
~~ECR-18~~	[October 24] Verify the Submission Package Against the 11 Comm...	Akhmetov Nurali	Серьезная	Готово
~~ECR-16~~	[October 24] Obtain Supervisor Feedback and Address Comments	Akhmetov Nurali	Серьезная	Готово
~~ECR-14~~	[October 24] Verify and Extend the README and GitHub Reposito...	Aibekyly Alibi	Серьезная	Готово
~~ECR-15~~	[October 24] Document Project Stages, Risks, and Dependencies	Akhmetov Nurali	Серьезная	Готово
~~ECR-13~~	[October 24] Prepare the Verification and Evaluation Plan	Akhmetov Nurali	Серьезная	Готово
~~ECR-8~~	[October 24] Define Administrative Requirements and the Access...	Akhmetov Nurali	Серьезная	Готово
ECR-23	[After October 24] Implement the Administrative Module and Rep...	Akhmetov Nurali	Обычная	Очередь
~~ECR-9~~	[October 24] Prepare the Key-Scenario UX Prototype	Mansur Urynbassar	Серьезная	Готово
~~ECR-11~~	[October 24] Prepare the Use Case Diagram	Mansur Urynbassar	Серьезная	Готово
~~ECR-5~~	[October 24] Compare Existing Booking Systems	Mansur Urynbassar	Серьезная	Готово
~~ECR-3~~	[October 24] Collect Evidence of Relevance and User Needs	Mansur Urynbassar	Серьезная	Готово
~~ECR-1~~	[October 24] Define Visitor and Administrator Scenarios	Mansur Urynbassar	Серьезная	Готово

All 24 tasks - owners, priorities and statuses


Original YouTrack screenshot | Part 2/2 | https://nerybr.youtrack.cloud/issues/ECR

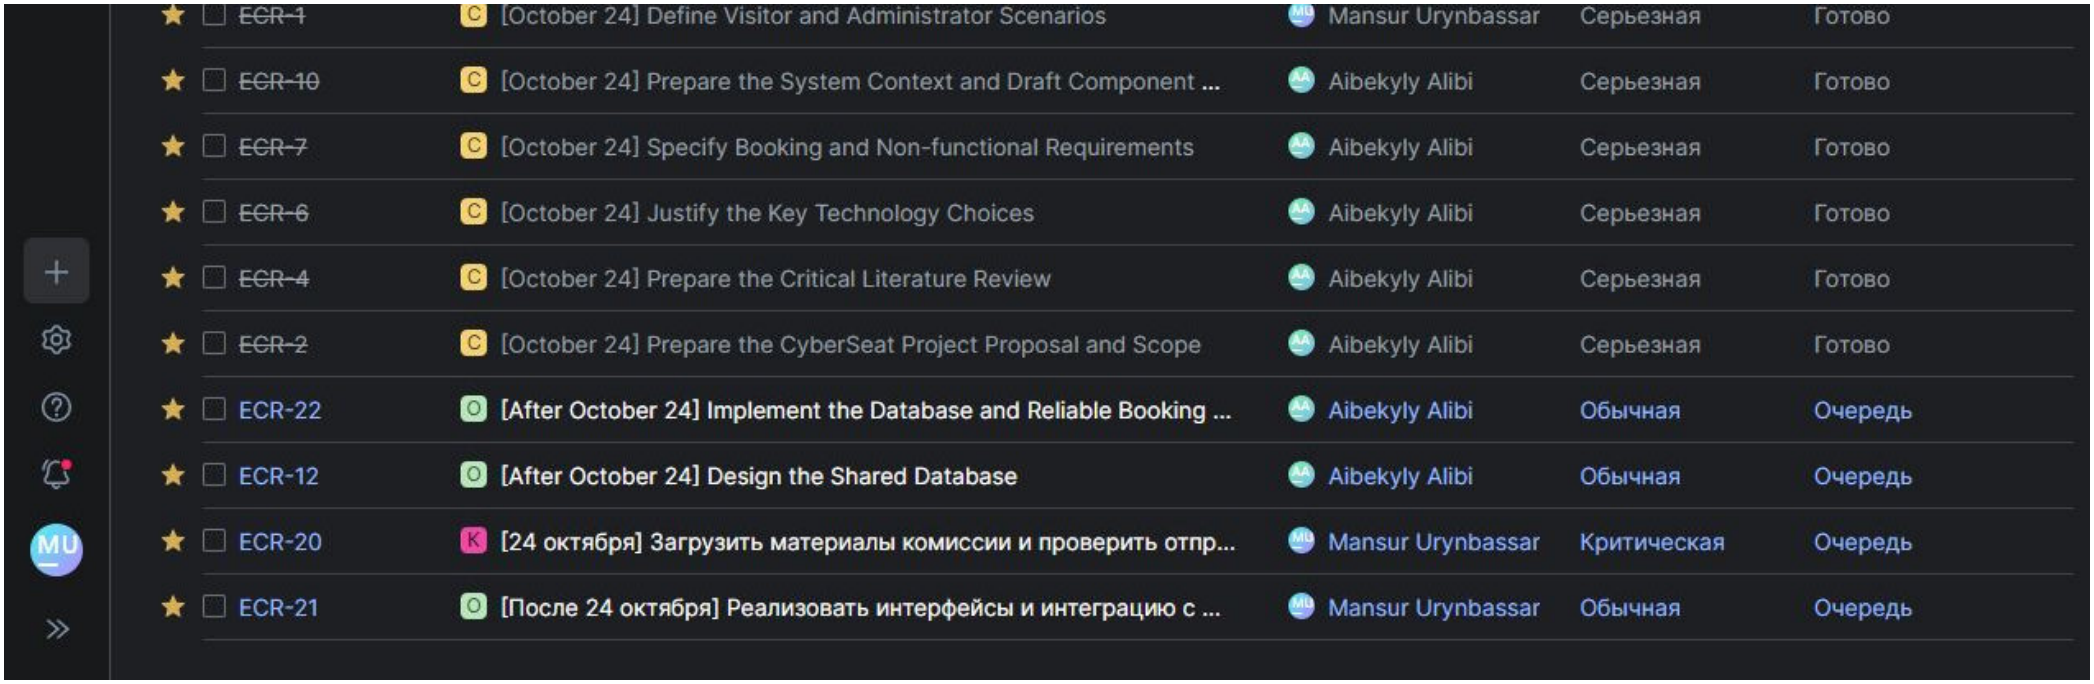

~~ECR-1~~	[October 24] Define Visitor and Administrator Scenarios	Mansur Urynbassar	Серьезная	Готово
~~ECR-10~~	[October 24] Prepare the System Context and Draft Component ...	Aibekyly Alibi	Серьезная	Готово
~~ECR-7~~	[October 24] Specify Booking and Non-functional Requirements	Aibekyly Alibi	Серьезная	Готово
~~ECR-6~~	[October 24] Justify the Key Technology Choices	Aibekyly Alibi	Серьезная	Готово
~~ECR-4~~	[October 24] Prepare the Critical Literature Review	Aibekyly Alibi	Серьезная	Готово
~~ECR-2~~	[October 24] Prepare the CyberSeat Project Proposal and Scope	Aibekyly Alibi	Серьезная	Готово
ECR-22	[After October 24] Implement the Database and Reliable Booking ...	Aibekyly Alibi	Обычная	Очередь
ECR-12	[After October 24] Design the Shared Database	Aibekyly Alibi	Обычная	Очередь
ECR-20	[24 октября] Загрузить материалы комиссии и проверить отпр...	Mansur Urynbassar	Критическая	Очередь
ECR-21	[После 24 октября] Реализовать интерфейсы и интеграцию с ...	Mansur Urynbassar	Обычная	Очередь

ECR-1 - criteria, result links and review evidence

Original YouTrack screenshot | Part 1/6 | https://nerybr.youtrack.cloud/issue/ECR-1

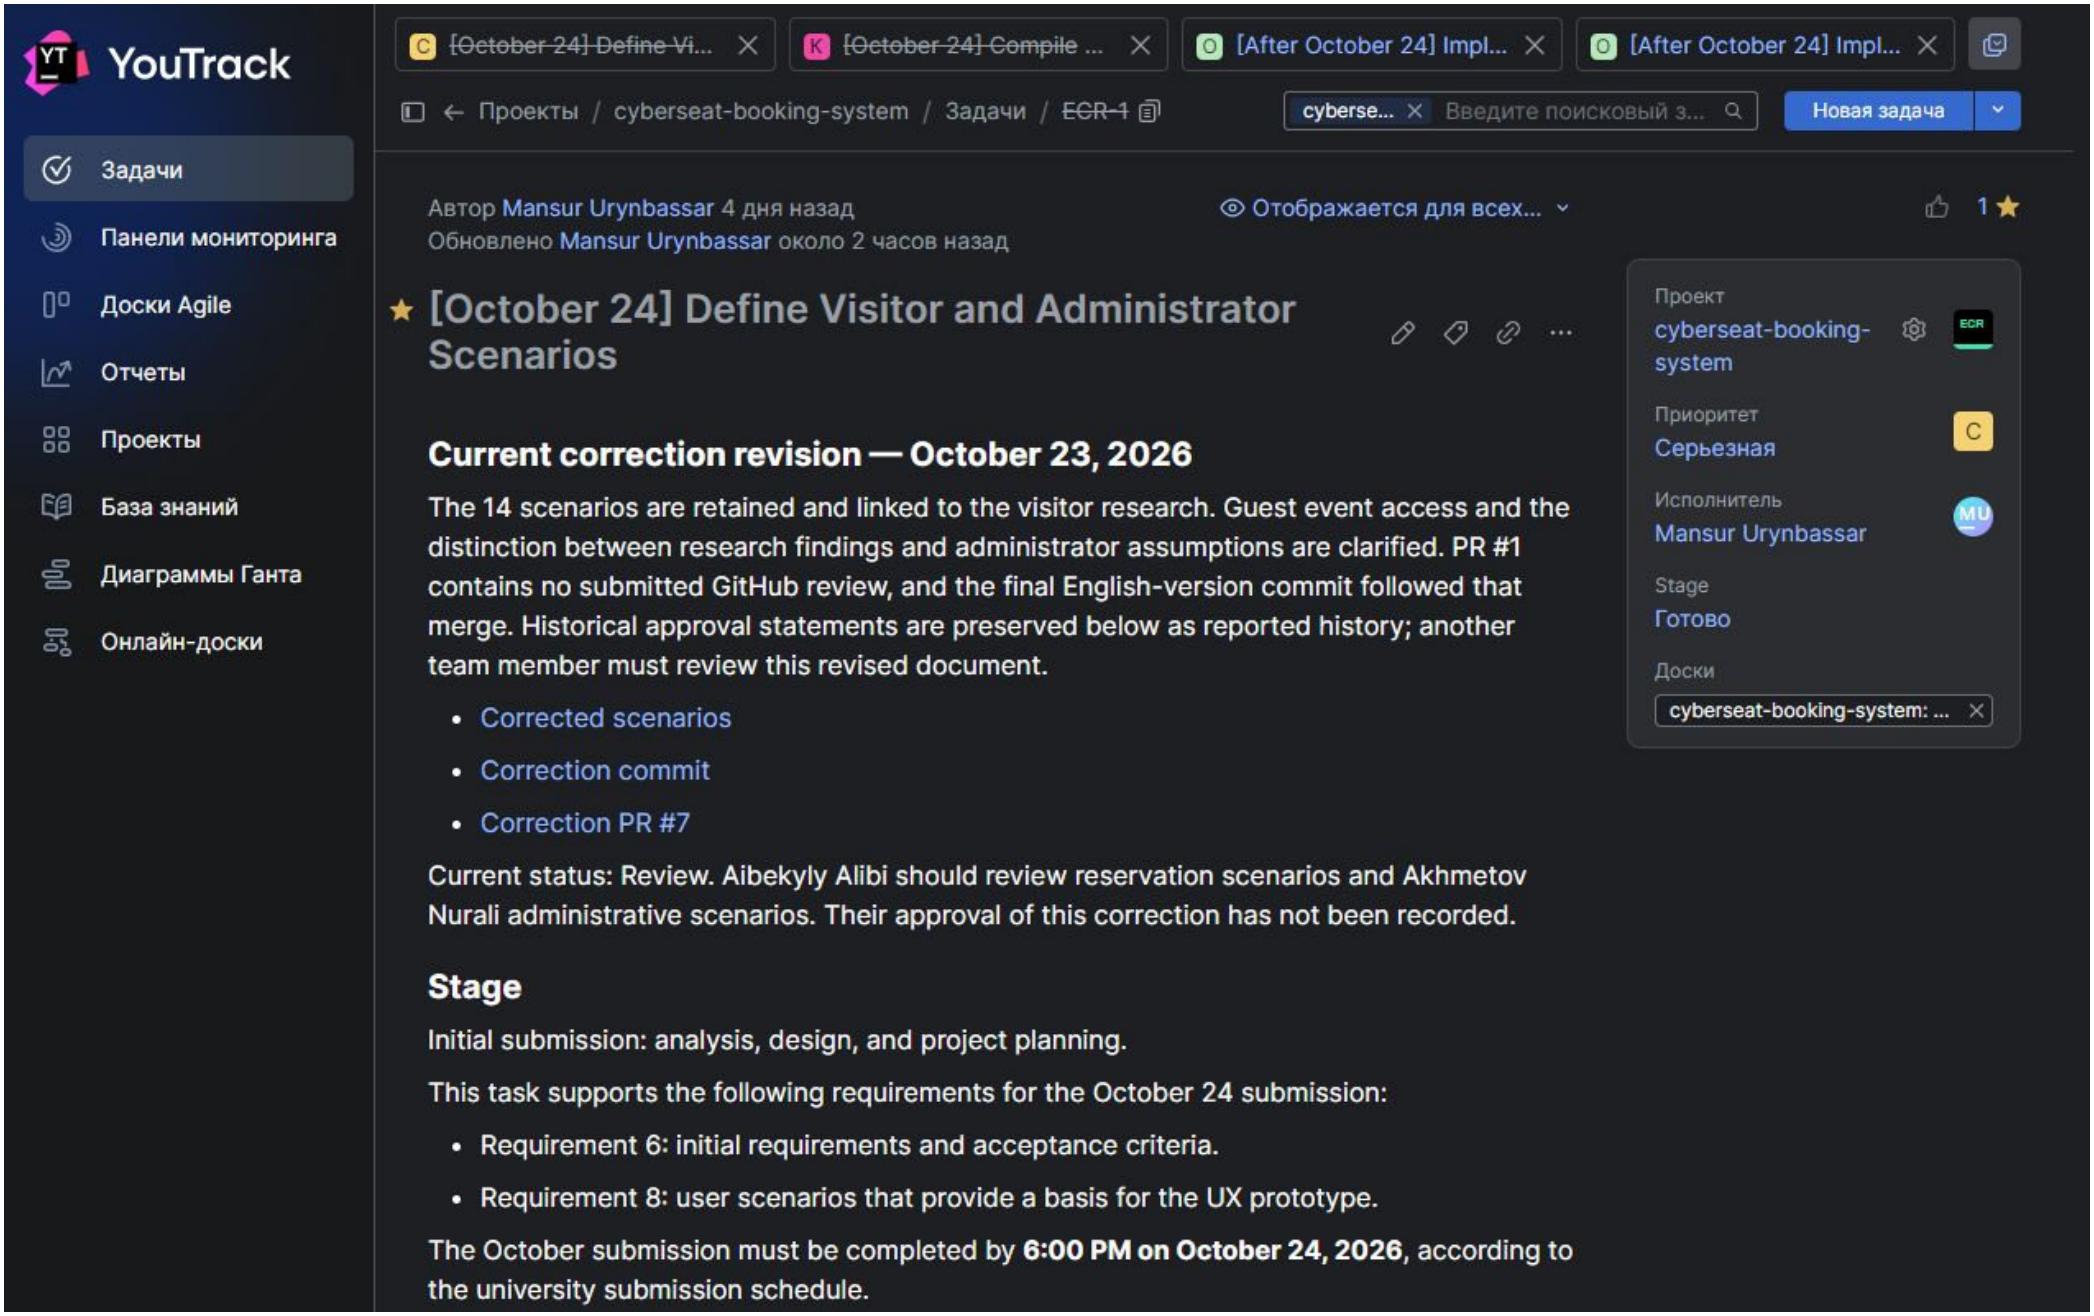

the university submission schedule.

A complete application, implemented backend or frontend, and final test results are not required at this stage.

Expected Result

An English-language document describing the principal visitor and administrator scenarios:

`docs/requirements/user-scenarios.md`

Acceptance Criteria

The document must include:

- club selection and club information;
- date, time, and gaming-station selection;
- reservation creation and availability revalidation;
- viewing and cancelling personal reservations;
- concurrent reservation conflict handling;
- event-calendar access;
- gaming-station and schedule management;
- maintenance and unavailable intervals;
- administrative access control;
- club reservations, events, and reports;
- loading, validation, server-error, and connection-loss states.

Each scenario must define:

- actor;
- preconditions;
- trigger;
- main flow;

- main flow;
- expected result;
- alternative and error flows;
- acceptance criteria.

The reservation scenarios must be reviewed by Aibekyly Alibi. The administrative scenarios and access-control rules must be reviewed by Akhmetov Nurali. Mansur Urynbassar is responsible for document preparation and consistency with the planned interfaces.

Dependencies

The document is based on the approved project scope, team justifications, and CyberSeat README.

The scenarios provide input for the requirements specification, Use Case diagram, and UX mockups. They do not replace these separate deliverables.

Historical completion report (before correction)


The final English document contains 14 visitor and administrator scenarios. It also includes common interface states, traceability to ~~ECR-1~~, approved team decisions, and team-review results.

The previous completion report stated that all team members approved the document on October 23, 2026. These are reported historical statements, not evidence of a submitted GitHub review for the correction:

- Mansur Urynbassar reviewed consistency with the planned visitor and administrator interfaces.
- Aibekyly Alibi reviewed reservation, availability, cancellation, and conflict-prevention scenarios.
- Akhmetov Nurali reviewed administrative operations, access control, schedules, events, and reporting.


Historical completion evidence

Document:

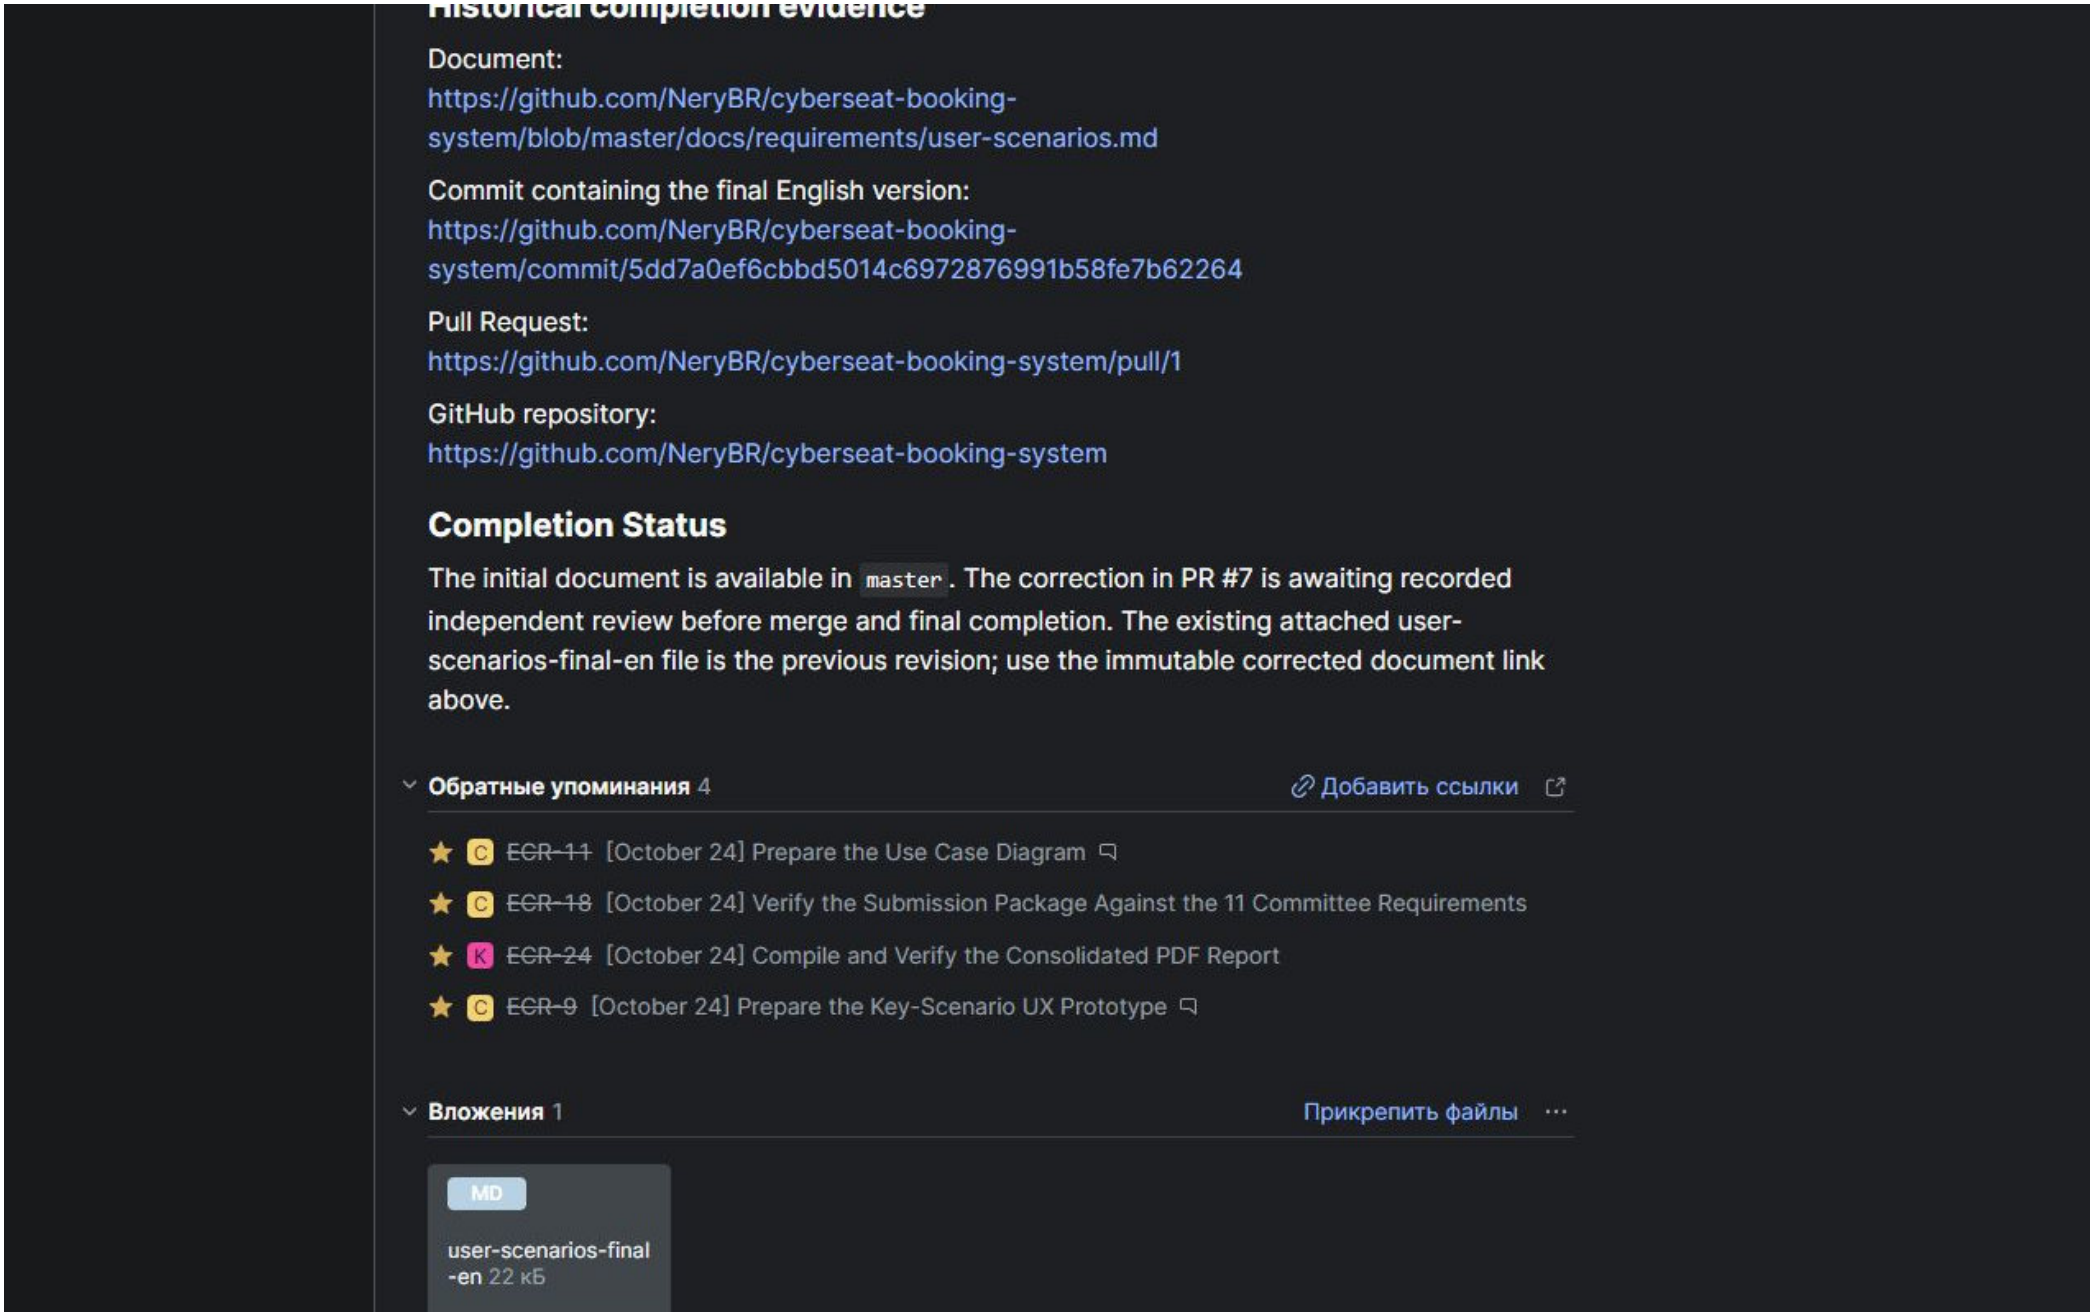
Historical completion evidence
Document:
https://github.com/NeryBR/cyberseat-booking-system/blob/master/docs/requirements/user-scenarios.md
Commit containing the final English version:
https://github.com/NeryBR/cyberseat-booking-system/commit/5dd7a0ef6cbbd5014c6972876991b58fe7b62264
Pull Request:
https://github.com/NeryBR/cyberseat-booking-system/pull/1
GitHub repository:
https://github.com/NeryBR/cyberseat-booking-system
Completion Status
The initial document is available in master. The correction in PR #7 is awaiting recorded independent review before merge and final completion. The existing attached user-scenarios-final-en file is the previous revision; use the immutable corrected document link above.
Обратные упоминания 4
Добавить ссылки
ECR-11 [October 24] Prepare the Use Case Diagram
ECR-18 [October 24] Verify the Submission Package Against the 11 Committee Requirements
ECR-24 [October 24] Compile and Verify the Consolidated PDF Report
ECR-9 [October 24] Prepare the Key-Scenario UX Prototype
Вложения 1
Прикрепить файлы
MD
user-scenarios-final-en 22 кБ


ECR-1 - criteria, result links and review evidence

Original YouTrack screenshot | Part 5/6 | https://nerybr.youtrack.cloud/issue/ECR-1

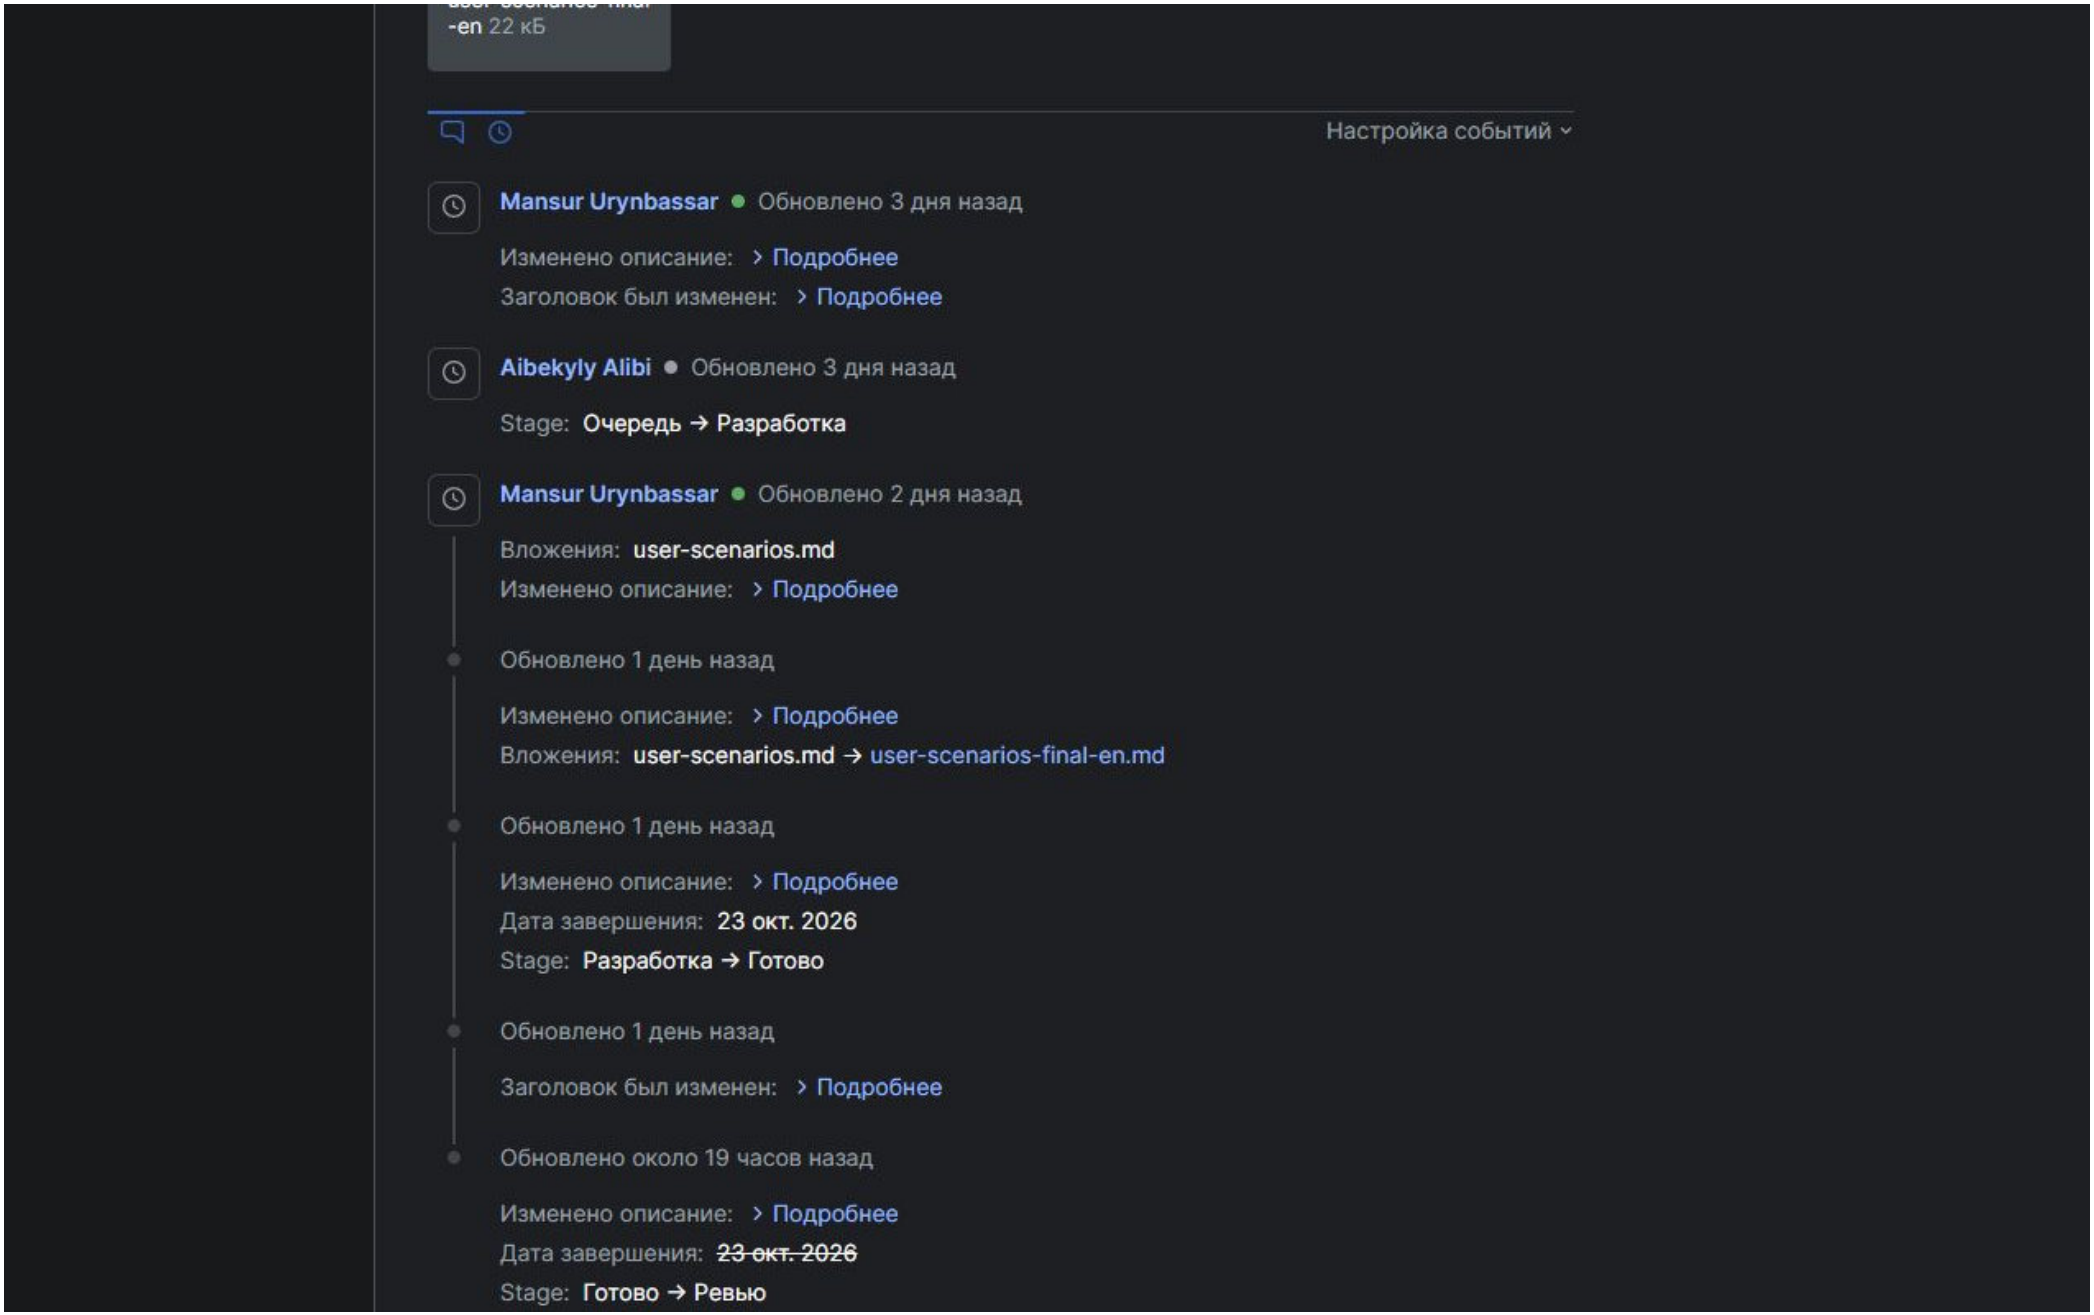


ECR-1 - criteria, result links and review evidence

Original YouTrack screenshot | Part 6/6 | https://nerybr.youtrack.cloud/issue/ECR-1

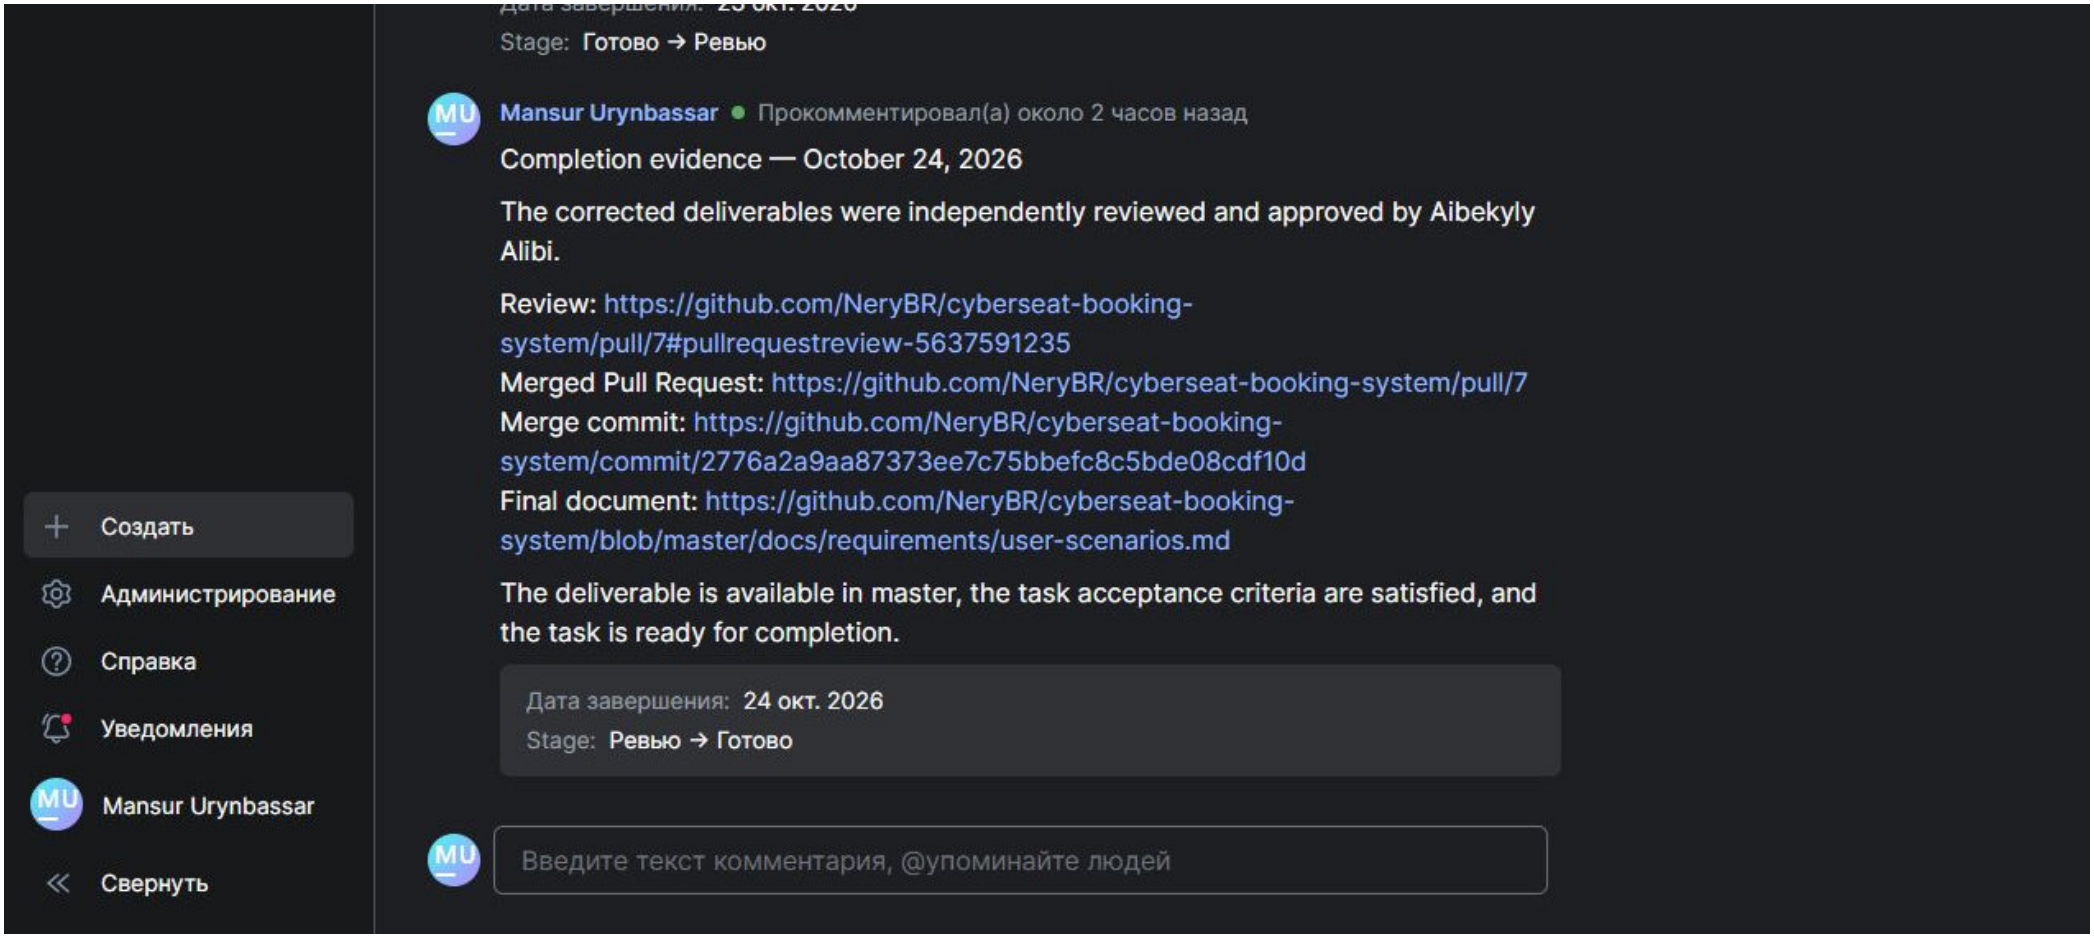

ECR-2 - criteria, result links and review evidence

Original YouTrack screenshot | Part 1/3 | https://nerybr.youtrack.cloud/issue/ECR-2

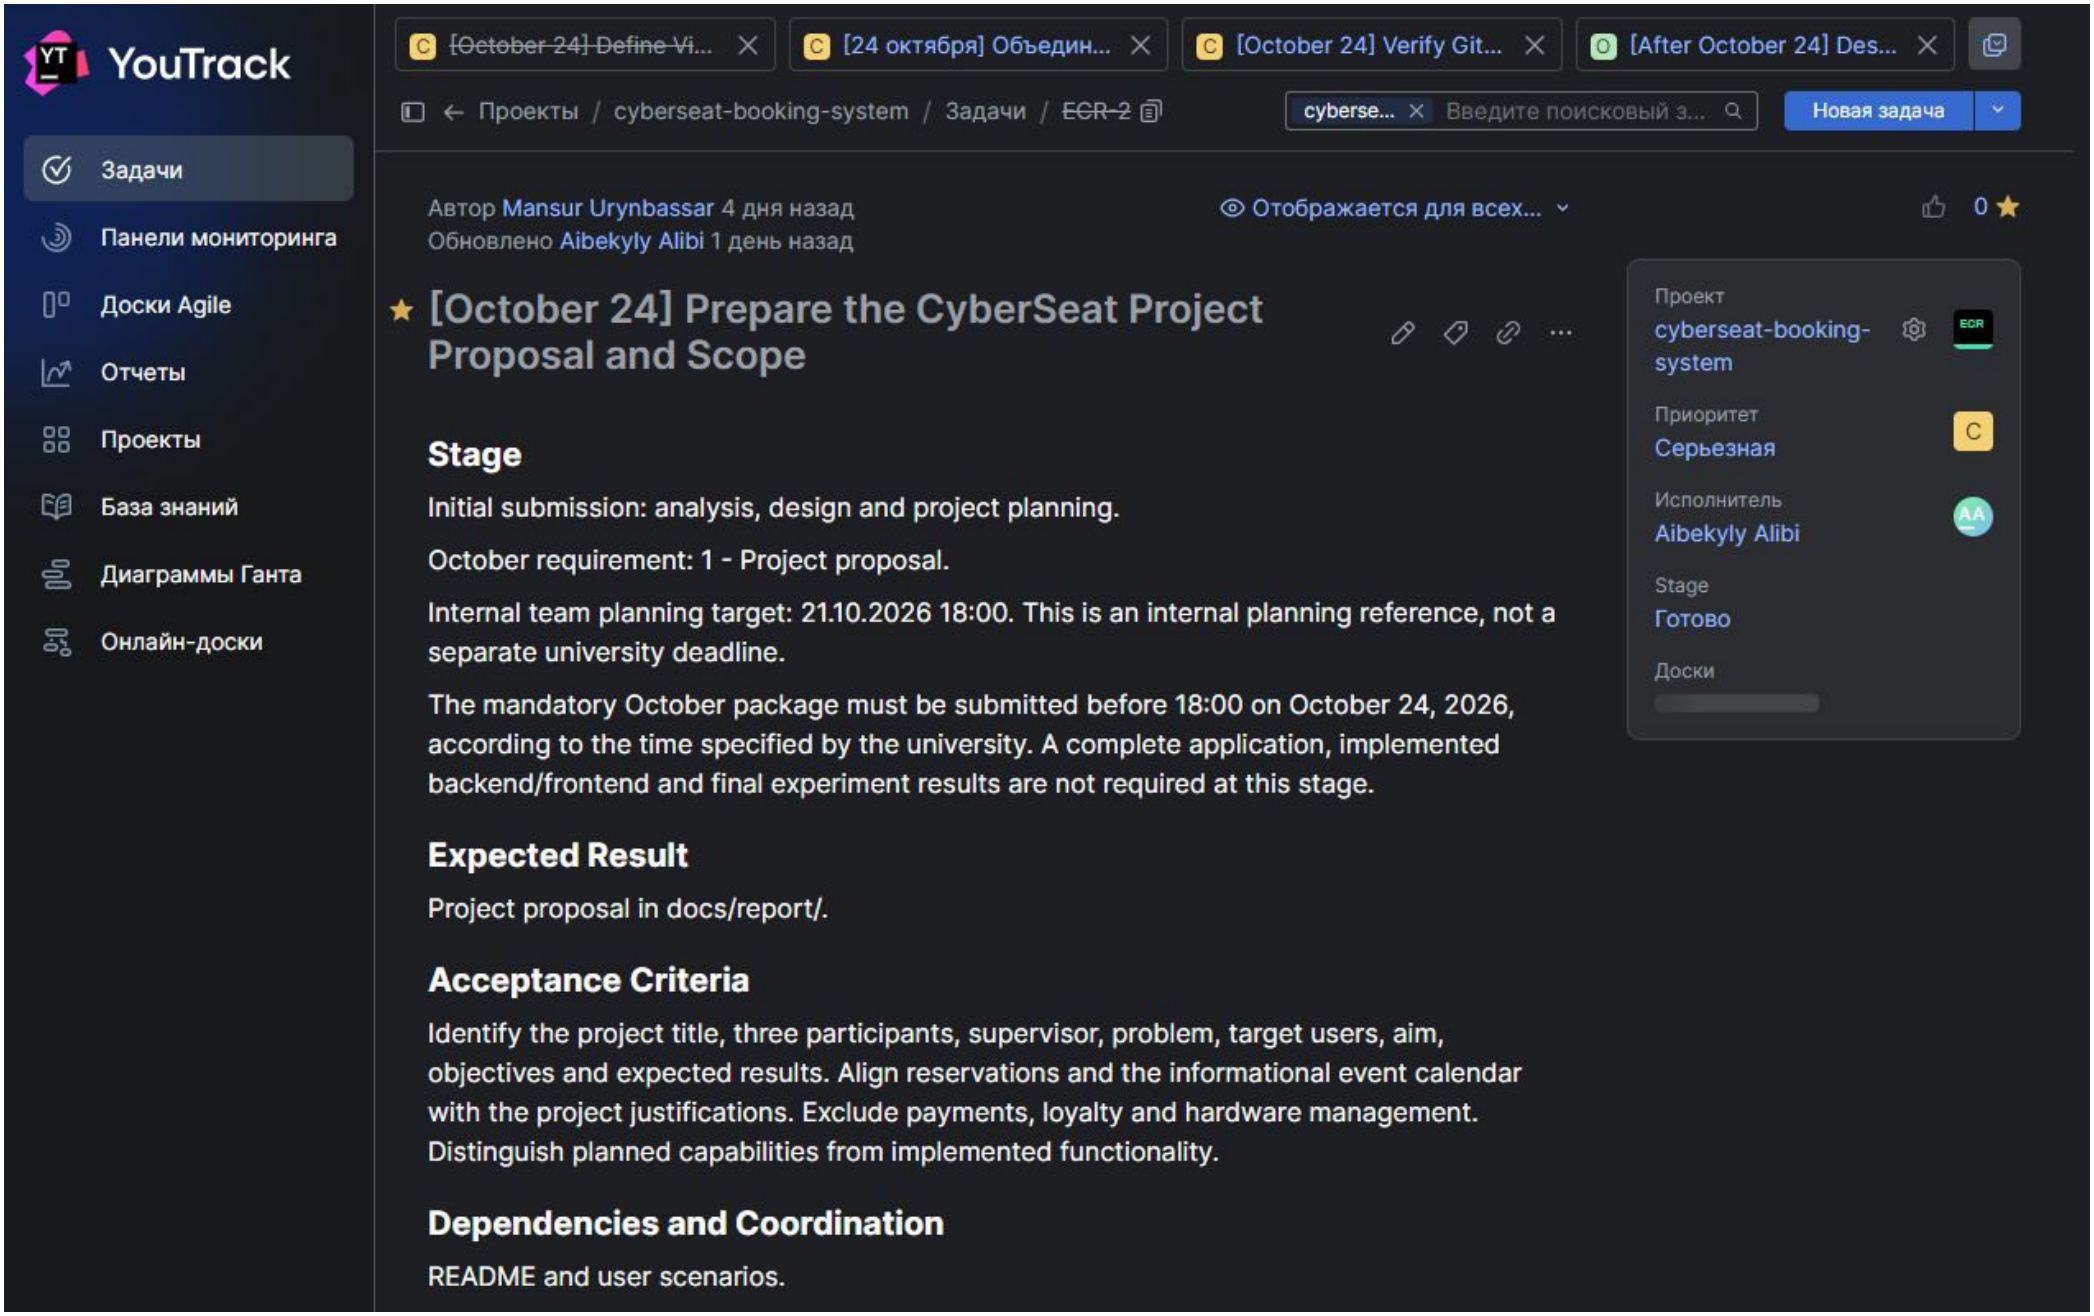

README and user scenarios.

Completion Evidence

Provide the deliverable and commit/Pull Request links and identify the reviewing participant. Mark Done only after the acceptance criteria are satisfied.

Repository

https://github.com/NeryBR/cyberseat-booking-system

Completed Deliverable

https://github.com/NeryBR/cyberseat-booking-system/blob/codex/alibi-october24-deliverables/docs/report/project-proposal.md

Pull Request: https://github.com/NeryBR/cyberseat-booking-system/pull/3

Package commit: https://github.com/NeryBR/cyberseat-booking-system/commit/0fc2c4555821922e0dae7b233e091281e36a89f3

Combined PDF: https://github.com/NeryBR/cyberseat-booking-system/blob/codex/alibi-october24-deliverables/docs/report/CyberSeat_Alibi_October24.pdf

Team Agreement

On October 23, 2026, Alibi confirmed in the working chat that his teammates agree with all prepared materials and instructed that the tasks be completed. Team agreement is recorded on the basis of Alibi's confirmation; it is not represented as a separate GitHub approval submitted by the teammates.

Review areas: Mansur: visitor/event scope; Nurali: administration and evaluation.

The documentation deliverable is complete. Implementation and final experiment results remain later-stage work.


Document Presentation

The linked PDF has been redesigned as a 36-page portrait dossier with clickable contents, PDF bookmarks, section navigation, readable source/requirement cards and full-page architectural views. All 16 BR, 10 NFR and 13 source IDs are preserved.

+ Создать


ECR-2 - criteria, result links and review evidence


Original YouTrack screenshot | Part 3/3 | https://nerybr.youtrack.cloud/issue/ECR-2

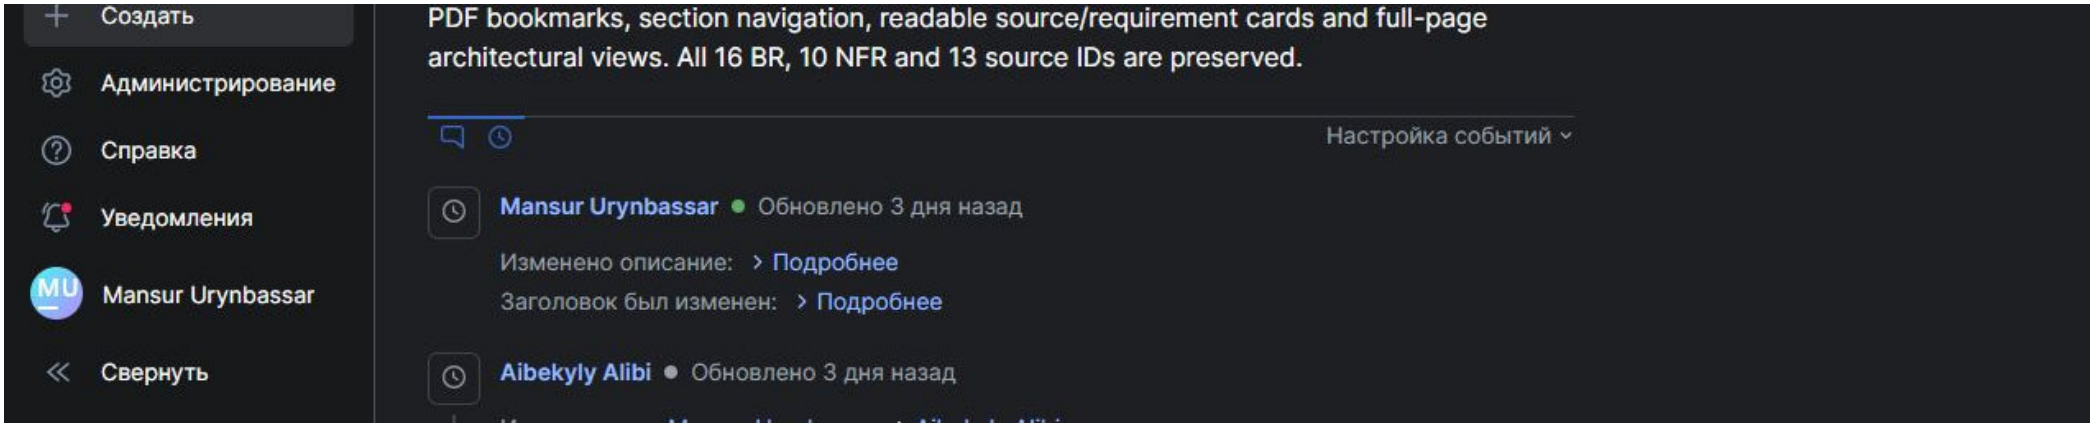

ECR-8 - criteria, result links and review evidence

Original YouTrack screenshot | Part 1/4 | https://nerybr.youtrack.cloud/issue/ECR-8

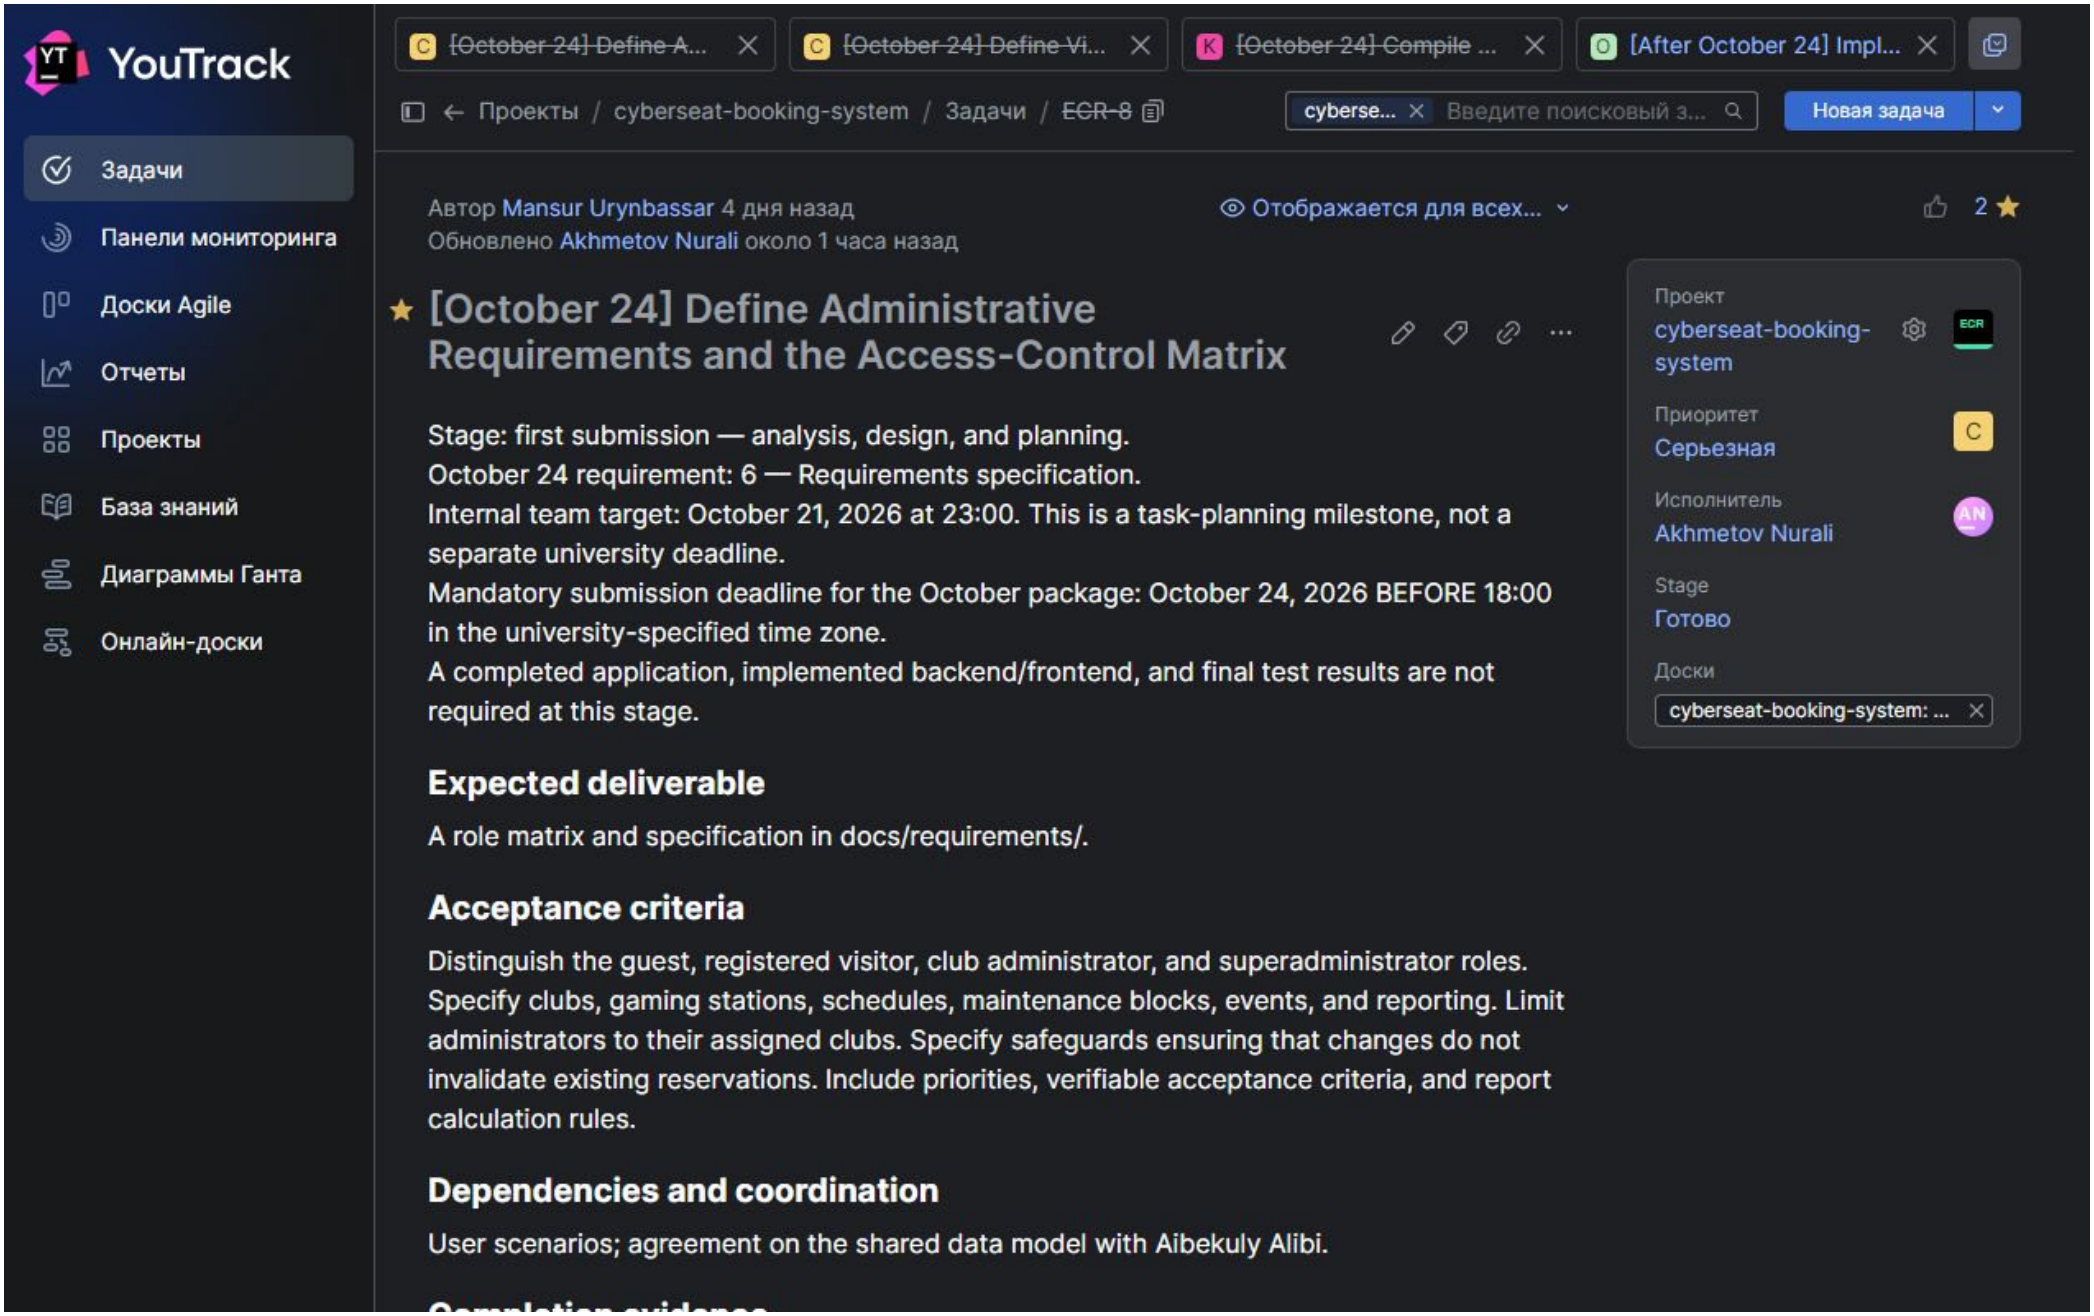

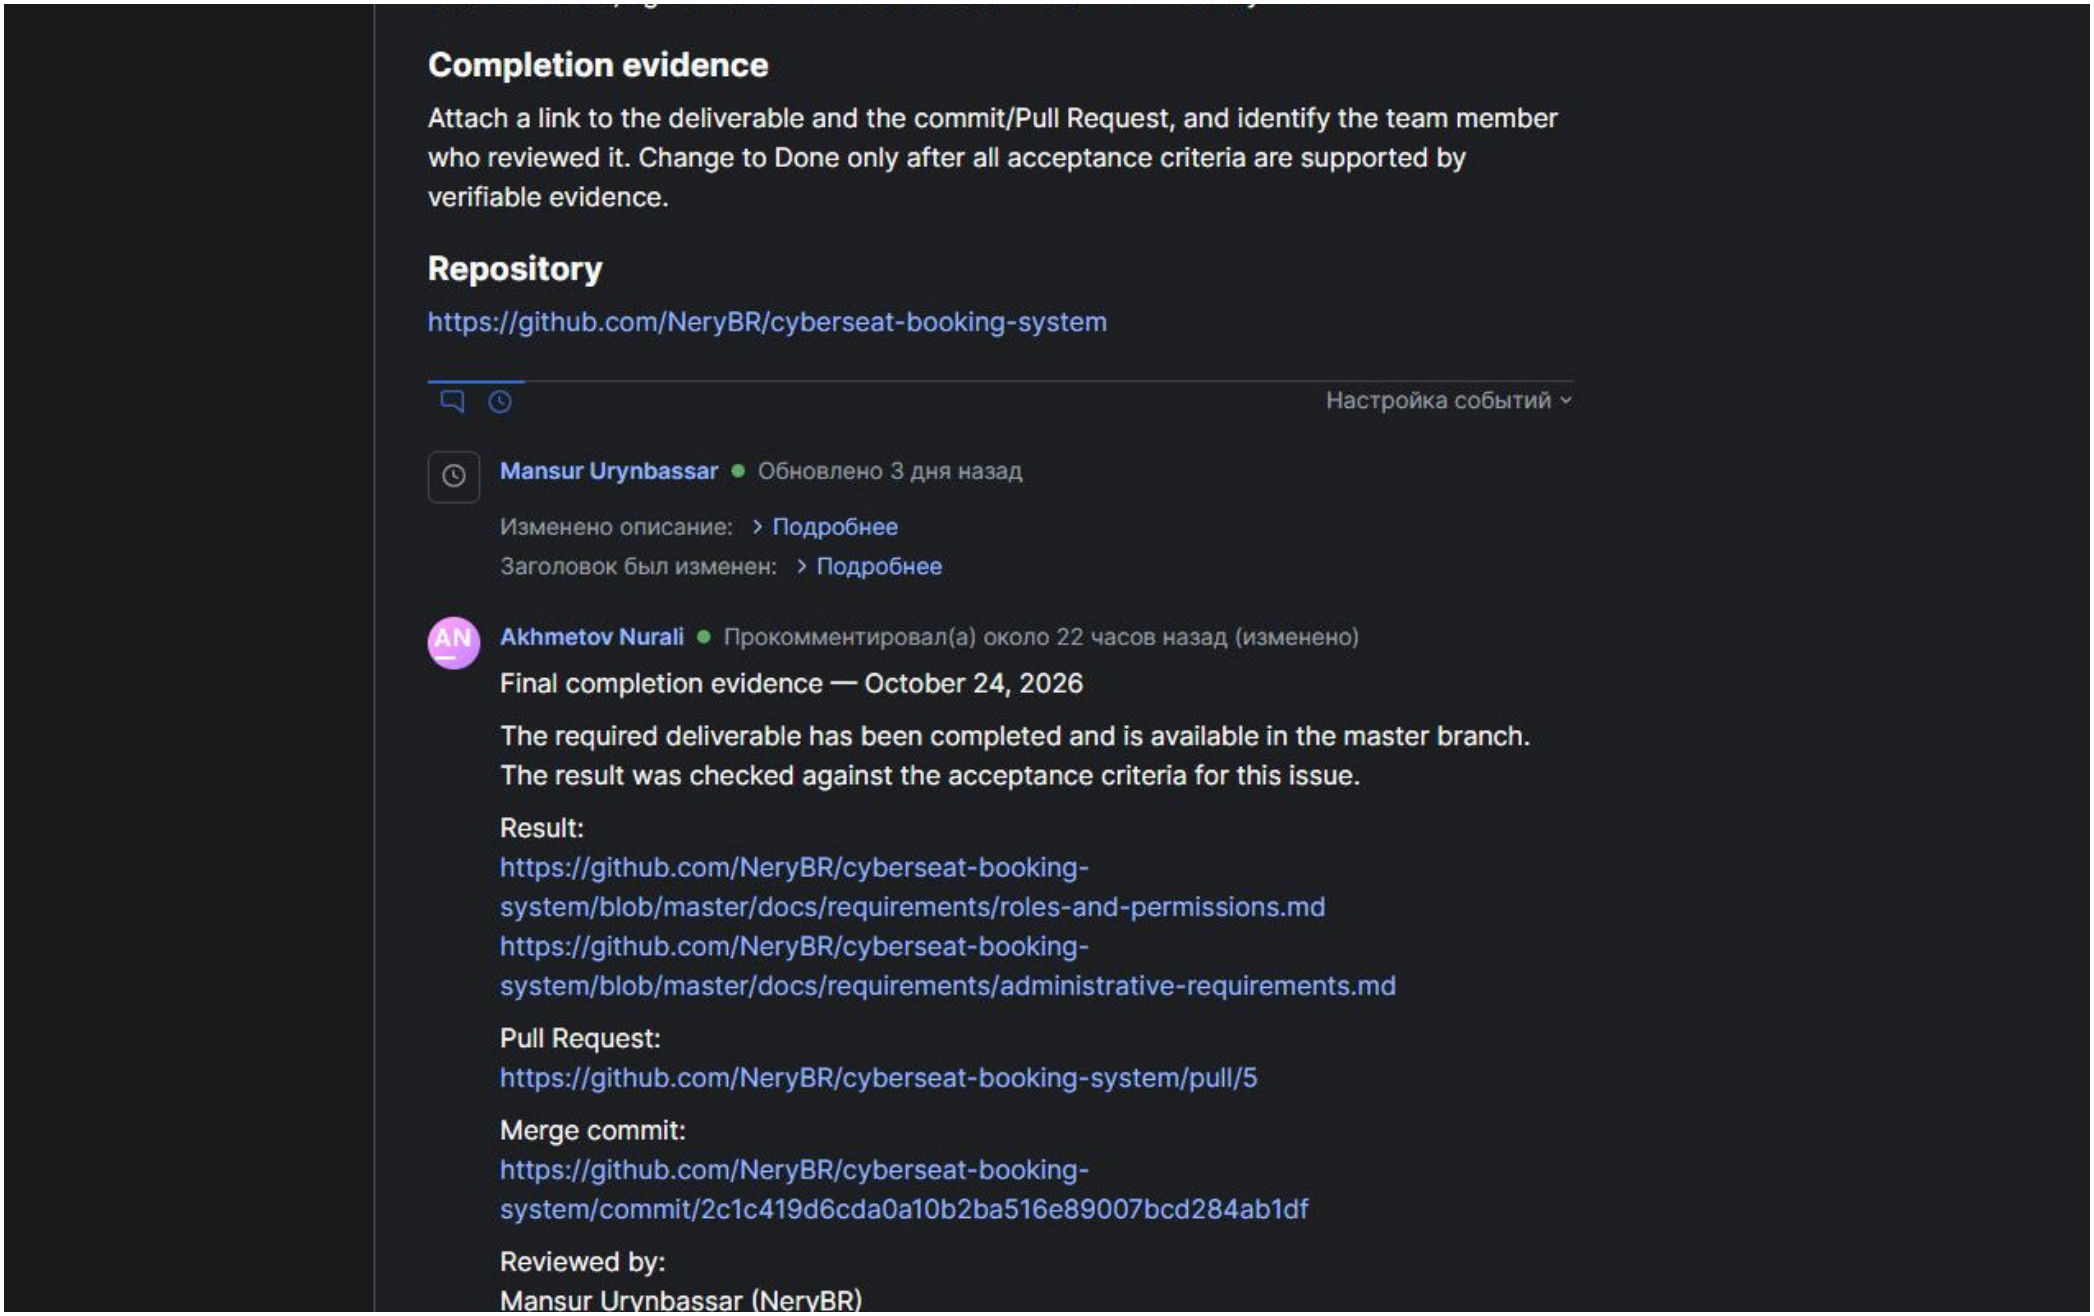
Completion evidence
Attach a link to the deliverable and the commit/Pull Request, and identify the team member who reviewed it. Change to Done only after all acceptance criteria are supported by verifiable evidence.
Repository
https://github.com/NeryBR/cyberseat-booking-system
Настройка событий
Mansur Urynbassar • Обновлено 3 дня назад
Изменено описание: › Подробнее
Заголовок был изменен: › Подробнее
AN
Akhmetov Nurali • Прокомментировал(а) около 22 часов назад (изменено)
Final completion evidence — October 24, 2026
The required deliverable has been completed and is available in the master branch.
The result was checked against the acceptance criteria for this issue.
Result:
https://github.com/NeryBR/cyberseat-booking-system/blob/master/docs/requirements/roles-and-permissions.md
https://github.com/NeryBR/cyberseat-booking-system/blob/master/docs/requirements/administrative-requirements.md
Pull Request:
https://github.com/NeryBR/cyberseat-booking-system/pull/5
Merge commit:
https://github.com/NeryBR/cyberseat-booking-system/commit/2c1c419d6cda0a10b2ba516e89007bcd284ab1df
Reviewed by:
Mansur Urynbassar (NeryBR)

Reviewed by:
Mansur Urynbassar (NeryBR)

Review:
https://github.com/NeryBR/cyberseat-booking-system/pull/5#pullrequestreview-5637447311

Completion status:
The documented acceptance criteria for the October analysis-and-design submission are satisfied. This result does not claim that the final software system has been implemented or fully tested.

Дата завершения: 23 окт. 2026
Stage: Очередь → Готово

MU **Mansur Urynbassar** • Прокомментировал(а) около 1 часа назад (изменено)


Checklist verification — October 24, 2026, assisted by Codex.

The issue was already Done. The criteria were mapped to the specification: four roles, assigned-club restrictions, ADM-01–15, protection of existing reservations, priorities, acceptance criteria, and report formulas.

Specification:
https://github.com/NeryBR/cyberseat-booking-system/blob/834f87e1a78a5ebc1b5c29097b856427dd43f993/docs/requirements/administrative-requirements.md
Role matrix:
https://github.com/NeryBR/cyberseat-booking-system/blob/834f87e1a78a5ebc1b5c29097b856427dd43f993/docs/requirements/roles-and-permissions.md
Pull Request:
https://github.com/NeryBR/cyberseat-booking-system/pull/5
Reviewed commit: 834f87e1a78a5ebc1b5c29097b856427dd43f993
Actual GitHub review by Mansur Urynbassar (NeryBR):
https://github.com/NeryBR/cyberseat-booking-system/pull/5#pullrequestreview-5637447311


ECR-8 - criteria, result links and review evidence


Original YouTrack screenshot | Part 4/4 | https://nerybr.youtrack.cloud/issue/ECR-8

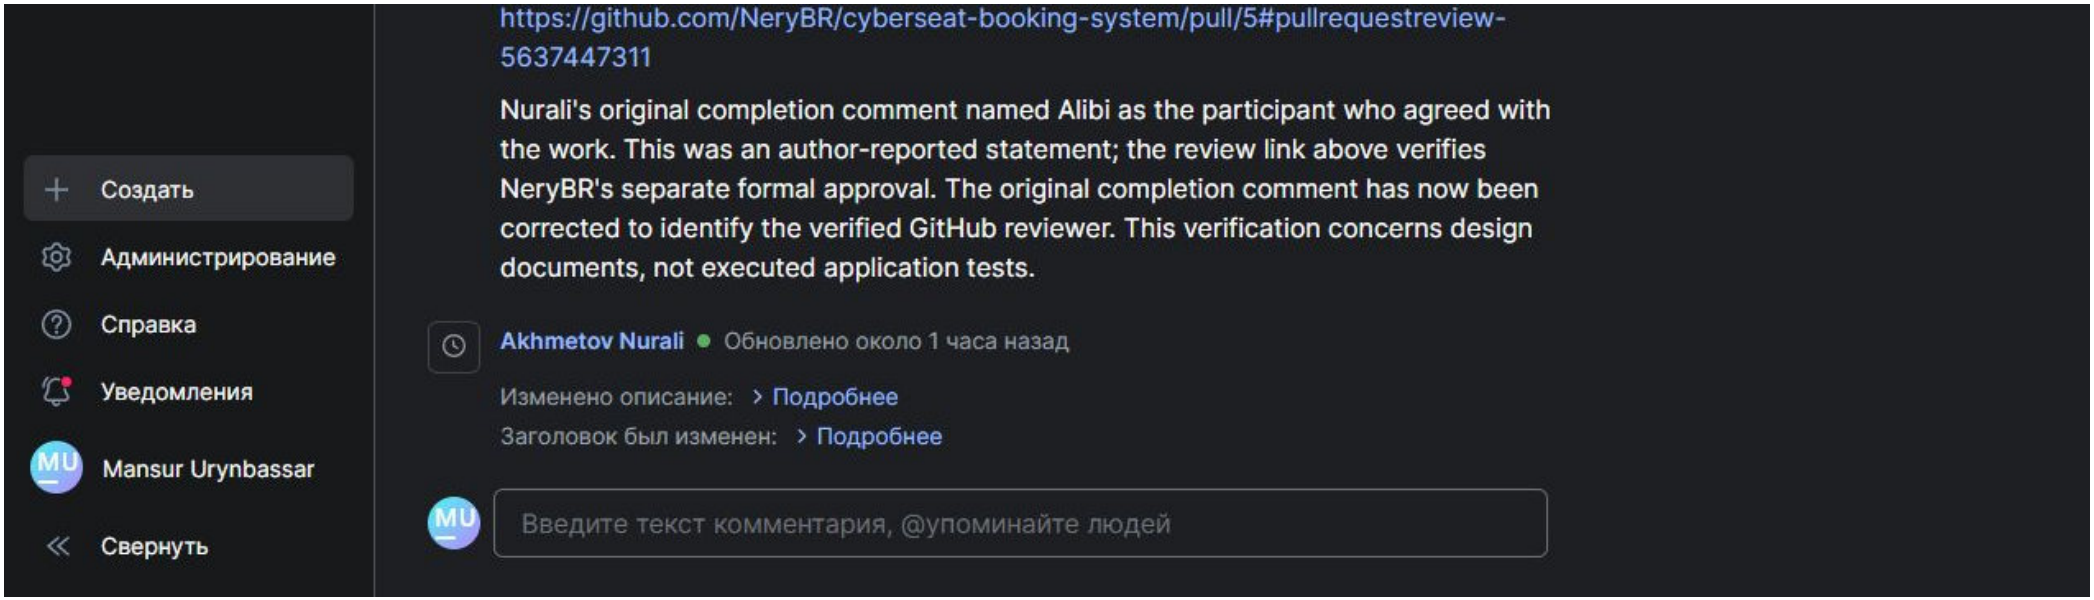

ECR-14 - criteria, result links and review evidence

Original YouTrack screenshot | Part 1/5 | https://nerybr.youtrack.cloud/issue/ECR-14

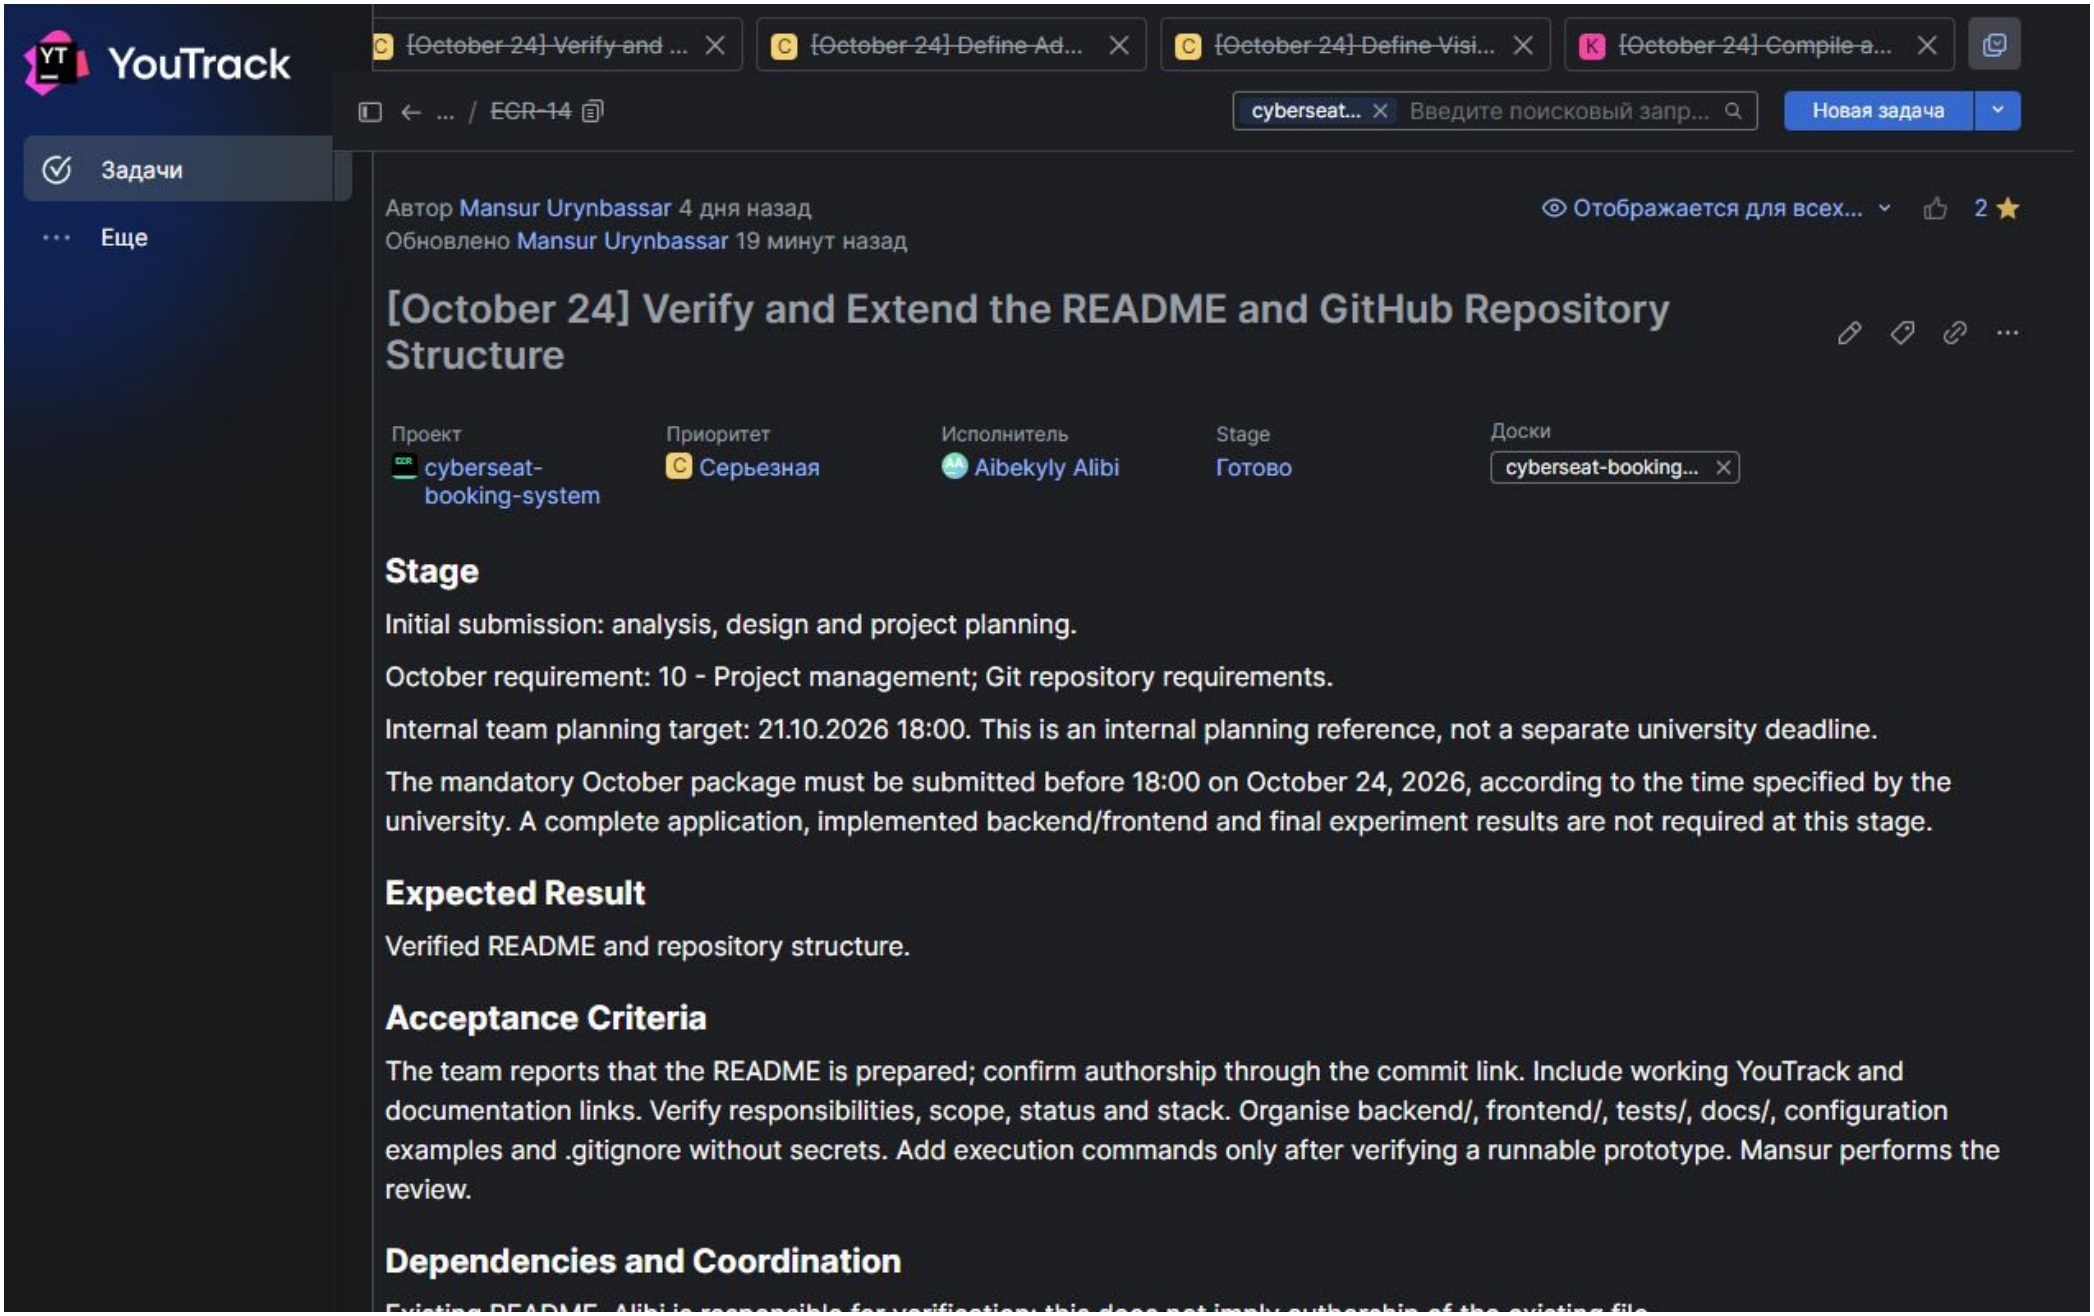

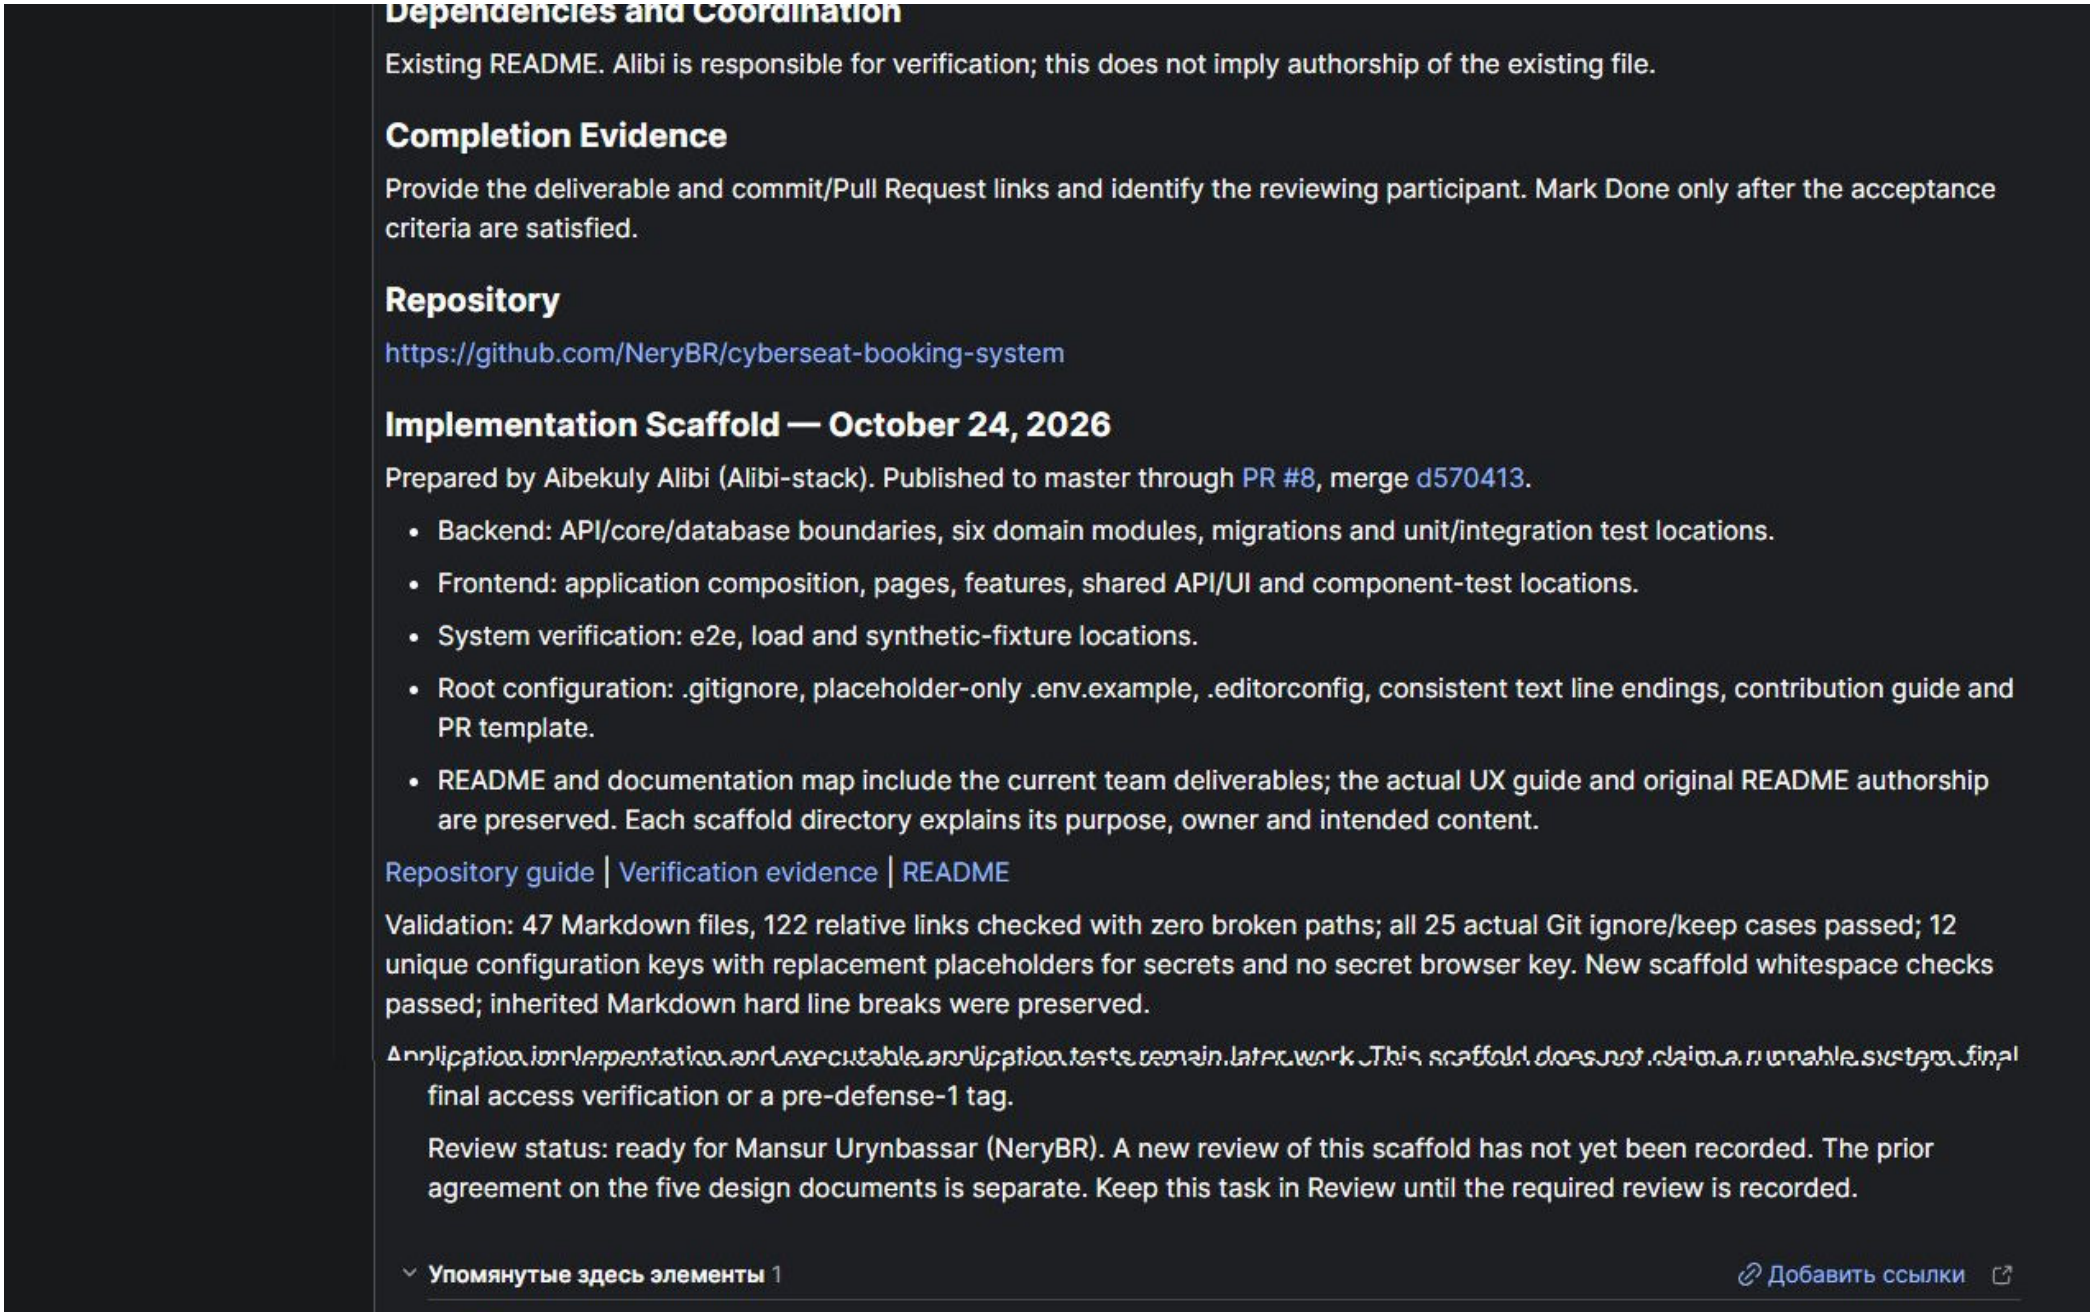

Dependencies and Coordination

Existing README. Alibi is responsible for verification; this does not imply authorship of the existing file.

Completion Evidence

Provide the deliverable and commit/Pull Request links and identify the reviewing participant. Mark Done only after the acceptance criteria are satisfied.

Repository

https://github.com/NeryBR/cyberseat-booking-system

Implementation Scaffold — October 24, 2026

Prepared by Aibekuly Alibi (Alibi-stack). Published to master through PR #8, merge d570413.

- Backend: API/core/database boundaries, six domain modules, migrations and unit/integration test locations.
- Frontend: application composition, pages, features, shared API/UI and component-test locations.
- System verification: e2e, load and synthetic-fixture locations.
- Root configuration: .gitignore, placeholder-only .env.example, .editorconfig, consistent text line endings, contribution guide and PR template.
- README and documentation map include the current team deliverables; the actual UX guide and original README authorship are preserved. Each scaffold directory explains its purpose, owner and intended content.


Repository guide | Verification evidence | README


Validation: 47 Markdown files, 122 relative links checked with zero broken paths; all 25 actual Git ignore/keep cases passed; 12 unique configuration keys with replacement placeholders for secrets and no secret browser key. New scaffold whitespace checks passed; inherited Markdown hard line breaks were preserved.

Application implementation and executable application tests remain later work. This scaffold does not claim a runnable system, final final access verification or a pre-defense-1 tag.

Review status: ready for Mansur Urynbassar (NeryBR). A new review of this scaffold has not yet been recorded. The prior agreement on the five design documents is separate. Keep this task in Review until the required review is recorded.

Упомянутые здесь элементы 1 Добавить ссылки

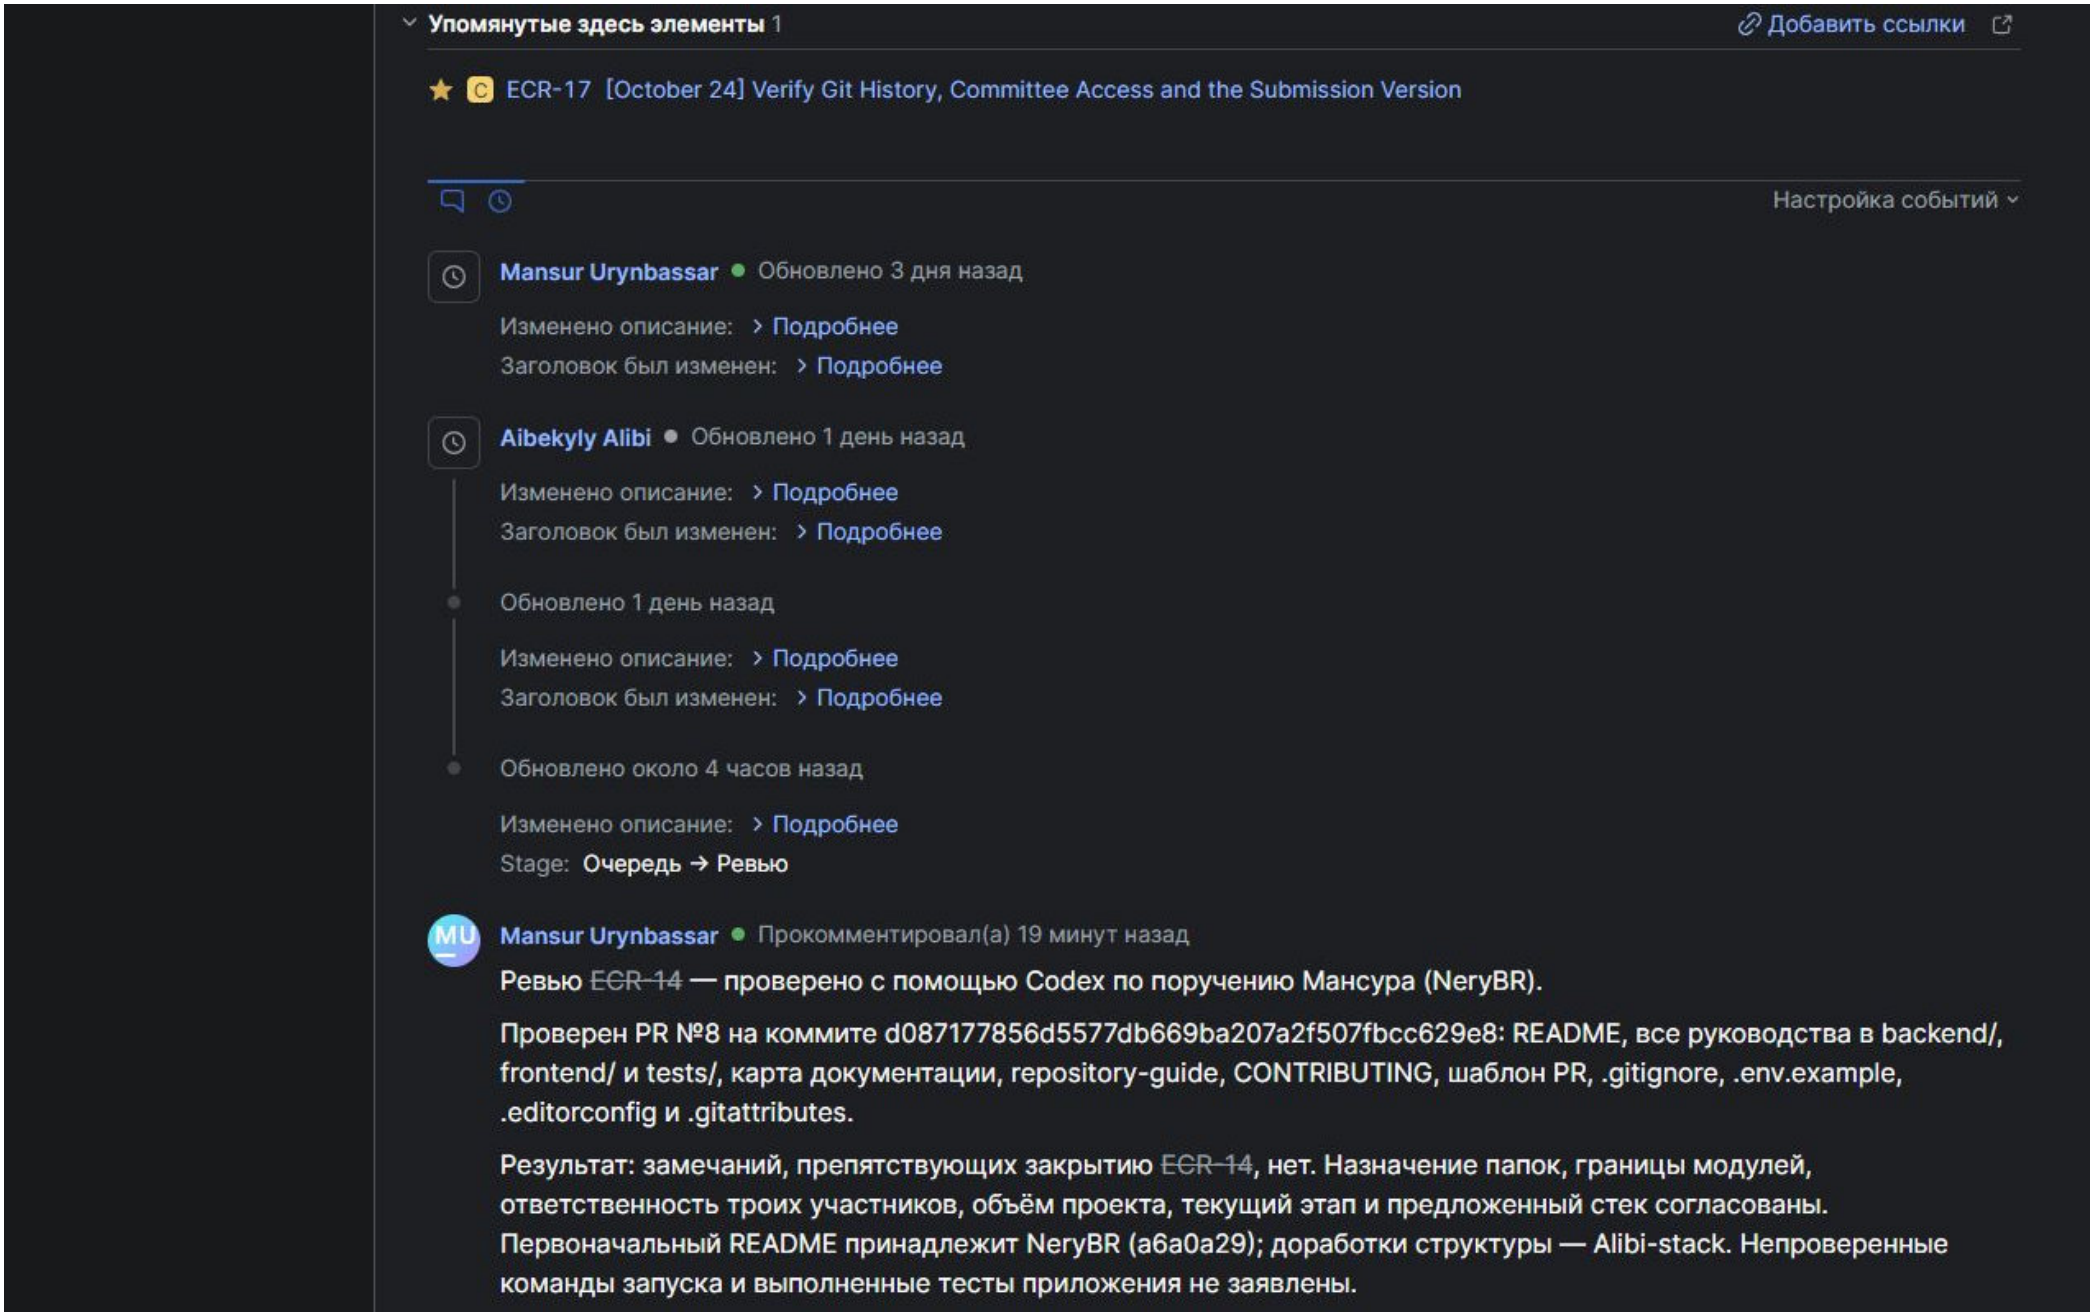
Упомянутые здесь элементы 1
Добавить ссылки
ECR-17 [October 24] Verify Git History, Committee Access and the Submission Version
Настройка событий
Mansur Urynbassar • Обновлено 3 дня назад
Изменено описание: › Подробнее
Заголовок был изменен: › Подробнее
Aibekyly Alibi • Обновлено 1 день назад
Изменено описание: › Подробнее
Заголовок был изменен: › Подробнее
Обновлено 1 день назад
Изменено описание: › Подробнее
Заголовок был изменен: › Подробнее
Обновлено около 4 часов назад
Изменено описание: › Подробнее
Stage: Очередь → Ревью
Mansur Urynbassar • Прокомментировал(а) 19 минут назад
Ревью ECR-14 — проверено с помощью Codex по поручению Мансура (NeryBR).
Проверен PR №8 на коммите d087177856d5577db669ba207a2f507fbcc629e8: README, все руководства в backend/, frontend/ и tests/, карта документации, repository-guide, CONTRIBUTING, шаблон PR, .gitignore, .env.example, .editorconfig и .gitattributes.
Результат: замечаний, препятствующих закрытию ECR-14, нет. Назначение папок, границы модулей, ответственность троих участников, объём проекта, текущий этап и предложенный стек согласованы. Первоначальный README принадлежит NeryBR (a6a0a29); доработки структуры — Alibi-stack. Непроверенные команды запуска и выполненные тесты приложения не заявлены.

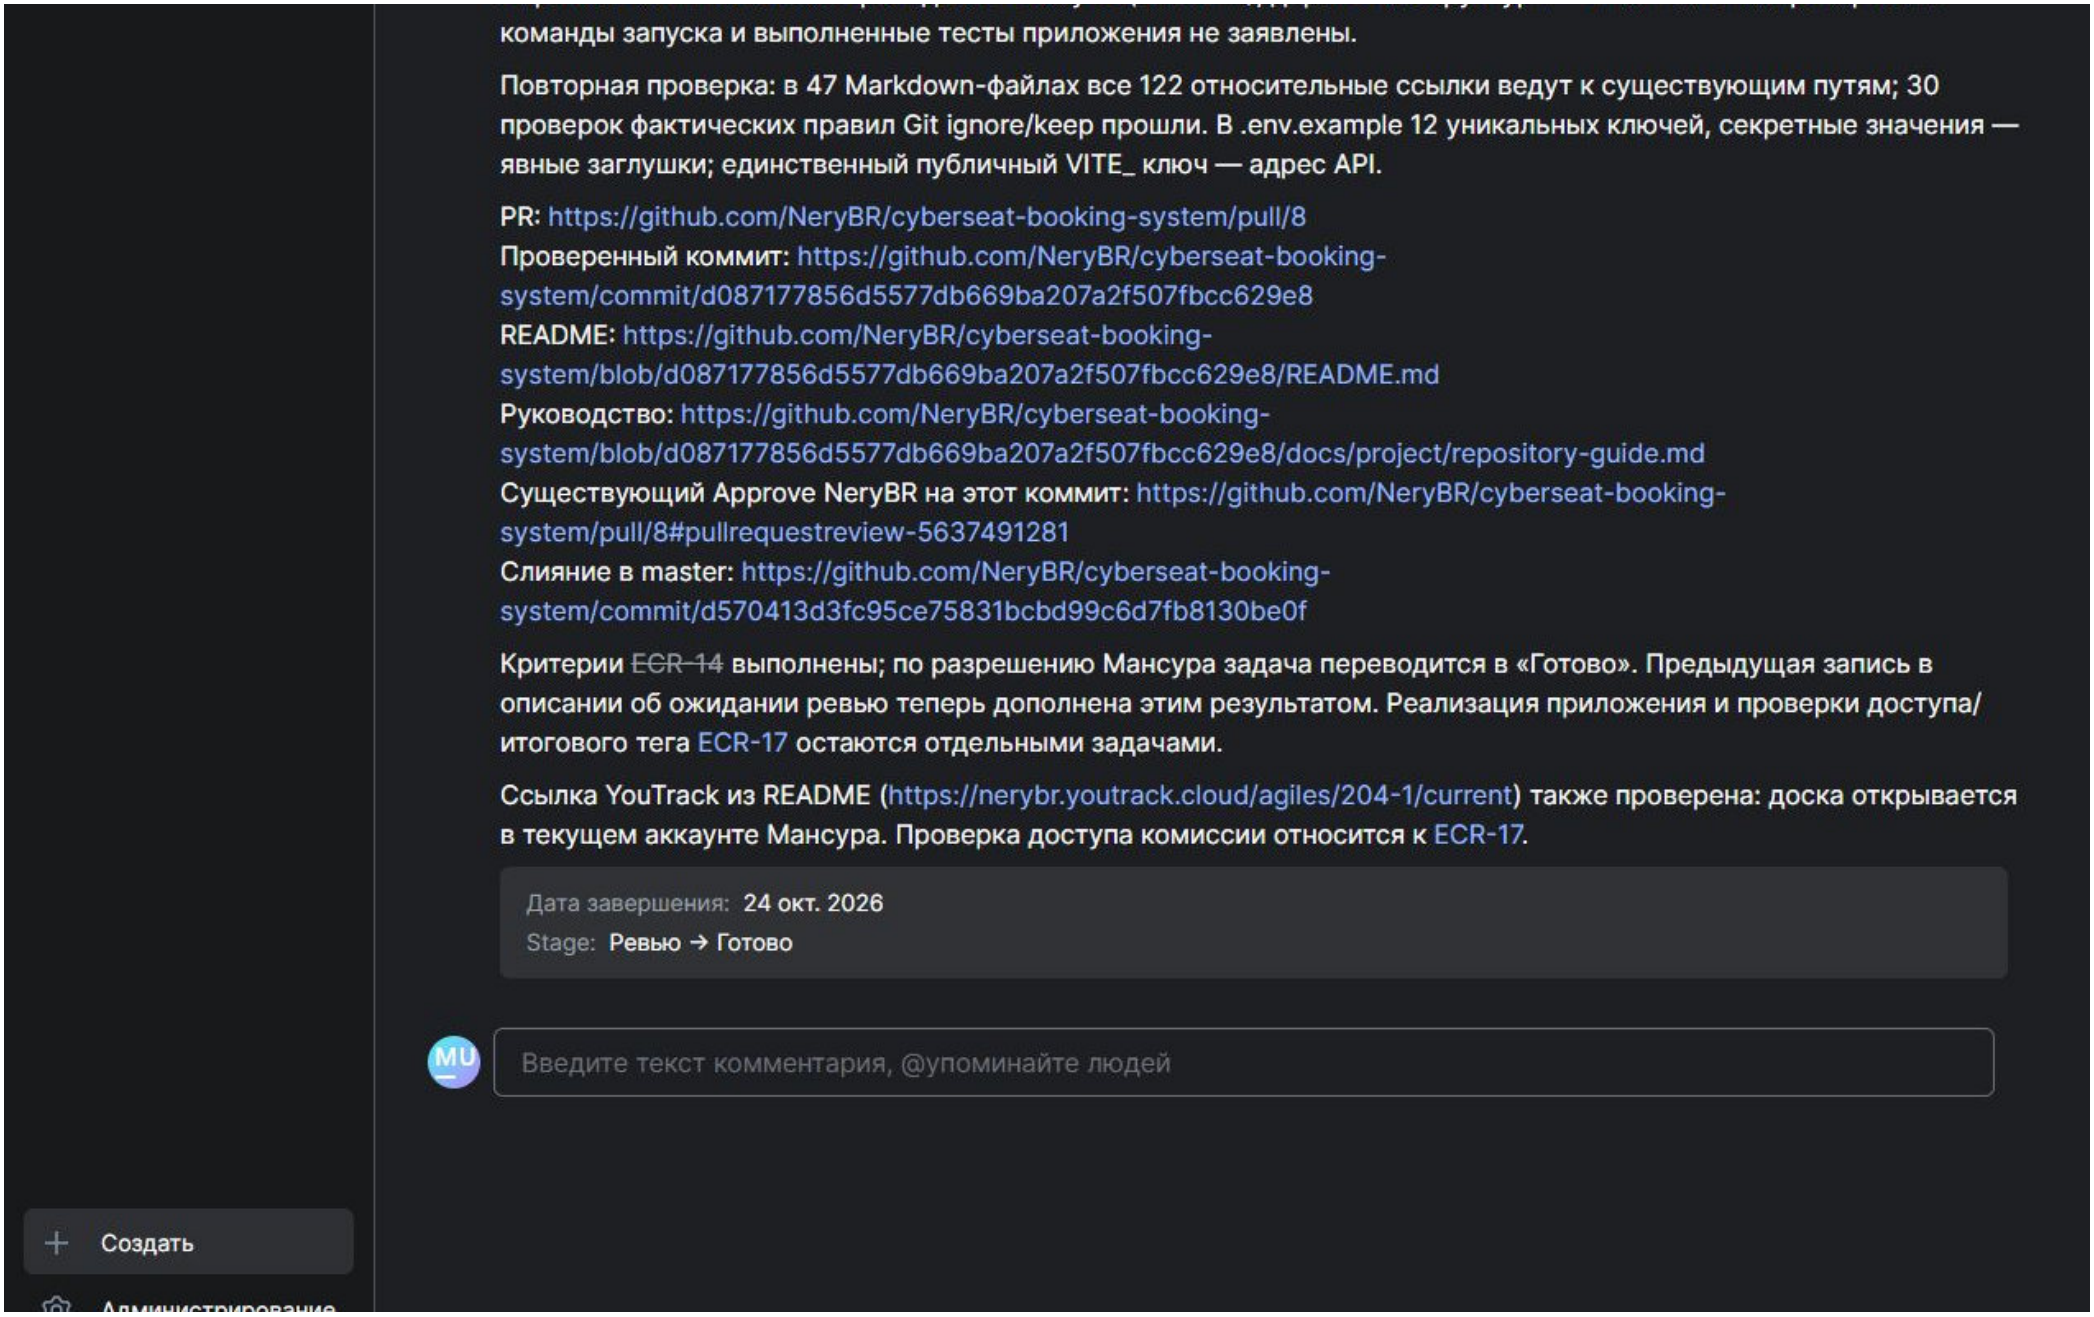
команды запуска и выполненные тесты приложения не заявлены.
Повторная проверка: в 47 Markdown-файлах все 122 относительные ссылки ведут к существующим путям; 30 проверок фактических правил Git ignore/keep прошли. В .env.example 12 уникальных ключей, секретные значения — явные заглушки; единственный публичный VITE_ ключ — адрес API.
PR: https://github.com/NeryBR/cyberseat-booking-system/pull/8
Проверенный коммит: https://github.com/NeryBR/cyberseat-booking-system/commit/d087177856d5577db669ba207a2f507fbcc629e8
README: https://github.com/NeryBR/cyberseat-booking-system/blob/d087177856d5577db669ba207a2f507fbcc629e8/README.md
Руководство: https://github.com/NeryBR/cyberseat-booking-system/blob/d087177856d5577db669ba207a2f507fbcc629e8/docs/project/repository-guide.md
Существующий Approve NeryBR на этот коммит: https://github.com/NeryBR/cyberseat-booking-system/pull/8#pullrequestreview-5637491281
Слияние в master: https://github.com/NeryBR/cyberseat-booking-system/commit/d570413d3fc95ce75831bcbd99c6d7fb8130be0f
Критерии ECR-14 выполнены; по разрешению Мансура задача переводится в «Готово». Предыдущая запись в описании об ожидании ревью теперь дополнена этим результатом. Реализация приложения и проверки доступа/итогового тега ECR-17 остаются отдельными задачами.
Ссылка YouTrack из README (https://nerybr.youtrack.cloud/agiles/204-1/current) также проверена: доска открывается в текущем аккаунте Мансура. Проверка доступа комиссии относится к ECR-17.
Дата завершения: 24 окт. 2026
Stage: Ревью → Готово
MU
Введите текст комментария, @упоминайте людей
Создать
Администрирование


ECR-14 - criteria, result links and review evidence


Original YouTrack screenshot | Part 5/5 | https://nerybr.youtrack.cloud/issue/ECR-14



ECR-16 - criteria, result links and review evidence

Original YouTrack screenshot | Part 1/5 | https://nerybr.youtrack.cloud/issue/ECR-16

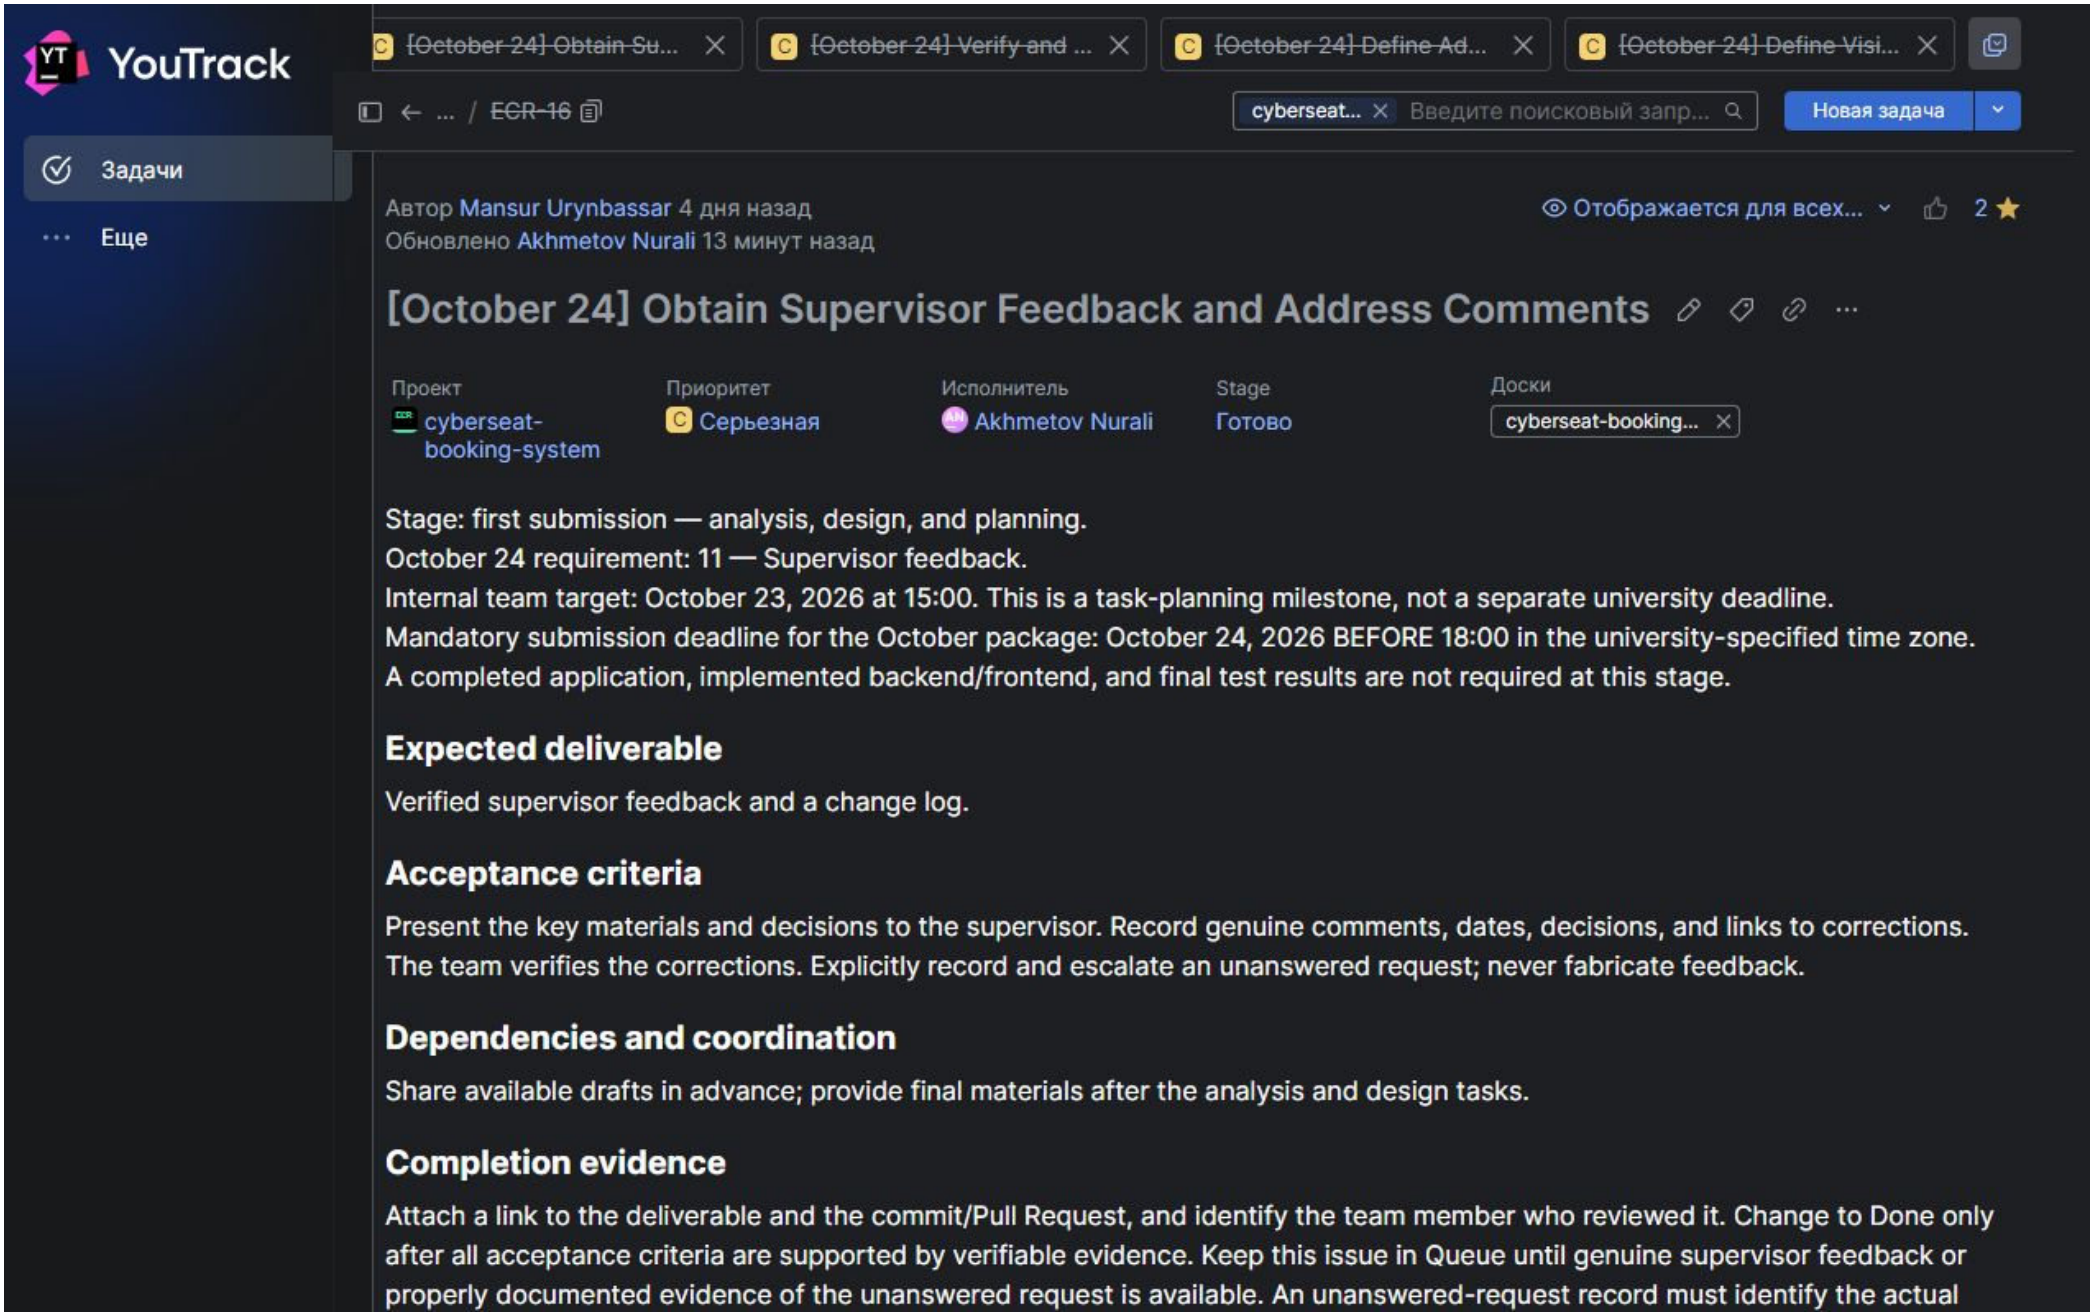

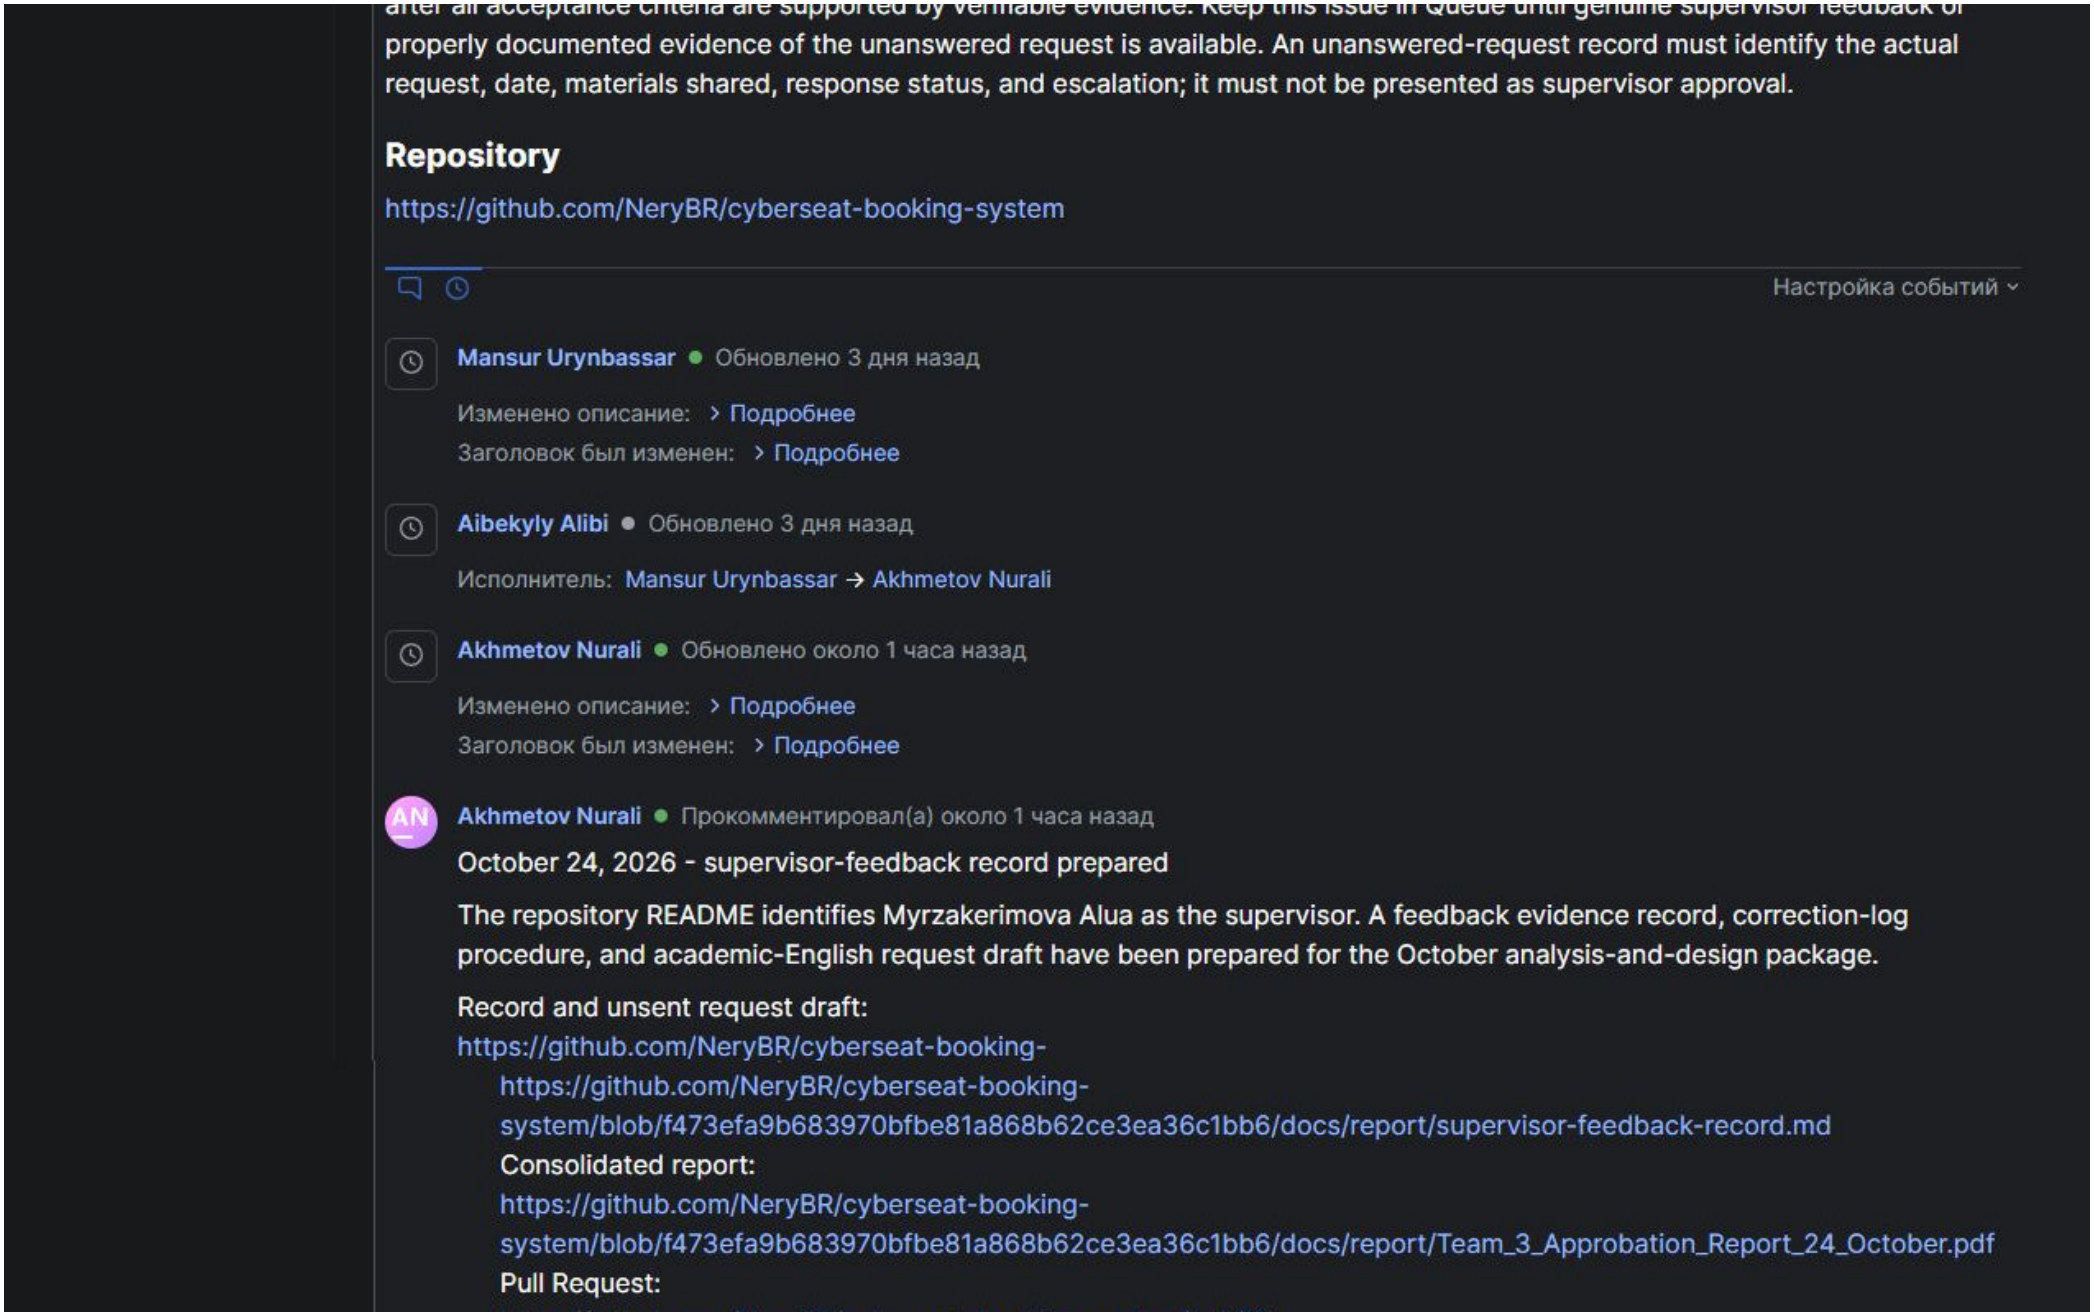
after all acceptance criteria are supported by verifiable evidence. Keep this issue in Queue until genuine supervisor feedback or
properly documented evidence of the unanswered request is available. An unanswered-request record must identify the actual request, date, materials shared, response status, and escalation; it must not be presented as supervisor approval.
Repository
https://github.com/NeryBR/cyberseat-booking-system
Настройка событий
Mansur Urynbassar • Обновлено 3 дня назад
Изменено описание: › Подробнее
Заголовок был изменен: › Подробнее
Aibekyly Alibi • Обновлено 3 дня назад
Исполнитель: Mansur Urynbassar → Akhmetov Nurali
Akhmetov Nurali • Обновлено около 1 часа назад
Изменено описание: › Подробнее
Заголовок был изменен: › Подробнее
AN
Akhmetov Nurali • Прокомментировал(а) около 1 часа назад
October 24, 2026 - supervisor-feedback record prepared
The repository README identifies Myrzakerimova Alua as the supervisor. A feedback evidence record, correction-log procedure, and academic-English request draft have been prepared for the October analysis-and-design package.
Record and unsent request draft:
https://github.com/NeryBR/cyberseat-booking-
https://github.com/NeryBR/cyberseat-booking-system/blob/f473efa9b683970bfbe81a868b62ce3ea36c1bb6/docs/report/supervisor-feedback-record.md
Consolidated report:
https://github.com/NeryBR/cyberseat-booking-system/blob/f473efa9b683970bfbe81a868b62ce3ea36c1bb6/docs/report/Team_3_Approbation_Report_24_October.pdf
Pull Request:

Pull Request:
https://github.com/NeryBR/cyberseat-booking-system/pull/13
Commit:
https://github.com/NeryBR/cyberseat-booking-system/commit/f473efa9b683970bfbe81a868b62ce3ea36c1bb6

Evidence status: no dated request, delivery reference, genuine supervisor response, or escalation record was found in the inspected repository or this issue's activity. This describes unavailable evidence, not proof that no communication occurred elsewhere. No supervisor feedback, approval, or feedback-driven correction is invented.

The request draft has not been sent. To complete the record, supply the actual recipient/channel, sending date, materials shared and request reference; then attach the real response and correction evidence, or document the actual unanswered request and escalation. Team verification of any corrections must identify the participant and exact revision.

Status: Queue retained until genuine feedback or properly documented evidence of the unanswered request and its handling is available. The report and review records concern analysis and design; final software implementation and application testing remain future work.

AN **Akhmetov Nurali** • Прокомментировал(а) 13 минут назад


Final completion evidence - October 24, 2026

Supervisor: Myrzakerimova Alua.
Channel: WhatsApp.
Date received: October 24, 2026, explicitly confirmed by Nurali. The image shows request 17:54 and reply 17:55; the image does not show a calendar date or time zone.

Verbatim supervisor reply:
Здравствуй Нурали! Да я проверила ваши работы в ютреке и пдф и гитхаб, мне все понравилось, не вижу никаких недочетов, так что я считаю что замечаний нет.

English translation:
Hello Nurali! Yes, I checked your work in YouTrack, the PDF, and GitHub. I liked everything, I do not see any shortcomings, so I consider that there are no comments.

Disposition: the supervisor reported no shortcomings or comments; no substantive correction was requested. The supplied reply and metadata are now recorded in the report and checklist. The original conversation image is retained separately, SHA-256 989c31282072dc4711cd3f82a23d8dc47e6f552effe1376488ac7d50af9ef50c. It is not embedded in the report or published in the repository. The respondent identity, date, and channel are attributed to Nurali's confirmation.

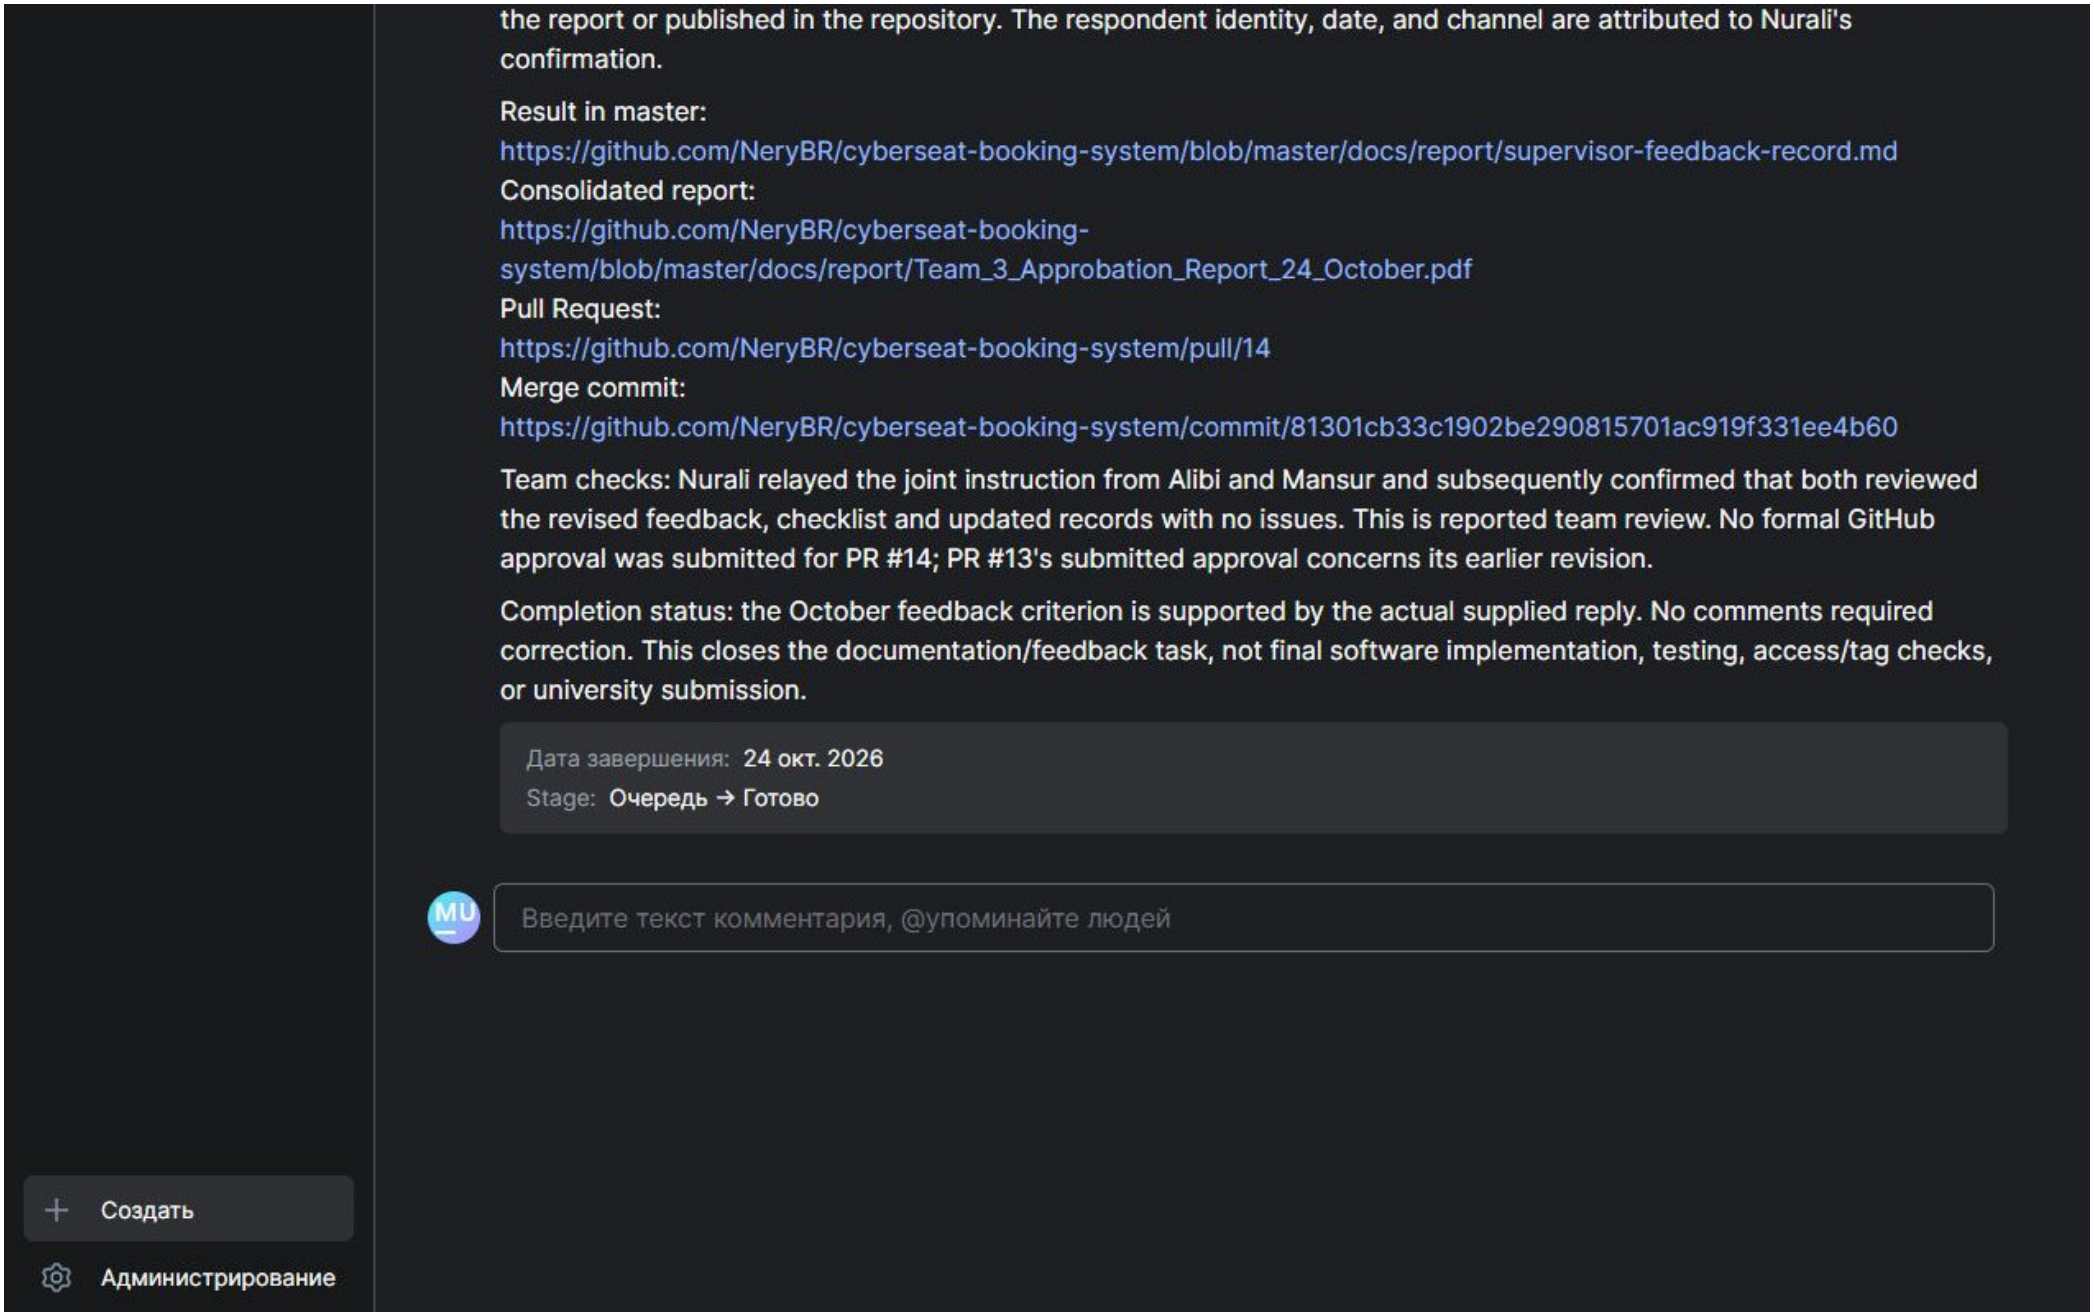
the report or published in the repository. The respondent identity, date, and channel are attributed to Nurali's confirmation.
Result in master:
https://github.com/NeryBR/cyberseat-booking-system/blob/master/docs/report/supervisor-feedback-record.md
Consolidated report:
https://github.com/NeryBR/cyberseat-booking-system/blob/master/docs/report/Team_3_Approbation_Report_24_October.pdf
Pull Request:
https://github.com/NeryBR/cyberseat-booking-system/pull/14
Merge commit:
https://github.com/NeryBR/cyberseat-booking-system/commit/81301cb33c1902be290815701ac919f331ee4b60
Team checks: Nurali relayed the joint instruction from Alibi and Mansur and subsequently confirmed that both reviewed the revised feedback, checklist and updated records with no issues. This is reported team review. No formal GitHub approval was submitted for PR #14; PR #13's submitted approval concerns its earlier revision.
Completion status: the October feedback criterion is supported by the actual supplied reply. No comments required correction. This closes the documentation/feedback task, not final software implementation, testing, access/tag checks, or university submission.
Дата завершения: 24 окт. 2026
Stage: Очередь → Готово
MU
Введите текст комментария, @упоминайте людей
Создать
Администрирование


ECR-16 - criteria, result links and review evidence


Original YouTrack screenshot | Part 5/5 | https://nerybr.youtrack.cloud/issue/ECR-16




ECR-18 - criteria, result links and review evidence

Original YouTrack screenshot | Part 1/5 | https://nerybr.youtrack.cloud/issue/ECR-18

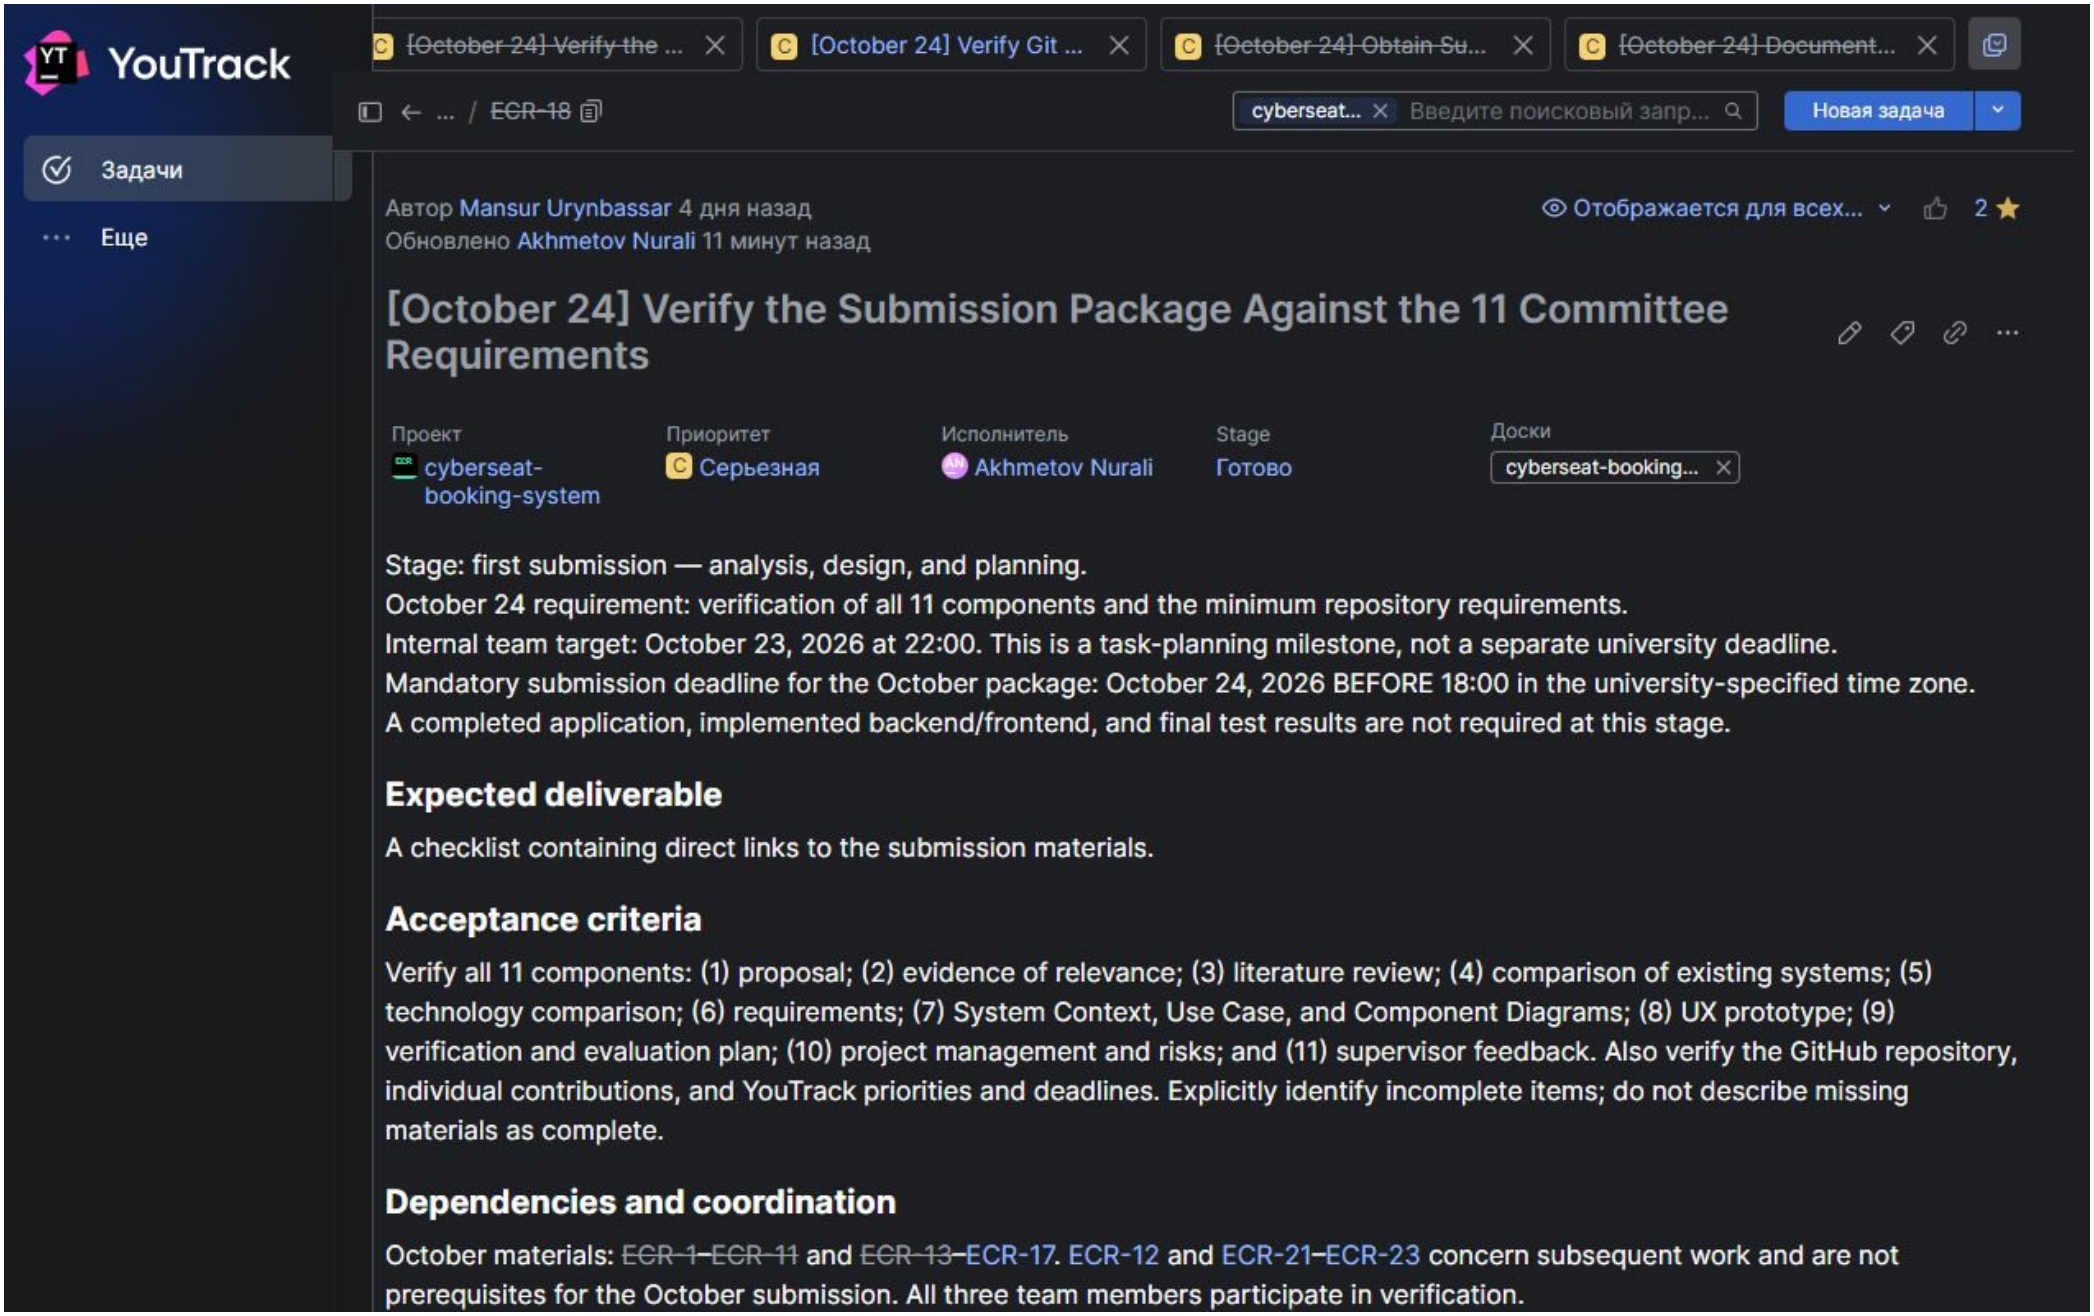

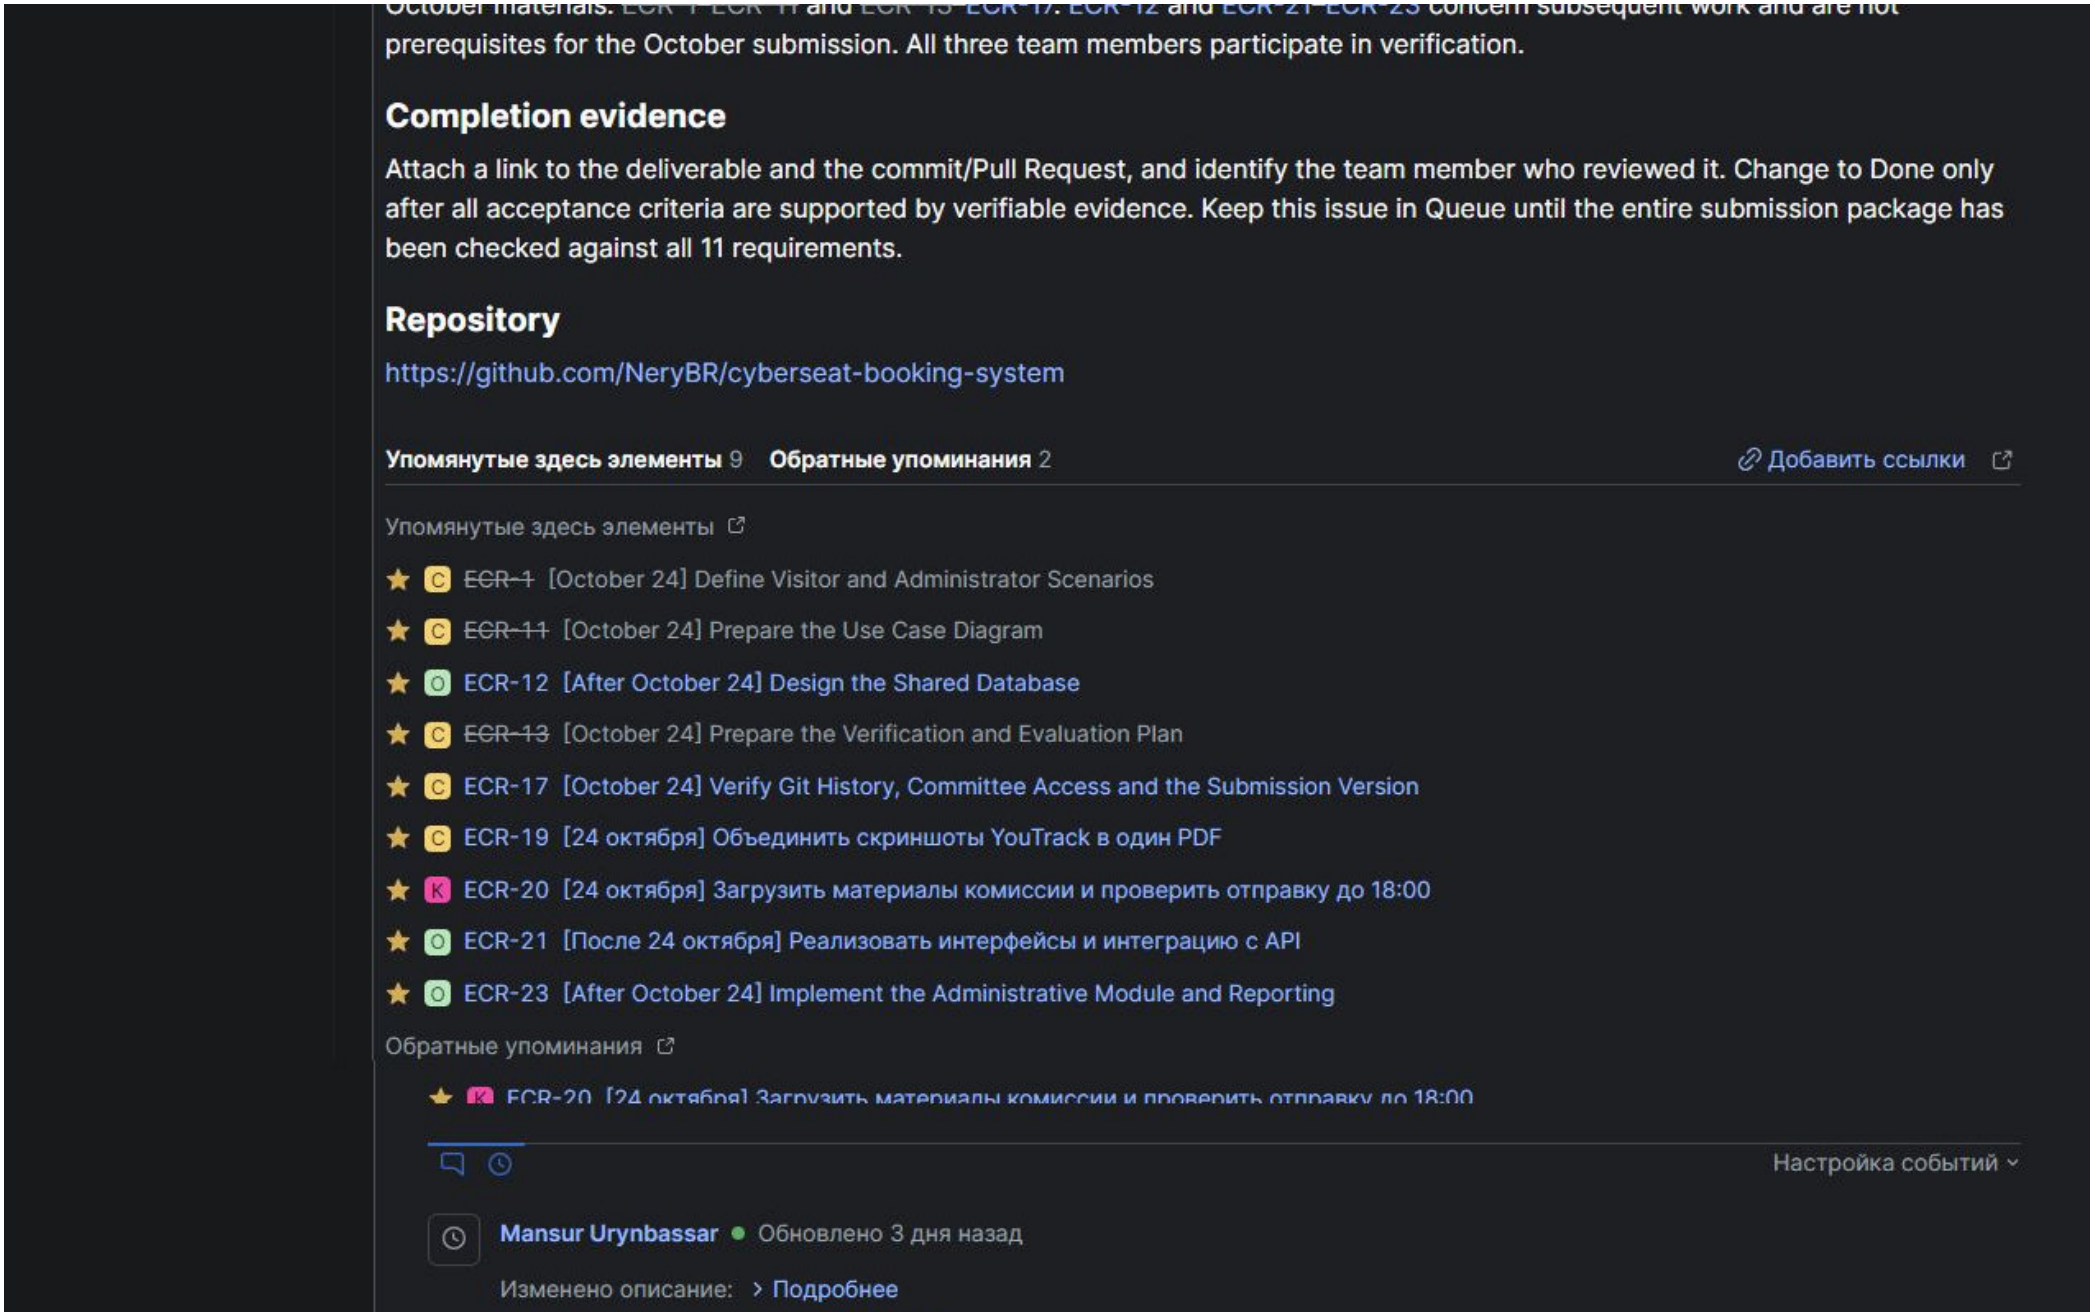
prerequisites for the October submission. All three team members participate in verification.
Completion evidence
Attach a link to the deliverable and the commit/Pull Request, and identify the team member who reviewed it. Change to Done only after all acceptance criteria are supported by verifiable evidence. Keep this issue in Queue until the entire submission package has been checked against all 11 requirements.
Repository
https://github.com/NeryBR/cyberseat-booking-system
Упомянутые здесь элементы 9
Обратные упоминания 2
Добавить ссылки
Упомянутые здесь элементы
ECR-1 [October 24] Define Visitor and Administrator Scenarios
ECR-11 [October 24] Prepare the Use Case Diagram
ECR-12 [After October 24] Design the Shared Database
ECR-13 [October 24] Prepare the Verification and Evaluation Plan
ECR-17 [October 24] Verify Git History, Committee Access and the Submission Version
ECR-19 [24 октября] Объединить скриншоты YouTrack в один PDF
ECR-20 [24 октября] Загрузить материалы комиссии и проверить отправку до 18:00
ECR-21 [После 24 октября] Реализовать интерфейсы и интеграцию с API
ECR-23 [After October 24] Implement the Administrative Module and Reporting
Обратные упоминания
Настройка событий
Mansur Urynbassar
Обновлено 3 дня назад
Изменено описание:
Подробнее

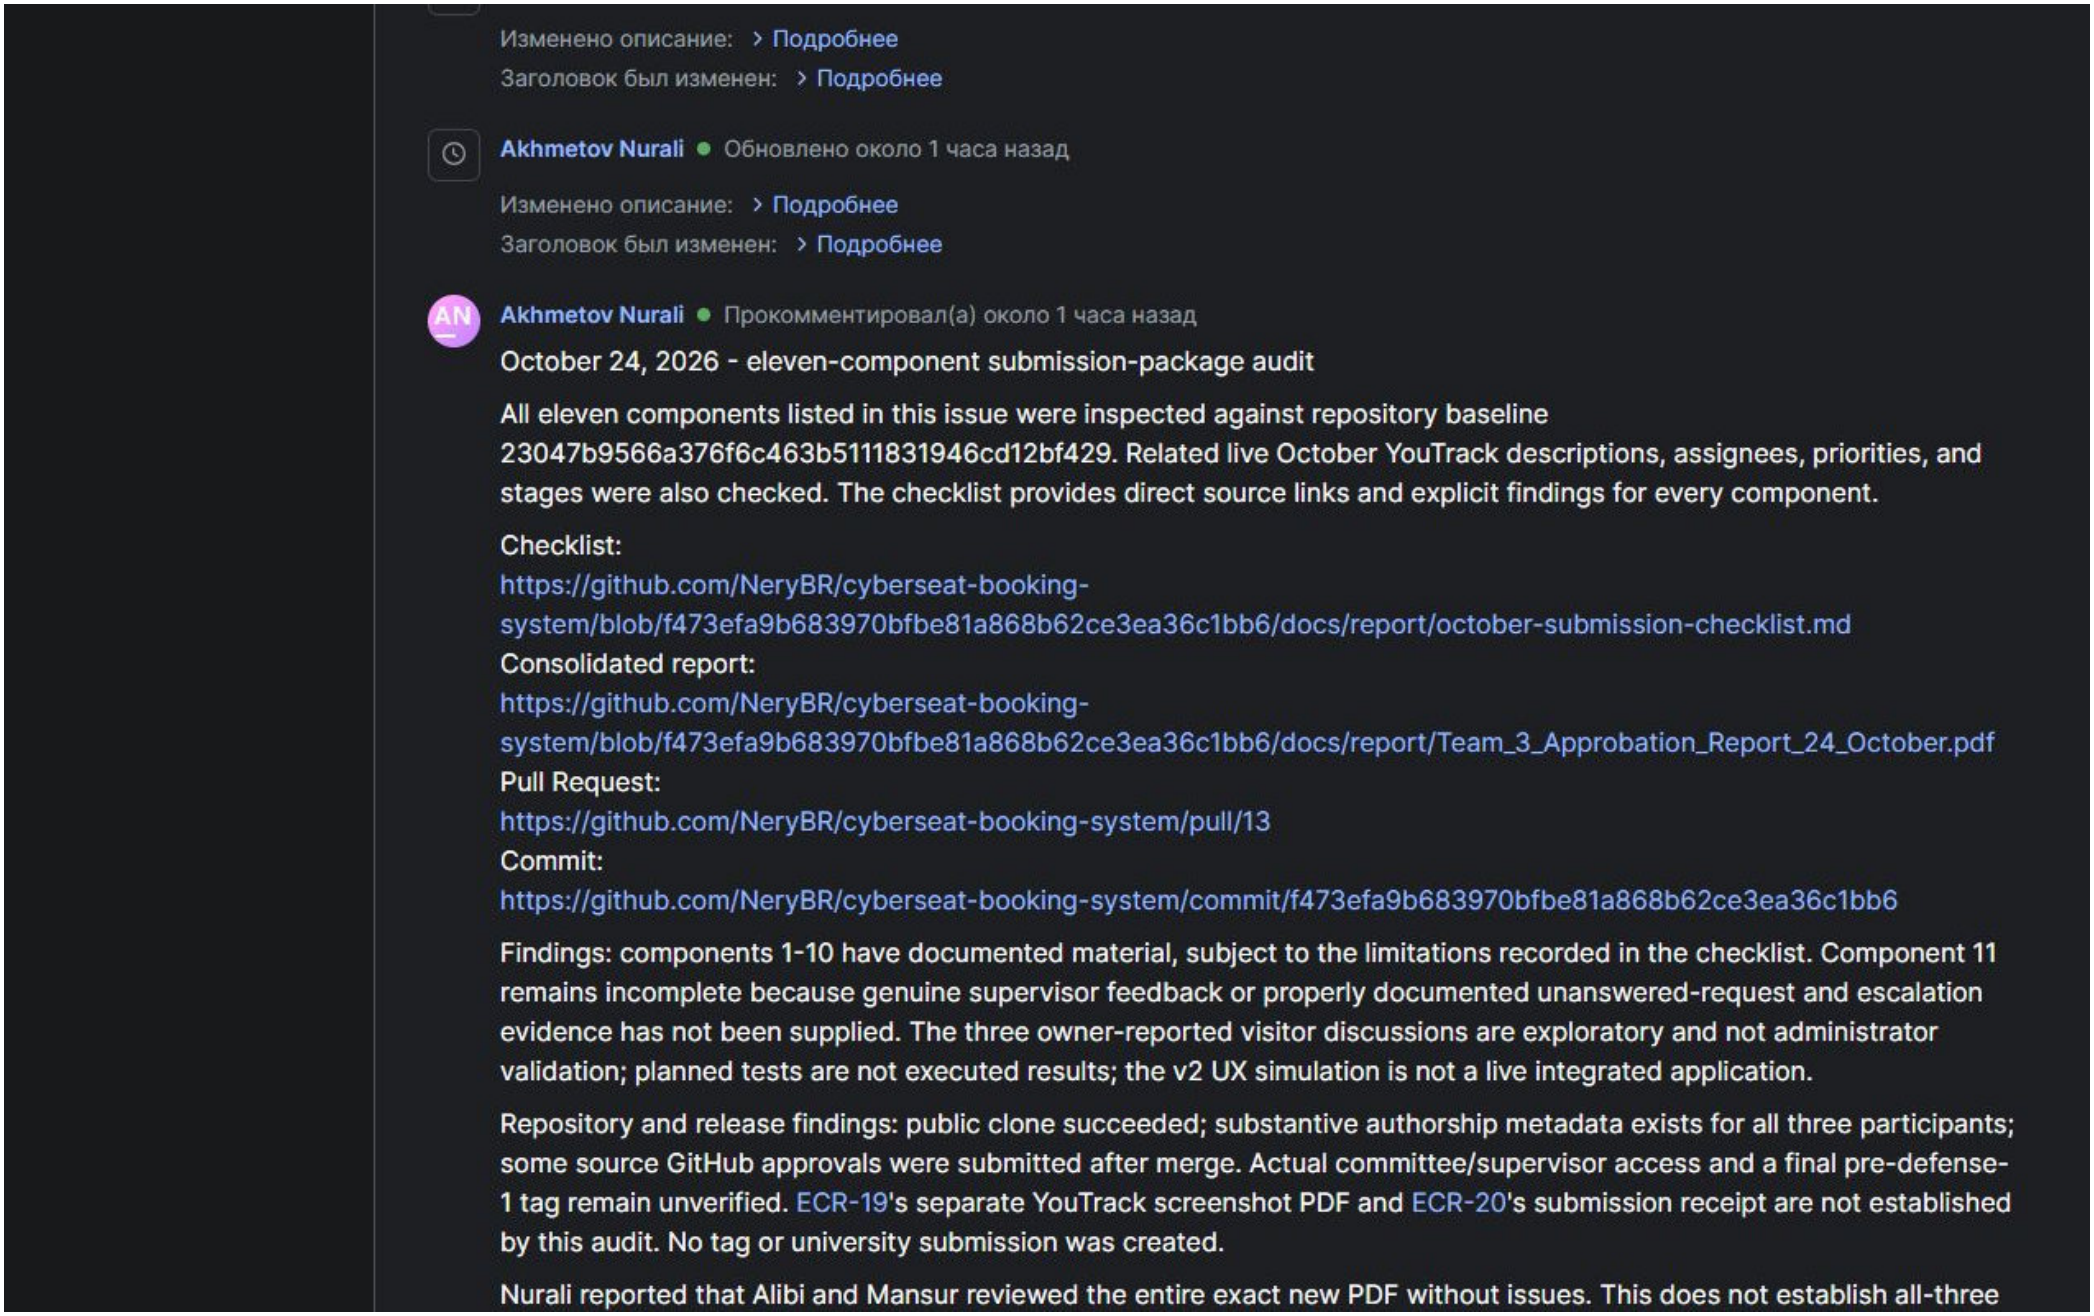

Изменено описание: › Подробнее
Заголовок был изменен: › Подробнее

Akhmetov Nurali • Обновлено около 1 часа назад

Изменено описание: › Подробнее
Заголовок был изменен: › Подробнее

Akhmetov Nurali • Прокомментировал(а) около 1 часа назад

October 24, 2026 - eleven-component submission-package audit

All eleven components listed in this issue were inspected against repository baseline 23047b9566a376f6c463b5111831946cd12bf429. Related live October YouTrack descriptions, assignees, priorities, and stages were also checked. The checklist provides direct source links and explicit findings for every component.

Checklist:
https://github.com/NeryBR/cyberseat-booking-system/blob/f473efa9b683970bfbe81a868b62ce3ea36c1bb6/docs/report/october-submission-checklist.md
Consolidated report:
https://github.com/NeryBR/cyberseat-booking-system/blob/f473efa9b683970bfbe81a868b62ce3ea36c1bb6/docs/report/Team_3_Approbation_Report_24_October.pdf
Pull Request:
https://github.com/NeryBR/cyberseat-booking-system/pull/13
Commit:
https://github.com/NeryBR/cyberseat-booking-system/commit/f473efa9b683970bfbe81a868b62ce3ea36c1bb6

Findings: components 1-10 have documented material, subject to the limitations recorded in the checklist. Component 11 remains incomplete because genuine supervisor feedback or properly documented unanswered-request and escalation evidence has not been supplied. The three owner-reported visitor discussions are exploratory and not administrator validation; planned tests are not executed results; the v2 UX simulation is not a live integrated application.

Repository and release findings: public clone succeeded; substantive authorship metadata exists for all three participants; some source GitHub approvals were submitted after merge. Actual committee/supervisor access and a final pre-defense-1 tag remain unverified. ECR-19's separate YouTrack screenshot PDF and ECR-20's submission receipt are not established by this audit. No tag or university submission was created.

Nurali reported that Alibi and Mansur reviewed the entire exact new PDF without issues. This does not establish all-three

Nurali reported that Alibi and Mansur reviewed the entire exact new PDF without issues. This does not establish all-three verification of the entire release package and is not a new GitHub approval.

Status: Queue retained. This audit identifies missing evidence; it does not declare the full package complete or the final software implemented.

AN **Akhmetov Nurali** • Прокомментировал(а) 11 минут назад

Final completion evidence - October 24, 2026

All eleven committee components have now been checked and linked, including the actual supervisor reply. Myrzakerimova Alua reported no comments through WhatsApp; Nurali confirmed October 24, 2026, and the supplied image shows 17:55. The checklist now records the feedback as received rather than missing.

Result in master:
https://github.com/NeryBR/cyberseat-booking-system/blob/master/docs/report/october-submission-checklist.md
Supervisor evidence record:
https://github.com/NeryBR/cyberseat-booking-system/blob/master/docs/report/supervisor-feedback-record.md
Consolidated report:
https://github.com/NeryBR/cyberseat-booking-system/blob/master/docs/report/Team_3_Approbation_Report_24_October.pdf
Pull Request:
https://github.com/NeryBR/cyberseat-booking-system/pull/14
Merge commit:
https://github.com/NeryBR/cyberseat-booking-system/commit/81301cb33c1902be290815701ac919f331ee4b60


Acceptance cross-check: proposal; relevance/user evidence; literature; existing systems; technologies; requirements; System Context, Use Case and Component Diagrams; UX prototype; verification/evaluation plan; management/risks; and supervisor feedback all have explicit findings and direct sources. GitHub contribution metadata and the live YouTrack assignees, priorities, stages, and stated deadlines were inspected. Existing limitations remain visible rather than treated as completed work.

Team participation: Nurali coordinates this audit with Codex assistance. He reported Alibi and Mansur's earlier full-document reviews, their joint instruction to incorporate the supervisor reply, and their checks of the updated feedback/checklist records with no issues. No independent account authentication or new formal GitHub approval is inferred. No formal GitHub approval was submitted for PR #14.

Completion status: Done for the eleven-component audit. This does not claim that every release control is complete


ECR-18 - criteria, result links and review evidence


Original YouTrack screenshot | Part 5/5 | https://nerybr.youtrack.cloud/issue/ECR-18

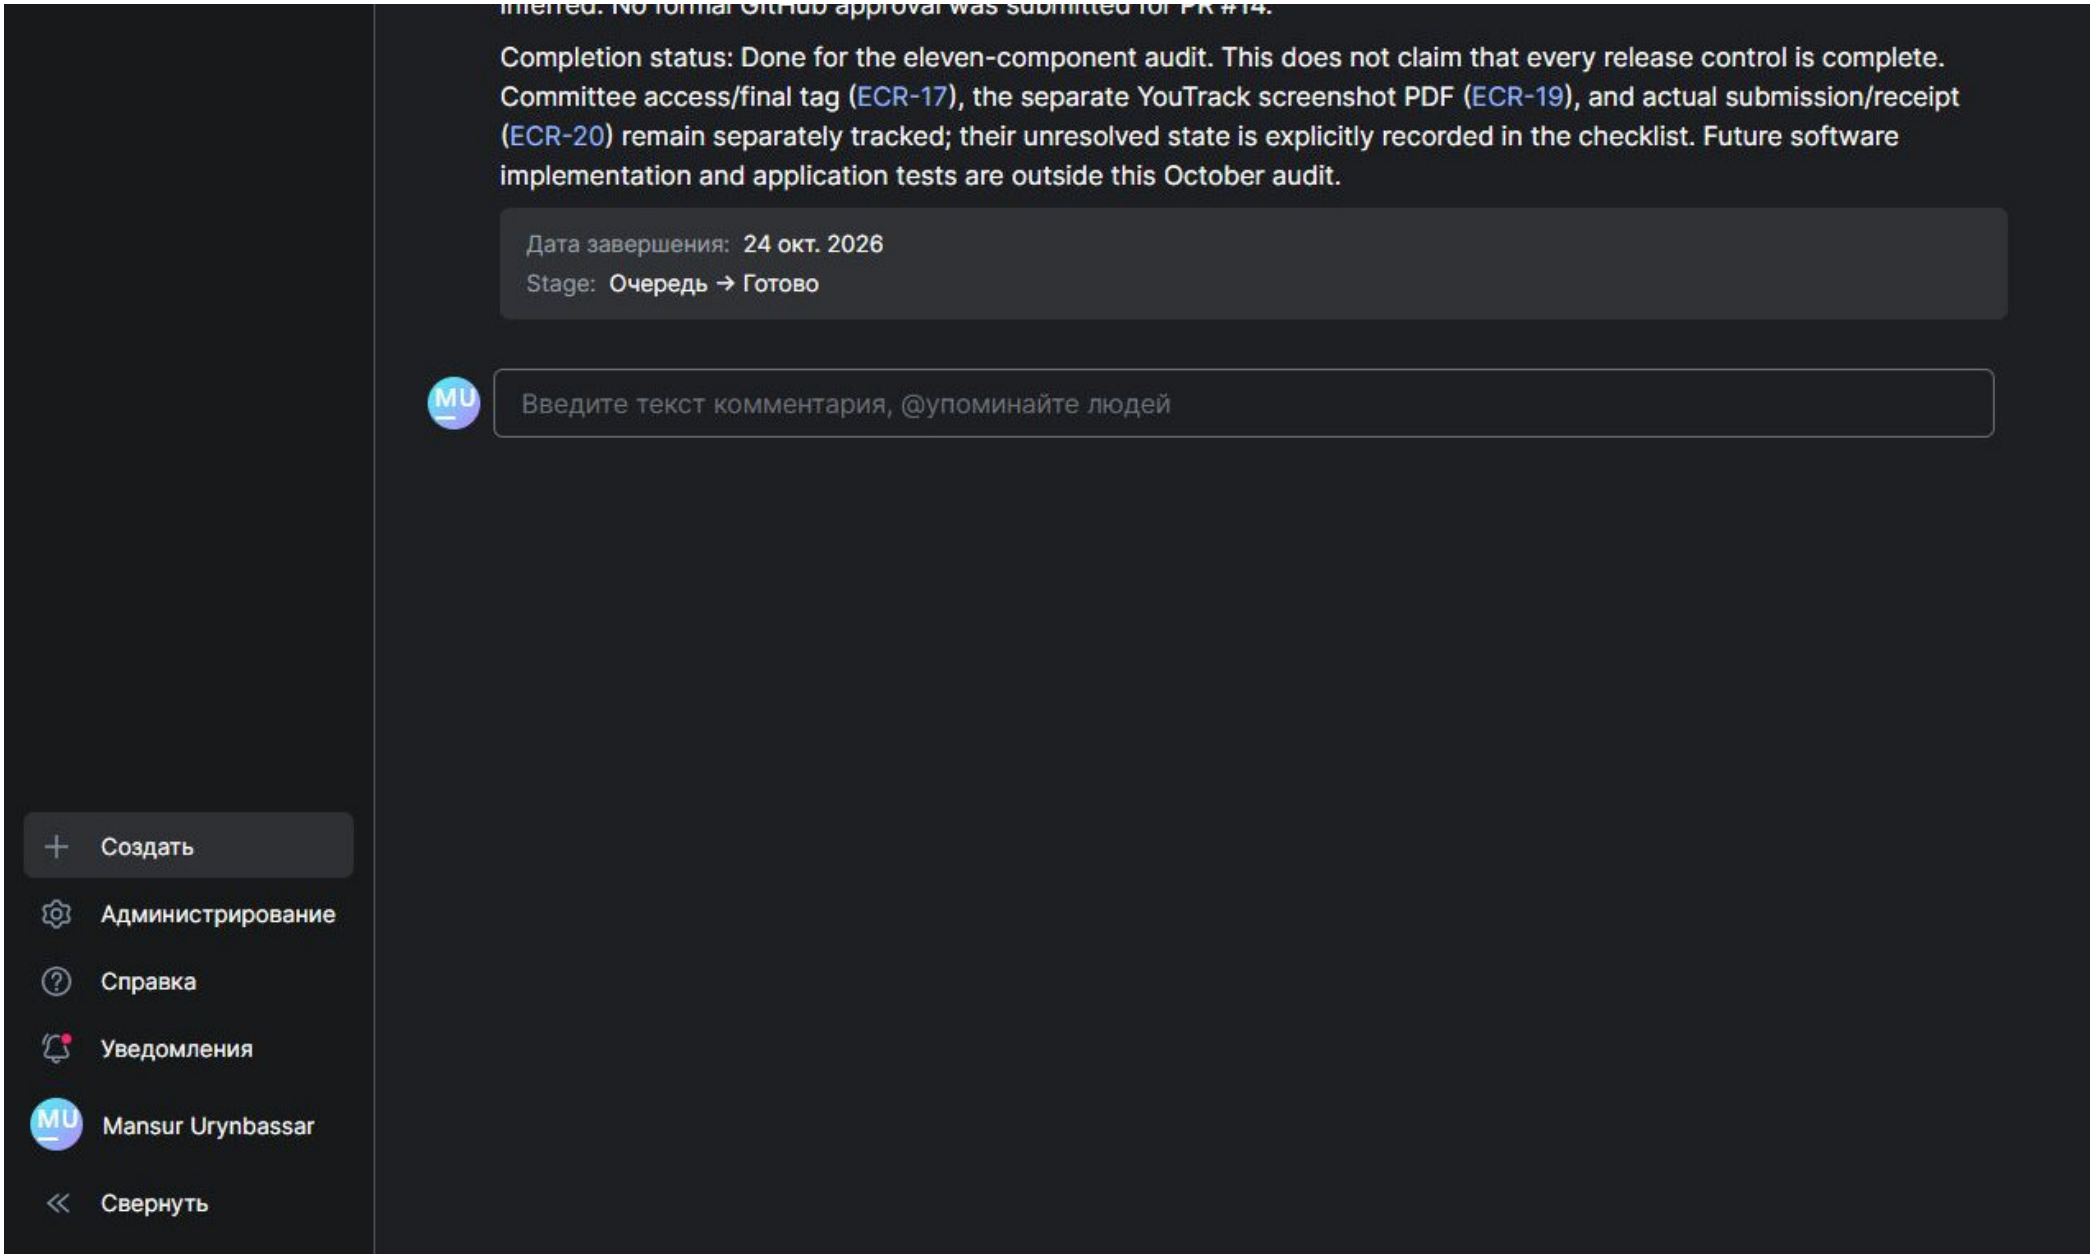

ECR-24 - criteria, result links and review evidence

Original YouTrack screenshot | Part 1/6 | https://nerybr.youtrack.cloud/issue/ECR-24

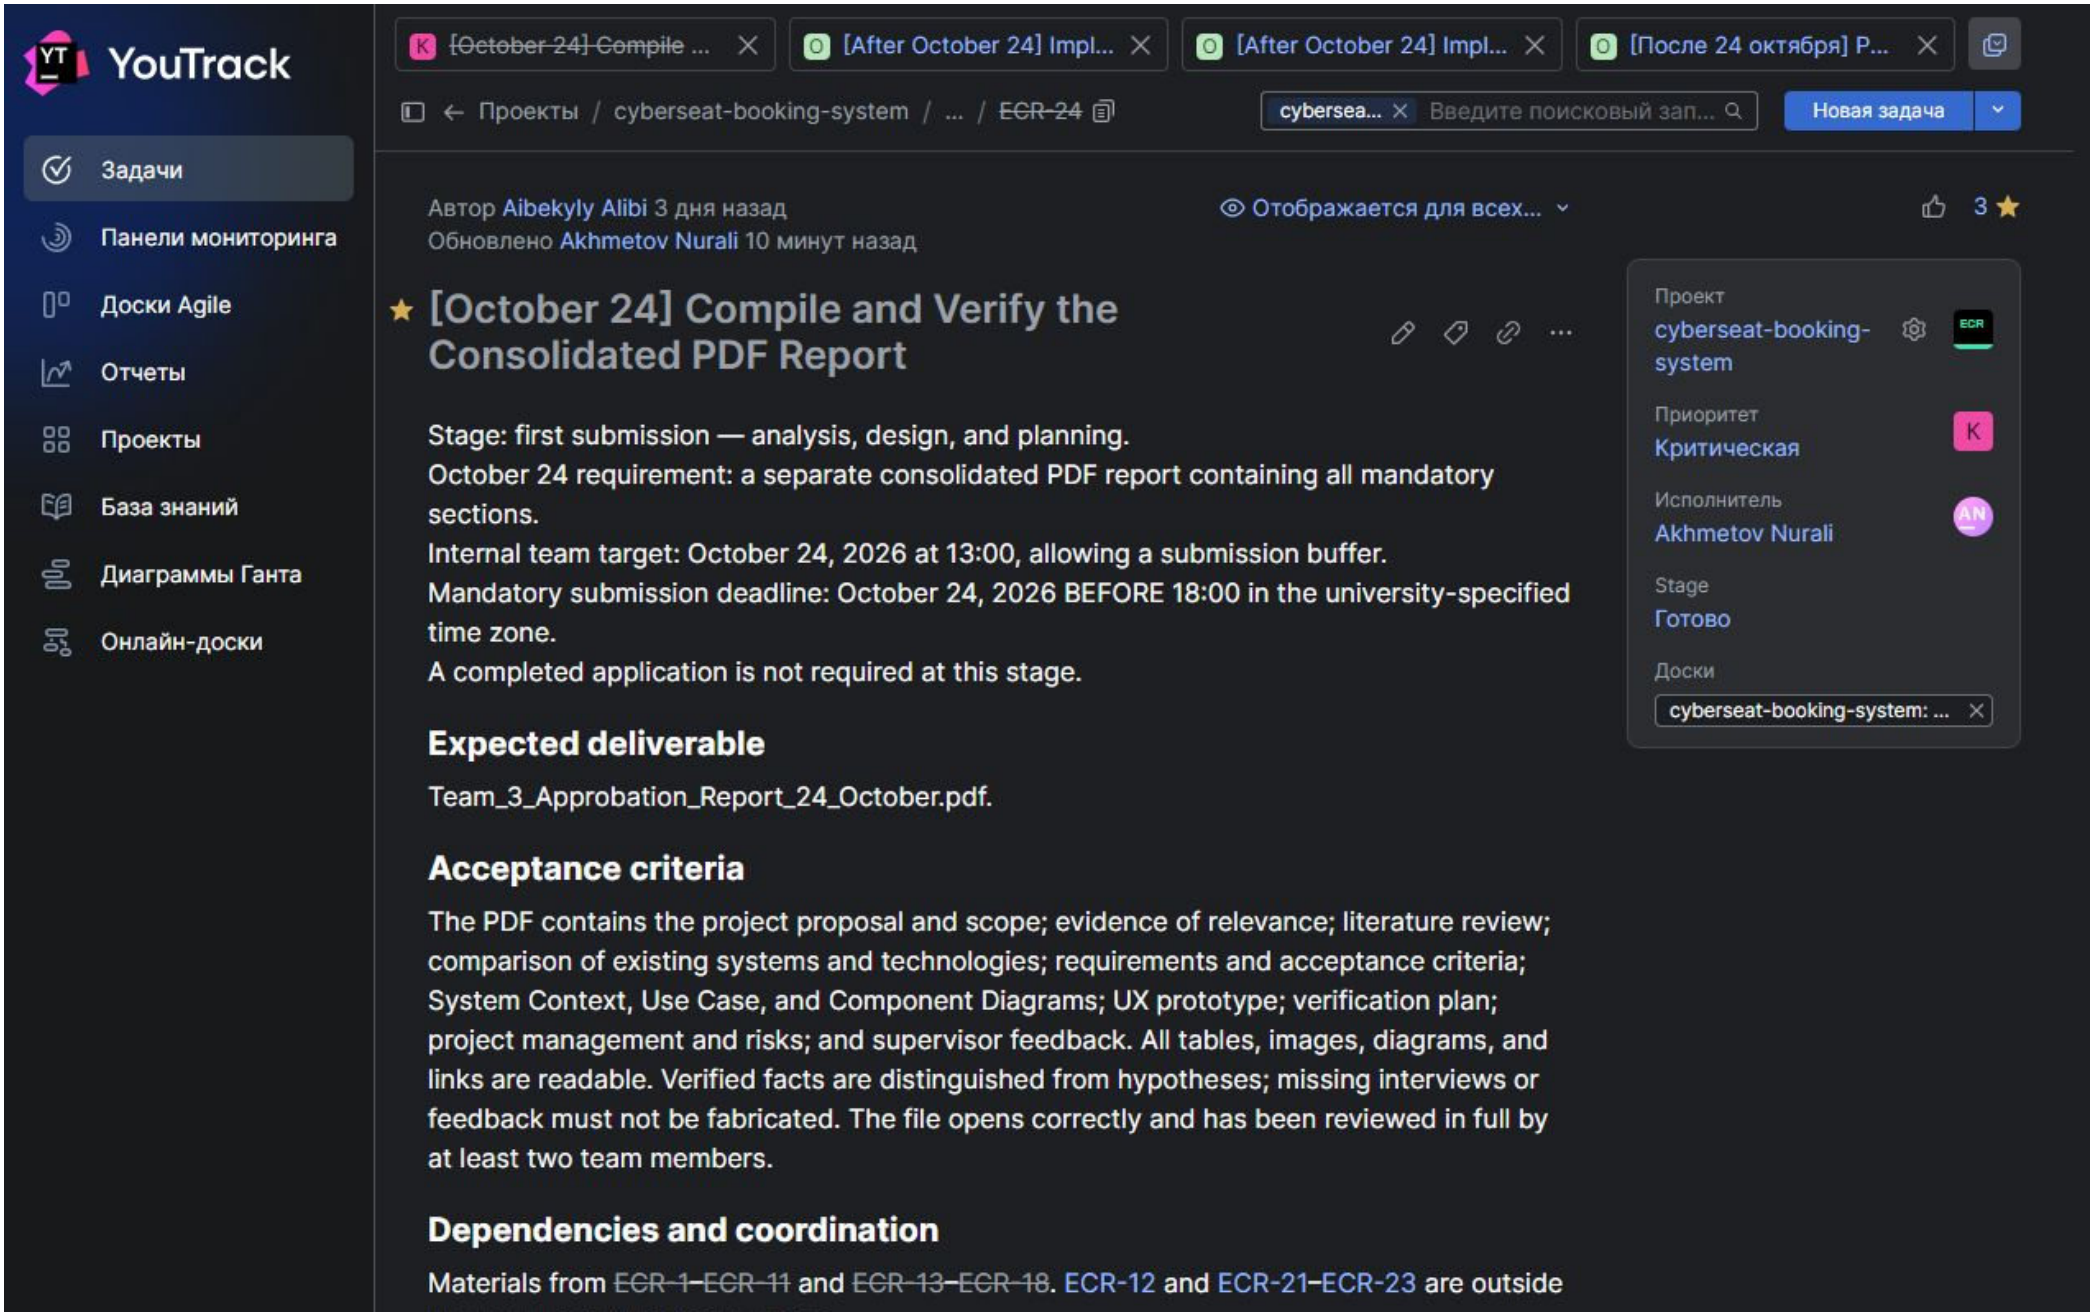

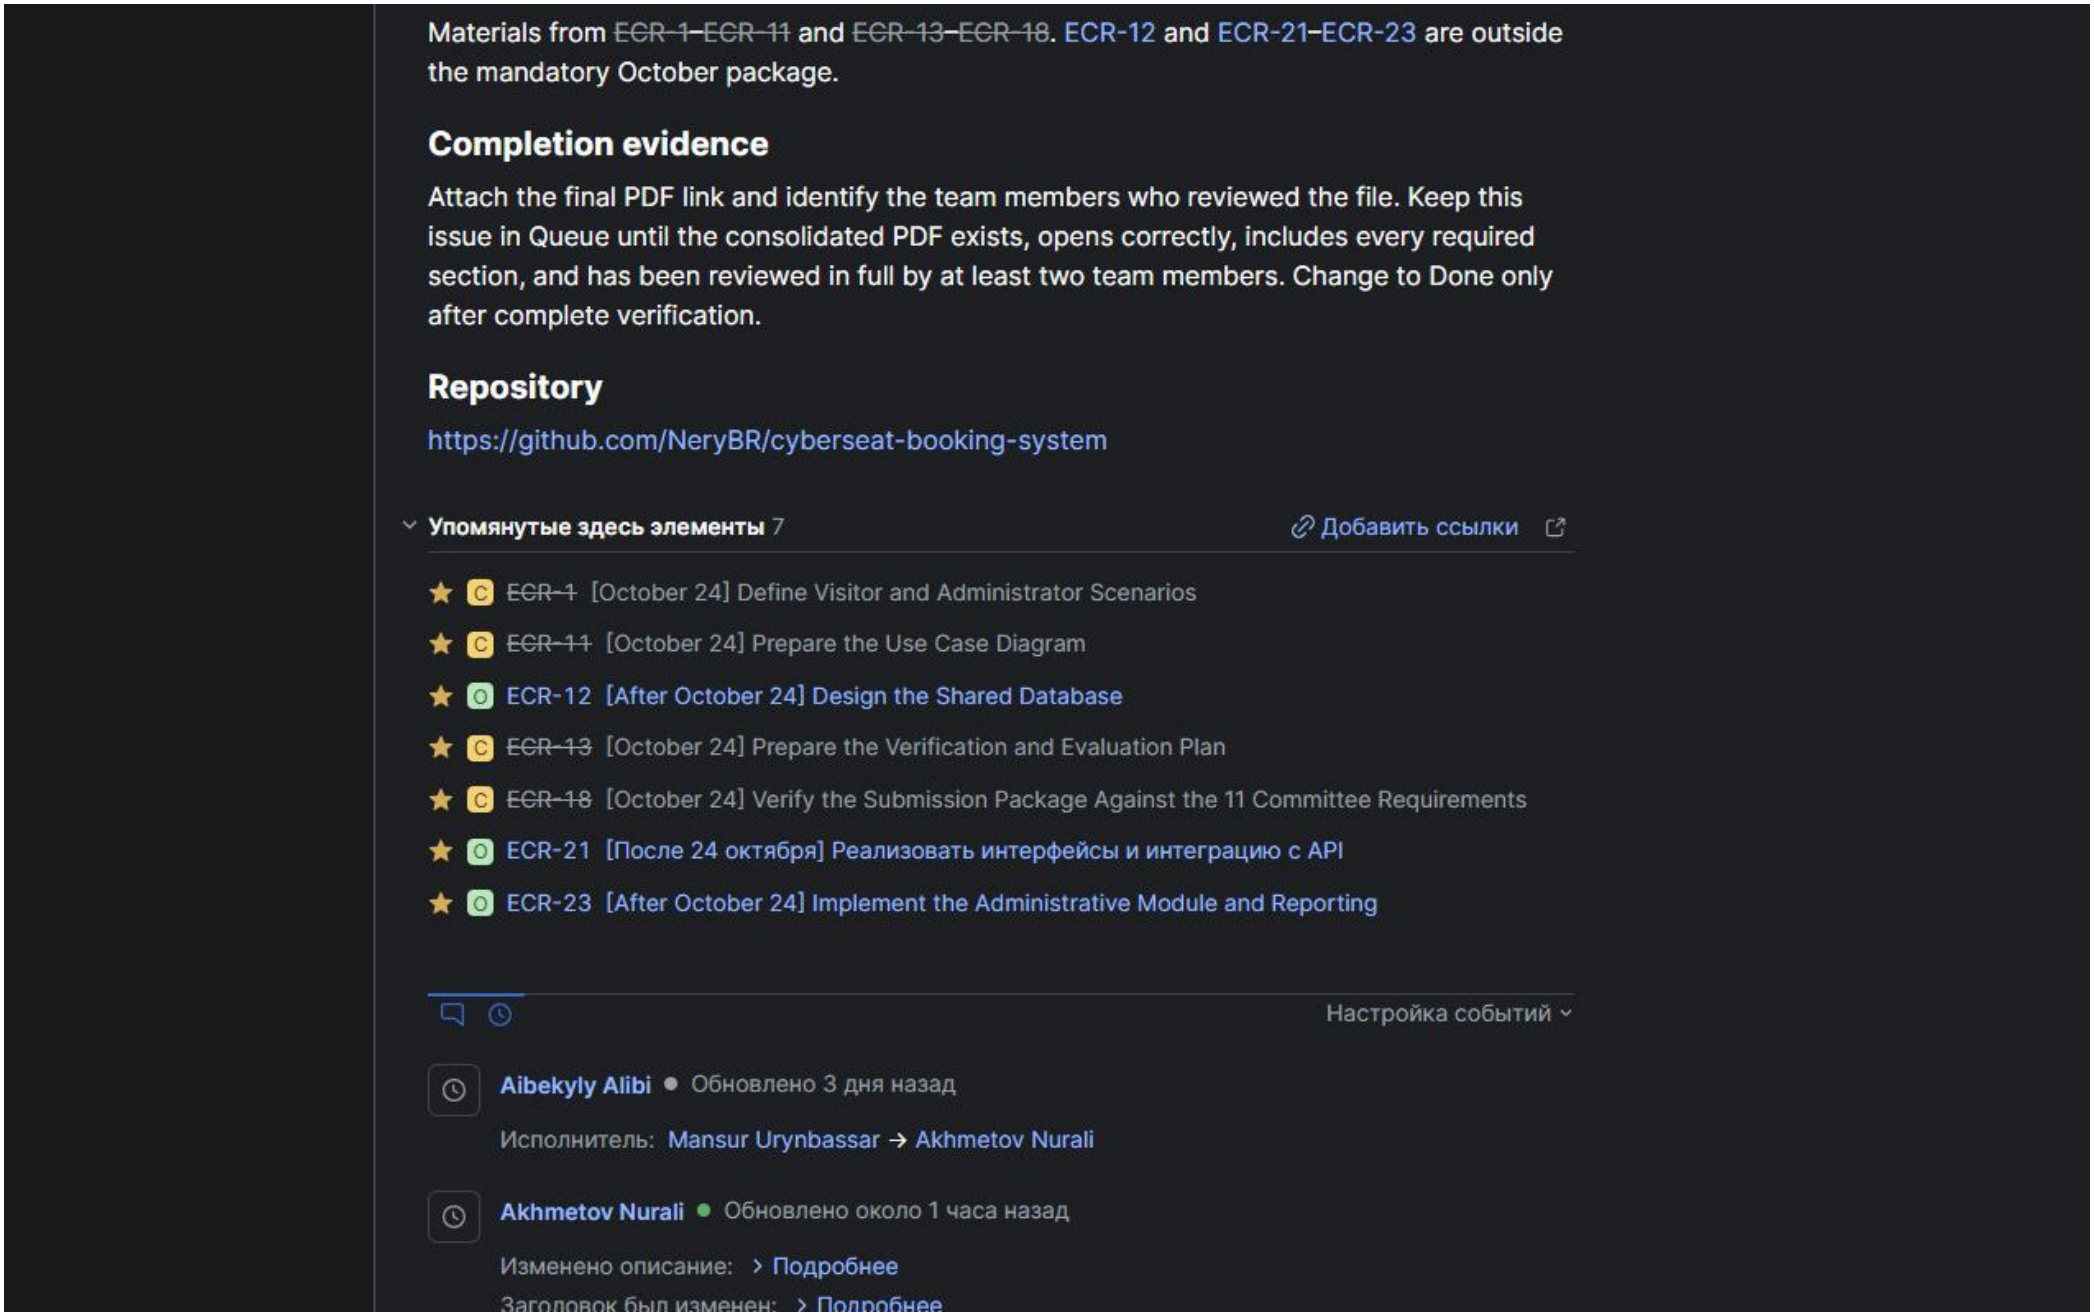
Materials from ~~ECR-1–ECR-11~~ and ~~ECR-13–ECR-18~~. ECR-12 and ECR-21–ECR-23 are outside the mandatory October package.
Completion evidence
Attach the final PDF link and identify the team members who reviewed the file. Keep this issue in Queue until the consolidated PDF exists, opens correctly, includes every required section, and has been reviewed in full by at least two team members. Change to Done only after complete verification.
Repository
https://github.com/NeryBR/cyberseat-booking-system
Упомянутые здесь элементы 7
Добавить ссылки
~~ECR-1~~ [October 24] Define Visitor and Administrator Scenarios
~~ECR-11~~ [October 24] Prepare the Use Case Diagram
ECR-12 [After October 24] Design the Shared Database
~~ECR-13~~ [October 24] Prepare the Verification and Evaluation Plan
~~ECR-18~~ [October 24] Verify the Submission Package Against the 11 Committee Requirements
ECR-21 [После 24 октября] Реализовать интерфейсы и интеграцию с API
ECR-23 [After October 24] Implement the Administrative Module and Reporting
Настройка событий
Aibekyly Alibi Обновлено 3 дня назад
Исполнитель: Mansur Urynbassar → Akhmetov Nurali
Akhmetov Nurali Обновлено около 1 часа назад
Изменено описание: Подробнее
Заголовок был изменен: Подробнее

Изменено описание: › Подробнее

Заголовок был изменен: › Подробнее

Akhmetov Nurali ● Прокомментировал(а) около 1 часа назад

October 24, 2026 - consolidated report compilation and verification

The consolidated English analysis-and-design report has been compiled from repository baseline 23047b9566a376f6c463b5111831946cd12bf429. It contains 121 pages, all three vector diagrams, requirements and acceptance criteria, research, the UX documentation and twelve explicitly dated historical screen plates, the verification plan, project management, risks, and a supervisor-feedback status section.

Report:
https://github.com/NeryBR/cyberseat-booking-system/blob/f473efa9b683970bfbe81a868b62ce3ea36c1bb6/docs/report/Team_3_Approbation_Report_24_October.pdf
Verification record:
https://github.com/NeryBR/cyberseat-booking-system/blob/f473efa9b683970bfbe81a868b62ce3ea36c1bb6/docs/report/consolidated-report-verification.md
Manifest:
https://github.com/NeryBR/cyberseat-booking-system/blob/f473efa9b683970bfbe81a868b62ce3ea36c1bb6/docs/report/submission-package-manifest.json
Pull Request:
https://github.com/NeryBR/cyberseat-booking-system/pull/13
Commit:
https://github.com/NeryBR/cyberseat-booking-system/commit/f473efa9b683970bfbe81a868b62ce3ea36c1bb6

Technical verification: the PDF was reopened and text was extracted from all 121 pages; every page was rendered with Poppler and inspected on eight contact sheets. A text-coordinate check found no characters outside the expected page bounds.

PDF SHA-256:
8498ccedb377999dc19c53ba91641f045663edc976c37b593bbe2c3f794fdcac

8498ccedb377999dc19c53ba91641f045663edc976c37b593bbe2c3f794fdcac

On October 24, Nurali reported that Aibekuly Alibi and Mansur Urynbassar had both reviewed this entire exact 121-page PDF and found no issues. This is an attributed user-reported PDF review, not a submitted GitHub approval. The PDF has not changed since the confirmation; the external verification record updates the compilation-time pending-review statements inside the PDF.


Remaining limitation: no genuine supervisor request/response or properly documented unanswered-request and escalation evidence is available. A feedback-status section identifying this gap is not supervisor feedback. ~~ECR-24~~ remains Queue until its evidence requirements are fully satisfied. PR #13 is open for review; no merge, formal GitHub approval, final software implementation, or executed application tests are claimed.

AN **Akhmetov Nurali** ● Прокомментировал(а) 10 минут назад

Final completion evidence - October 24, 2026

The consolidated report has been rebuilt with genuine supervisor feedback and is available in master. The screenshot is not embedded. The report records Myrzakerimova Alua's verbatim reply, an English translation, WhatsApp channel, October 24 date confirmed by Nurali, and displayed reply time 17:55. The supervisor reported no shortcomings or comments.

Result:
https://github.com/NeryBR/cyberseat-booking-system/blob/master/docs/report/Team_3_Approbation_Report_24_October.pdf
Verification and review record:
https://github.com/NeryBR/cyberseat-booking-system/blob/master/docs/report/consolidated-report-verification.md
Source manifest:
https://github.com/NeryBR/cyberseat-booking-system/blob/master/docs/report/submission-package-manifest.json
Pull Request:
https://github.com/NeryBR/cyberseat-booking-system/pull/14

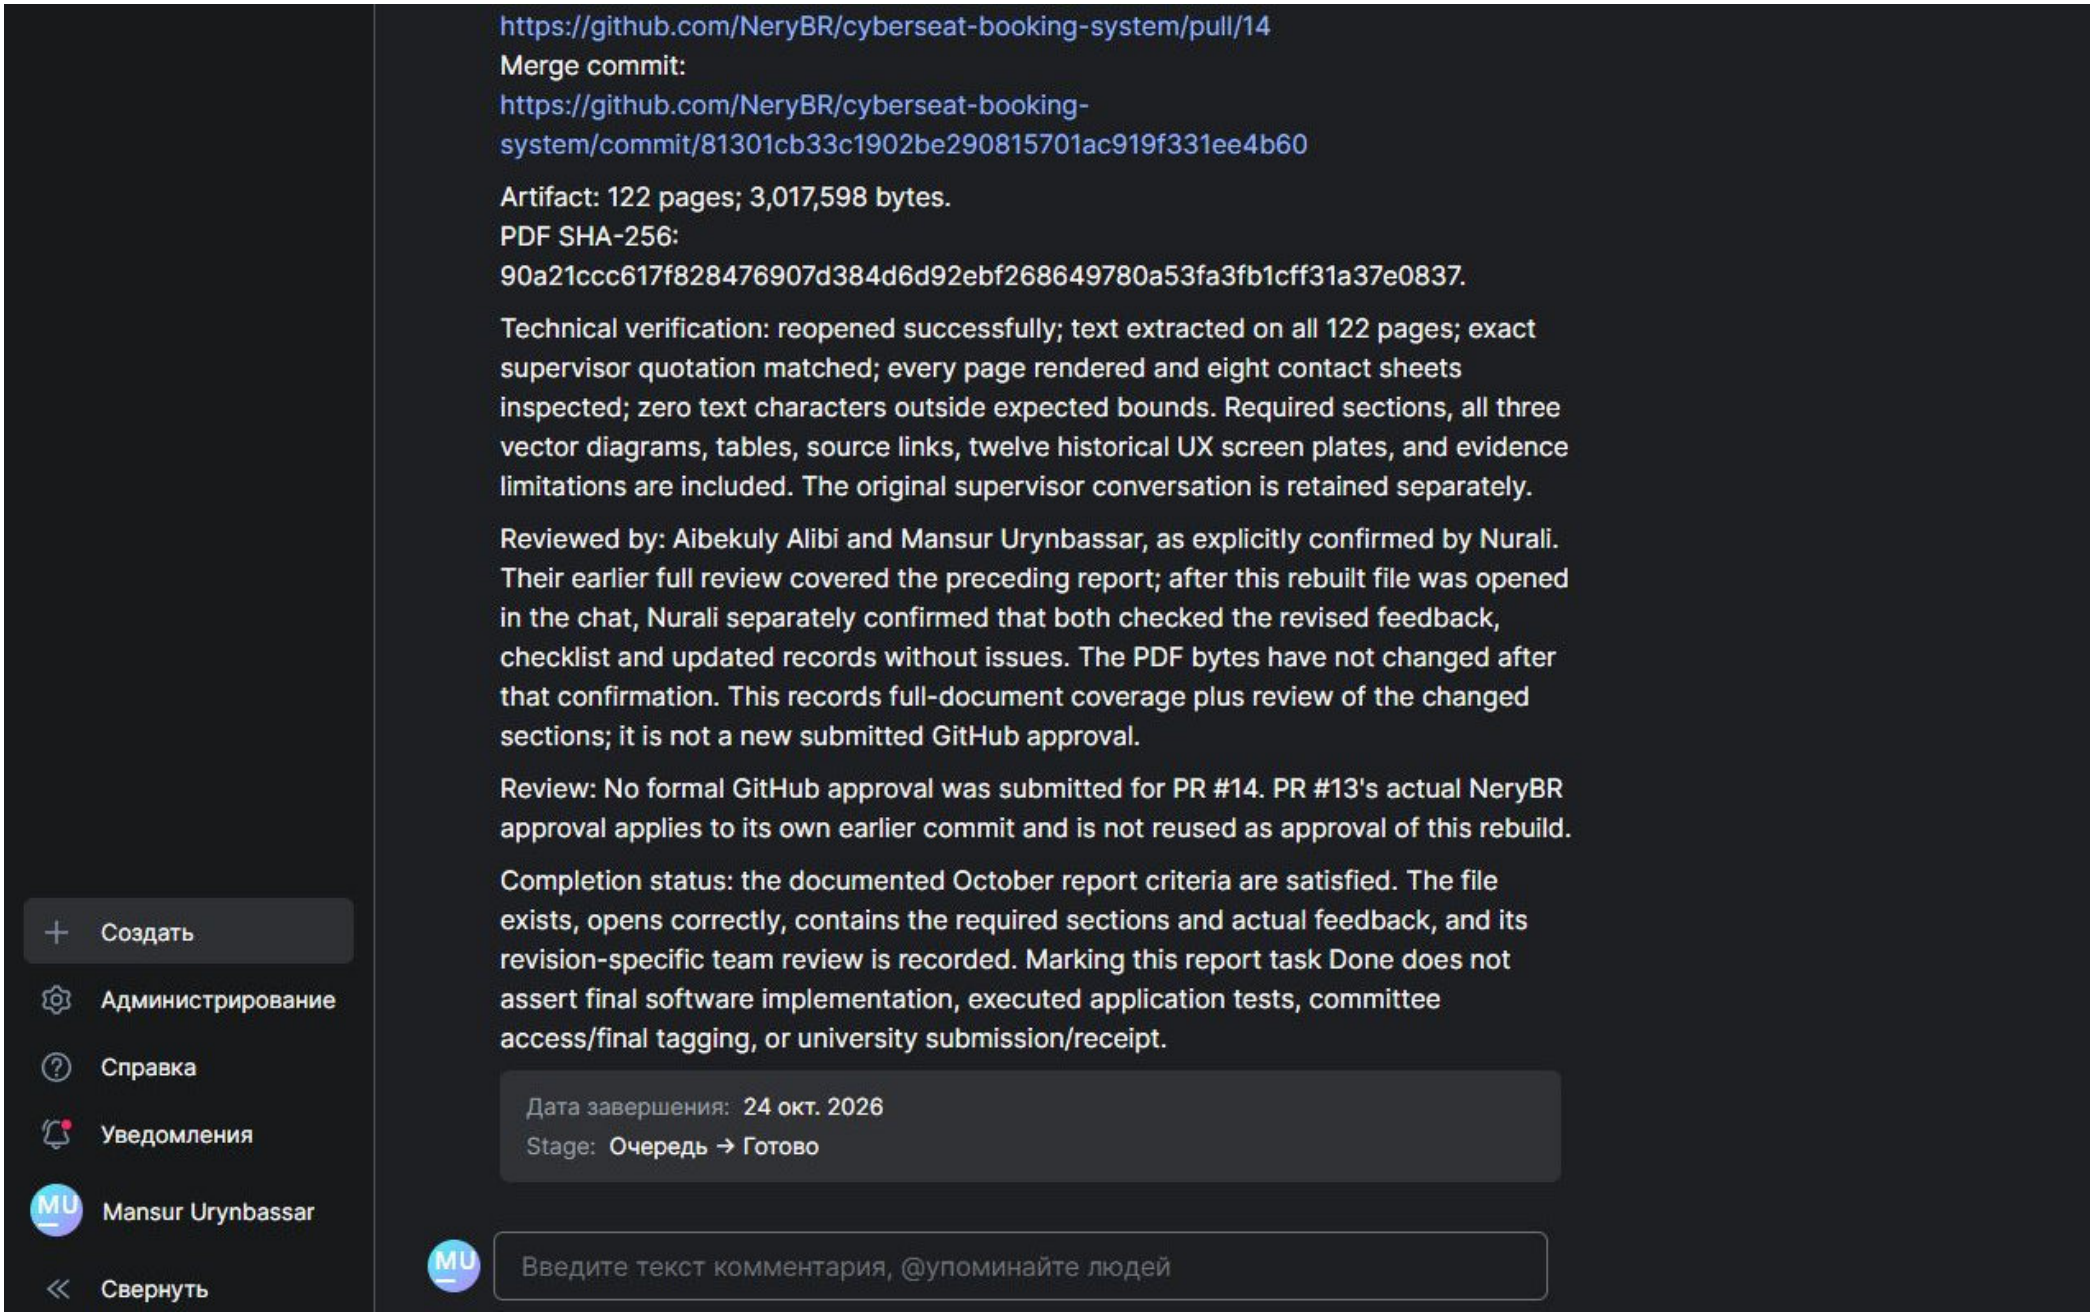
https://github.com/NeryBR/cyberseat-booking-system/pull/14
Merge commit:
https://github.com/NeryBR/cyberseat-booking-system/commit/81301cb33c1902be290815701ac919f331ee4b60
Artifact: 122 pages; 3,017,598 bytes.
PDF SHA-256:
90a21ccc617f828476907d384d6d92ebf268649780a53fa3fb1cff31a37e0837.
Technical verification: reopened successfully; text extracted on all 122 pages; exact supervisor quotation matched; every page rendered and eight contact sheets inspected; zero text characters outside expected bounds. Required sections, all three vector diagrams, tables, source links, twelve historical UX screen plates, and evidence limitations are included. The original supervisor conversation is retained separately.
Reviewed by: Aibekuly Alibi and Mansur Urynbassar, as explicitly confirmed by Nurali. Their earlier full review covered the preceding report; after this rebuilt file was opened in the chat, Nurali separately confirmed that both checked the revised feedback, checklist and updated records without issues. The PDF bytes have not changed after that confirmation. This records full-document coverage plus review of the changed sections; it is not a new submitted GitHub approval.
Review: No formal GitHub approval was submitted for PR #14. PR #13's actual NeryBR approval applies to its own earlier commit and is not reused as approval of this rebuild.
Completion status: the documented October report criteria are satisfied. The file exists, opens correctly, contains the required sections and actual feedback, and its revision-specific team review is recorded. Marking this report task Done does not assert final software implementation, executed application tests, committee access/final tagging, or university submission/receipt.
Дата завершения: 24 окт. 2026
Stage: Очередь → Готово
Создать
Администрирование
Справка
Уведомления
MU
Mansur Urynbassar
Свернуть
MU
Введите текст комментария, @упоминайте людей

ECR-24 - criteria, result links and review evidence

Original YouTrack screenshot | Part 6/6 | https://nerybr.youtrack.cloud/issue/ECR-24

